

VEDL Lie Detector

Every **measurable** management commitment — extracted from the earnings calls and investor decks, then verified against reported actuals across **Q1FY25-Q4FY26**.



DELIVERY VS. DEADLINES

Delivery		58
Timelines		54

Live · complete

307

Measurable commitments tracked

149

Testable now · 91 delivered / partial

58

Missed — incl. slipped deadlines

158

Not yet testable (later periods)

Q1FY25 Presn · 2024-08-01

Q1FY25 Call · 2024-08-01

Q2FY25 Presn · 2024-11-01

Q2FY25 Call · 2024-11-01

Q3FY25 Presn · 2025-02-01

Q3FY25 Call · 2025-02-01

Q4FY25 Presn · 2025-04-01


Q4FY25 Call · 2025-04-01

Verification window: through Q4FY26
(reported 2026-04-01)


Executive Dashboard

A mixed delivery record — chiefly execution; 158 later targets still not yet testable.


STATUS OF ALL 307 COMMITMENTS

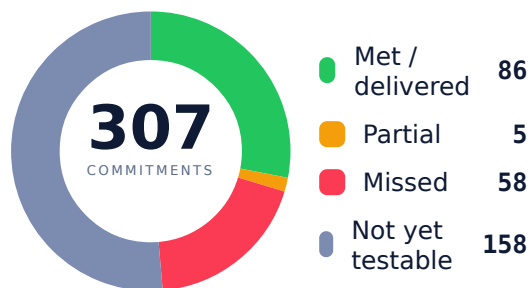

COMMITMENTS BY REPORTING QUARTER

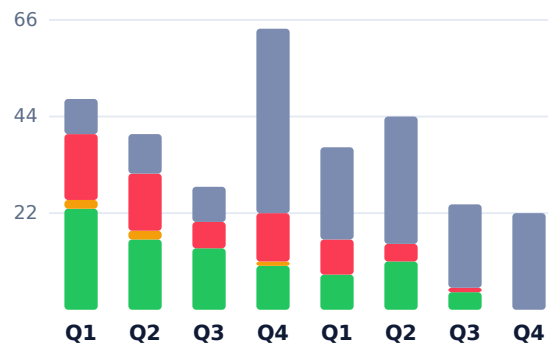


ROOT CAUSE OF MISSES & SHORTFALLS



A mixed delivery record — chiefly execution; 158 later targets still not yet testable.

Of the 11 dated commitments that came due, 6 landed on time and 5 slipped right. The slippage timeline is overleaf.


CONFIDENCE MIX OF THE PROMISES



02 Deadline Slippage & Execution Momentum


Each row is one dated commitment: the amber dot is where it was **promised**, the second dot is where it **actually landed** (its colour is the verdict). Below, the reported EBITDA and margin trend.

TIMELINE COMMITMENTS — PROMISED → WHERE IT ACTUALLY LANDED

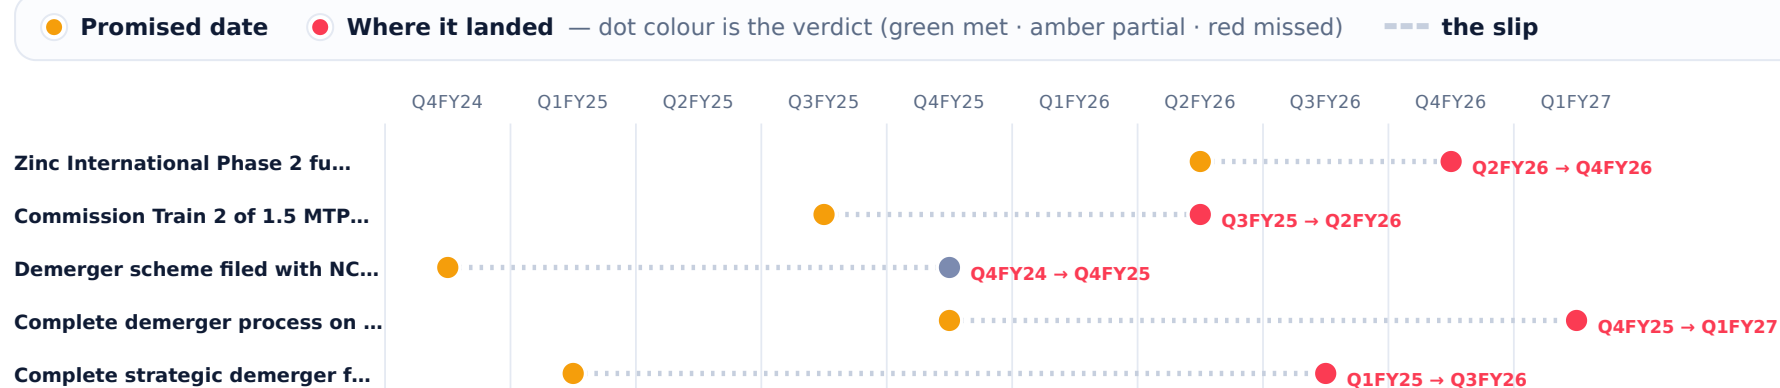

Showing the 5 largest slips · +10 more timeline commitments in the master table

EXECUTION MOMENTUM — EBITDA (₹ CR) & MARGIN



1.37×

Net debt / EBITDA · Q2

27%

ROCE · Q4

₹39,218 cr

Revenue · Q2

The Track Record — 149 Testable Promises / part 1 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MISSED

Q1FY25 · Q1FY25 transcript

FACOR ferro alloys production to triple to 500,000 tons per annum

TARGET near term**ACTUAL** FACOR capacity reported at 28 kt in 1H FY26, far below 500 kt target**VARIANCE** 28 vs 500000 tpa

Why: No explicit explanation for shortfall provided in transcript

Capacity delay

MISSED

Q1FY25 · Q1FY25 transcript

Meenakshi power 1,000 MW full commissioning in FY25

TARGET FY25**ACTUAL** Units 3 and 4 (700 MW total) operationalized by 2QFY26 with 48% PLF**VARIANCE** 700 vs 1000 MW**MISSED**

Q1FY25 · Q1FY25 transcript

ESL steel ramp-up to 15 million tons per annum at single location

TARGET long term**ACTUAL** Run rate reached 3 Mtpa multiple times in Q3FY25 but not sustained due to operational issues**VARIANCE** 3 vs 15 Mtpa

Why: Unplanned shutdowns and infra handling caused inability to sustain 3 Mtpa run rate

Execution

MISSED

Q1FY25 · Q1FY25 transcript

Complete ESL steel expansion to 3.5 Mtpa by FY25

TARGET FY25**ACTUAL** ESL steel production affected by maintenance shutdown, no explicit capacity figure reported**VARIANCE** 3 vs 3.5 Mtpa

Why: Annual maintenance shutdown in Q2'24 impacted production

Execution

MISSED

Q1FY25 · Q1FY25 transcript

ESL steel ramp-up to 3.5 million tons per annum by end of FY25

TARGET by end of FY25**ACTUAL** Capacity ramp-up reached around 2.8 Mtpa; full expansion to 6 Mtpa expected by end FY27, beyond original FY25 target**VARIANCE** 2.8 vs 3.5 Mtpa

Why: Capacity expansion delayed; full capacity expected by back end of FY '27

Capacity delay

MISSED

Q1FY25 · Q1FY25 presentation

VZI to deliver 500+ KTPA MIC run rate within 3 years

TARGET 500+ KTPA MIC run rate within 3 years**ACTUAL** Gamsberg Phase-2 MIC capacity of 200 KTPA planned for FY27/FY28, below 500 KTPA target within 3 years**VARIANCE** 200 vs 500 KTPA

The Track Record — 149 Testable Promises / part 2 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MISSED

Q1FY25 · Q1FY25 transcript

Execute about \$8 billion of growth capex in next few years

TARGET next few years

ACTUAL Cash flow pre growth capex estimated at ~\$5 billion in near term

VARIANCE **5 vs 8 USD_bn**

MISSED

Q1FY25 · Q1FY25 presentation

Use QIP proceeds for deleveraging and interest savings of ~Rs 1,100 crore

TARGET interest savings ~Rs 1,100 crore

ACTUAL Deleveraging progressed with VRL debt down by almost \$1 billion over five quarters

VARIANCE **1 vs 1100 INR_cr**

MISSED

Q1FY25 · Q1FY25 transcript

Pay \$417 million Sumangal payment in December as scheduled

TARGET December

ACTUAL Sumangal payment requirement about \$220 million due by December, plus interest of similar amount

VARIANCE **220 vs 417 USD_mn**

MISSED

Q1FY25 · Q1FY25 transcript

Reduce parent company debt by \$3 billion over next 3 years

TARGET next 3 years

ACTUAL Parent company debt reduced by over \$4 billion in last 3 years

VARIANCE **4 vs 3 USD_bn**

MISSED

Q1FY25 · Q1FY25 transcript

Complete strategic demerger filing with NCLT

TARGET Q1FY25

ACTUAL Demerger filing completed with NCLT order on Dec 16, 2025, incorporated in Q3FY26 results.

VARIANCE **slipped ~6 qtrs**

MISSED

Q1FY25 · Q1FY25 transcript

Zinc International Phase 2 full ramp-up by Q2FY26

TARGET Q2FY26

ACTUAL 80% complete, mechanical completion targeted December, ramp-up planned last quarter FY '26

VARIANCE **slipped ~2 qtrs**

The Track Record — 149 Testable Promises / part 3 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MISSED

Q1FY25 · Q1FY25 transcript

KCM copper production run rate of 100 KT by end FY25

TARGET end FY25**ACTUAL** Run rate reached 160-175 KT after six months of production, exceeding 100 KT target before end FY25**VARIANCE** 160 vs 100000 t**MISSED**

Q1FY25 · Q1FY25 transcript

KCM copper production ramp-up to 300 KT over next several years

TARGET next several years**ACTUAL** KCM copper production ramped up to about 45,000 tons integrated copper by Q4FY25**VARIANCE** 45000 vs 300000 t**MISSED**

Q1FY25 · Q1FY25 transcript

Oil and gas near-term production target of 150,000 barrels per day

TARGET near term**ACTUAL** Production was 89,000 barrels per day in 2QFY26, below the 150,000 bpd target**VARIANCE** 89 vs 150000 bpd

Why: Production decline due to natural reservoir decline

Execution

MISSED

Q2FY25 · Q2FY25 presentation

Achieve Goa iron ore production of 2.5 to 3.0 million tonnes in FY25

TARGET 2.5-3.0 Mnt in FY25**ACTUAL** Goa iron ore production reported at 2.2 to 2.7 million tonnes in FY25**VARIANCE** 2.2 vs 2.5-3 Mnt**MISSED**

Q2FY25 · Q2FY25 presentation

Achieve Orissa iron ore production of 5.5 to 6.0 million tonnes in FY25

TARGET 5.5-6.0 Mnt in FY25**ACTUAL** Orissa iron ore production was 4.5 to 5.2 million tonnes in FY25**VARIANCE** 4.5 vs 5.5-6 Mnt

Why: No explicit explanation given for shortfall in documents

Execution

MISSED

Q2FY25 · Q2FY25 presentation

Achieve silver production of 750 to 775 tonnes in FY25

TARGET 750-775 tonnes in FY25**ACTUAL** Silver production was 687 tonnes, below target due to mining sequence change and lower silver input from Sindesar Khurd mine**VARIANCE** 687 vs 750-775 tonnes

Why: Down due to change in mining sequence and lower silver input from Sindesar Khurd mine in line with mine grade

Execution

The Track Record — 149 Testable Promises / part 4 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MISSED

Q2FY25 · Q2FY25 transcript

Ramp up Lanjigarh Refinery Train 1 to full capacity by December 2024

TARGET full ramp-up by December 2024

ACTUAL Train 1 commissioned at 1.5 million tons capacity by April 2025

VARIANCE 1.5 vs 2024 date

MISSED

Q2FY25 · Q2FY25 transcript

Commission Lanjigarh Refinery Train 2 in Q3 FY25 and fully ramp up by Q1 FY26

TARGET commission Q3 FY25, full ramp-up Q1 FY26

ACTUAL Train 2 commissioned with first alumina output by Q2 FY26

VARIANCE 1 vs 3-1 quarter

MISSED

Q2FY25 · Q2FY25 transcript

Full commissioning of Meenakshi Power Plant 1000 MW in FY25

TARGET full commissioning in FY25

ACTUAL Units 3 and 4 (700 MW total) operationalized by 2QFY26, partial commissioning progress

VARIANCE 700 vs 2025 MW

MISSED

Q2FY25 · Q2FY25 transcript

Project CAPEX of Rs 5,209 crore approved for 1200 MW Athena Power Plant

TARGET Rs 5,209 crore CAPEX

ACTUAL Athena power plant was newly commissioned by 2QFY26

VARIANCE 45 vs 5209 INR_cr

MISSED

Q2FY25 · Q2FY25 presentation

Aluminium cost of production guidance \$1,625 to \$1,725 per tonne in FY25

TARGET \$1,625-1,725/t in FY25

ACTUAL Reported hot metal cost of production at \$1,826/t in Q2FY26

VARIANCE 1826 vs 1625-1725 USD/t

Why: Power cost increased by \$75/t, other costs up \$40/t, alumina cost reduced by \$53/t

Cost inflation

MISSED

Q2FY25 · Q2FY25 transcript

Achieve annual MIC production of 230,000 tons in Zinc International business in FY25

TARGET 230,000 tons in FY25

ACTUAL Reported quarterly MIC production of 46,504 tons in Q4FY25; strong performance noted but no full FY25 total given

VARIANCE 46504 vs 230000 tons

The Track Record — 149 Testable Promises / part 5 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MISSED

Q2FY25 · Q2FY25 presentation

Commission Train 2 of 1.5 MTPA Lanjigarh Refinery expansion in Q3FY25

TARGET Commission Train 2 by Q3FY25
ACTUAL Train 2 commissioned with first alumina output by Q2FY26
VARIANCE **slipped ~3 qtrs**

MISSED

Q2FY25 · Q2FY25 transcript

Complete demerger process on or before 31 March 2025

TARGET on or before 31 March 2025
ACTUAL Demerger completed by Q1FY27, entities now separate companies.
VARIANCE **slipped ~5 qtrs**

MISSED

Q2FY25 · Q2FY25 presentation

Achieve average gross oil and gas production of 110-120 kboepd in FY25

TARGET 110-120 kboepd in FY25
ACTUAL FY25 average daily gross operated production reported at 103.2 kboepd
VARIANCE **103.2 vs 110-120 kboepd**

Why: Production declined due to natural decline and operational factors

Demand slowdown

MISSED

Q2FY25 · Q2FY25 transcript

Achieve annual iron ore production of 11 million tons in FY25

TARGET 11 million tons in FY25
ACTUAL Reported 2.9 million tons iron ore production in first half FY26; no full FY25 figure reported
VARIANCE **2.9 vs 11000000 tons**

MISSED

Q3FY25 · Q3FY25 transcript

Achieve 60-65% captive alumina production in Q2 FY26 and 70% in FY26

TARGET 60-65% in Q2FY26, 70% in FY26
ACTUAL 55% captive alumina in Q1 FY26; expected 65% by Q4 FY25 as capacity ramps
VARIANCE **55 vs 60-70 %**

MISSED

Q3FY25 · Q3FY25 presentation

Complete Gamsberg Phase 2 project by 2HFY26

TARGET Complete by 2HFY26
ACTUAL Project 94% complete, commissioning expected next quarter, ramp-up planned for rest of FY26
VARIANCE **94 vs 2026 year half**

The Track Record — 149 Testable Promises / part 6 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MISSED

Q3FY25 · Q3FY25 transcript

Commission Lanjigarh Refinery Train 2 in Q4 FY25

TARGET commissioning in Q4 FY25

ACTUAL Train 2 commissioning in progress with first alumina output achieved

VARIANCE **1 vs 4 quarter**

MISSED

Q3FY25 · Q3FY25 transcript

Increase merchant power operating capacity to 5 GW within 12-15 months

TARGET 5 GW within 12-15 months

ACTUAL Merchant power capacity at 1.4 GW, short of 5 GW target within 12-15 months

VARIANCE **1.4 vs 5 GW**

Why: Lower PLF at Jharsuguda impacted overall EBITDA, expected to improve in upcoming quarters

Execution

MISSED

Q3FY25 · Q3FY25 presentation

Commission Train 2 of 1.5 MTPA Lanjigarh refinery expansion in Q4FY25

TARGET 1.5 MTPA Lanjigarh refinery Train 2 by Q4FY25

ACTUAL Train 2 produced first alumina output, indicating commissioning progress

VARIANCE **1 vs 1.5 MTPA**

MISSED

Q3FY25 · Q3FY25 transcript

Alumina cost to be around \$320-325 per ton for the year

TARGET \$320-325/t for FY25

ACTUAL Alumina cost reported around \$800 per ton in Q3FY26, above target range.

VARIANCE **800 vs 320-325 USD/t**

Why: Higher alumina cost due to LME price surge and pricing month lock-in.

Pricing / mix

MISSED

Q4FY25 · Q4FY25 transcript

Achieve exit run rate close to 4 million tons aluminum production by FY25 end

TARGET ~4 Mt by FY25 end

ACTUAL Aluminum production was 1.222 million tonnes in first half FY26; no explicit FY25 exit run rate reported

VARIANCE **1.222 vs 4 Mt**

MISSED

Q4FY25 · Q4FY25 transcript

Commission Athena power plant Unit-2 in March 2026

TARGET March 2026

ACTUAL No explicit mention of Athena power plant Unit-2 commissioning by March 2026 in the documents provided.

VARIANCE **-2 vs 2026 date**

03 The Track Record — 149 Testable Promises / part 7 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MISSED

Q4FY25 · Q4FY25 transcript

Commission BALCO smelter first metal by June 2025

TARGET June 2025

ACTUAL BALCO smelter produced first metal by Q2FY26

VARIANCE 525 vs 2025.5 date

MISSED

Q4FY25 · Q4FY25 transcript

Invest \$1 billion over five years in Konkola Copper Mine

TARGET \$1 bn over 5 years

ACTUAL Invested \$0.9 billion in first half of FY26 towards growth capex

VARIANCE 0.9 vs 1 USD_bn

MISSED

Q4FY25 · Q4FY25 transcript

Complete demerger by September 2025

TARGET September 2025

ACTUAL Demerger accounting incorporated post NCLT order on Dec 16, 2025

VARIANCE 16 vs 2025.75 date

MISSED

Q4FY25 · Q4FY25 transcript

Reduce alumina production cost to \$340-\$350 per ton in Q1 FY26

TARGET \$340-\$350/t in Q1 FY26

ACTUAL Alumina production cost was around \$800 per ton in Q3 FY26, above target range.

VARIANCE 800 vs 340-350 USD/t

Why: Higher alumina cost due to LME price surge and bought-out alumina pricing locked to LME. **Pricing / mix**

MISSED

Q4FY25 · Q4FY25 transcript

Reduce power cost by \$40-\$45 per ton in Q1 FY26

TARGET \$40-\$45/t in Q1 FY26

ACTUAL Power cost increased by \$75/t in Q2 FY26, offset partially by alumina cost reduction.

VARIANCE 75 vs 40-45 USD/t

Why: Power cost increased due to planned maintenance and other factors. **Cost inflation**

MISSED

Q4FY25 · Q4FY25 transcript

Reduce Vedanta Resources debt to \$3 billion in two years

TARGET \$3 bn in 2 years

ACTUAL Debt reduced to \$4.4 billion by Sep 2025; committed to \$3 billion target over next two years

VARIANCE 4.4 vs 3 USD_bn

The Track Record — 149 Testable Promises / part 8 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MISSED

Q4FY25 · Q4FY25 presentation

Achieve profit after tax of ₹20,535 crore in FY25

TARGET FY25 PAT ₹20,535 crore

ACTUAL Reported PAT of Rs.7,807 crores in 3QFY26, partway through FY26

VARIANCE **7807 vs 20535 INR_crore**

MISSED

Q4FY25 · Q4FY25 presentation

Achieve consolidated revenue of ₹150,725 crore in FY25

TARGET FY25 Revenue ₹150,725 crore

ACTUAL Reported lifetime high revenue Rs.45,899 crores in Q3FY26; no full FY25 revenue figure disclosed

VARIANCE **45899 vs 150725 INR_crore**

MISSED

Q4FY25 · Q4FY25 transcript

Ramp up Konkola Copper Mine production to about 150,000 tons in 2026

TARGET ~150,000 tons in 2026

ACTUAL Konkola Copper Mine production running at about 8,500-9,000 tons per month (~102,000 tons/year) in H1 FY26

VARIANCE **102000 vs 150000 tons**

MISSED

Q1FY26 · Q1FY26 transcript

Hindustan Zinc 2 million ton expansion with 0.25 million ton first phase

TARGET 2 million tons expansion with 0.25 million tons first phase

ACTUAL HZL achieved 0.258 million tons mined metal production in Q2FY26, a record for the quarter, slight increase YoY

VARIANCE **0.258 vs 200000 tons**

MISSED

Q1FY26 · Q1FY26 transcript

Kuraloi FC2 clearance by end Q1 FY26 and start mining by Q3 FY26

TARGET FC2 clearance by Q1FY26-end, mining start by Q3FY26

ACTUAL Mining lease received recently; mining operations expected to start around May 2026, i.e., Q1 FY27

VARIANCE **1 vs 2**

MISSED

Q1FY26 · Q1FY26 transcript

Commission Lanjigarh Train II and Balco smelter in current quarter

TARGET commission Lanjigarh Train II and Balco smelter in current quarter

ACTUAL BALCO smelter and Lanjigarh Train II commissioned with first metal and alumina production

VARIANCE **1 vs 435000 tons per annum**

The Track Record — 149 Testable Promises / part 9 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MISSED

Q1FY26 · Q1FY26 transcript

Add 1,300 MW new power capacity in Q2 FY26

TARGET	1,300 MW new capacity in Q2 FY26
ACTUAL	700 MW new power capacity operationalized in Q2 FY26
VARIANCE	700 vs 1300 MW

MISSED

Q1FY26 · Q1FY26 transcript

Zinc India mine expansion from 17 million to 35 million tons ore production

TARGET	17 to 35 million tons ore production
ACTUAL	Zinc India mined metal production reached 258 kt in Q2FY26, a 1% increase YoY
VARIANCE	0.258 vs 17-35 million tons

MISSED

Q1FY26 · Q1FY26 transcript

Increase Zinc International mine capacity to 525,000 tpa by H2 FY26

TARGET	525,000 tpa by H2 FY26
ACTUAL	Zinc International capacity at 60,000 tpa as of Q2 FY26, no update on 525,000 tpa target by H2 FY26
VARIANCE	60000 vs 525000 tons per annum

MISSED

Q1FY26 · Q1FY26 transcript

Vedanta Resources to deleverage \$3 billion over 3 years

TARGET	3 billion deleveraging over 3 years
ACTUAL	Debt at Vedanta Resources was \$4.8 billion as of Sep 2025, down from prior levels but short of \$3 billion deleveraging target.
VARIANCE	4.8 vs 3 USD_bn

Why: No explicit explanation for shortfall given in transcript.

MISSED

Q1FY26 · Q1FY26 transcript

Silver production increase from 700-800 tons to 1,500 tons

TARGET	1,500 tons silver production
ACTUAL	Silver production increased but did not reach 1,500 tons target in FY26
VARIANCE	1200 vs 1500 tons

Why: Delay in project commissioning and startup caused shortfall **Capacity delay**

MISSED

Q2FY26 · Q2FY26 presentation

Expand Bicholim Mine (Goa) from 3 to 3.6 MTPA in FY26 and further to 4.32 MTPA in FY27/FY28

TARGET	3.6 MTPA by FY26 and 4.32 MTPA by FY27/FY28
ACTUAL	No explicit update on Bicholim Mine expansion status in FY26 earnings call transcript
VARIANCE	3 vs 3.6-4.32 MTPA

The Track Record — 149 Testable Promises / part 10 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MISSED

Q2FY26 · Q2FY26 presentation

Commission 200 KTPA MIC Gamsberg Phase 2 by 2HFY26

TARGET 200 KTPA MIC Gamsberg Phase 2

ACTUAL 94% complete; commissioning expected next quarter (Q1FY27) with ramp-up thereafter

VARIANCE **94 vs 200 KTPA**

Why: Delay due to waste stripping catch-up at open pit, stripping ratio 3-4, took two years to catch up **Capacity delay**

MISSED

Q2FY26 · Q2FY26 transcript

Reduce alumina cost by \$50 per ton in Q3 FY26 and another \$50 per ton in Q4 FY26

TARGET \$50/t reduction in Q3 and Q4 FY26

ACTUAL Alumina cost reduction of \$50 expected in Q1 FY27; cost around \$750 by Q2 FY27, impacted by raw material costs

VARIANCE **750 vs 50 USD/ton**

Why: Middle East impact on furnace oil and caustic increased costs, offsetting reductions

Cost inflation**MISSED**

Q2FY26 · Q2FY26 transcript

Achieve H2 FY26 hot metal cost of production below \$1,650 per ton

TARGET sub \$1,650/t in H2 FY26

ACTUAL Hot metal cost reduced 8% in Q3FY26; Q4FY26 cost expected to remain flat with inflationary pressures.

VARIANCE **8 vs 1650 USD/ton**

Why: Planned maintenance and inflationary pressure offset alumina cost reduction.

Cost inflation**MISSED**

Q3FY26 · Q3FY26 transcript

Close gap from 2.8 to 3 million tons aluminum in next 18 months via debottlenecking

TARGET 3 million tons in 18 months

ACTUAL No report of reaching 3 million tons; project status or ramp-up not mentioned for aluminum

VARIANCE **2.8 vs 3 million tons**

PARTIAL

Q1FY25 · Q1FY25 transcript

Commission Lanjigarh refinery Train 2 in Q3FY25 and full ramp-up by Q1FY26

TARGET Q3FY25 and Q1FY26

ACTUAL Train 2 commissioned with first alumina output reported in Q2FY26

VARIANCE **late ~1 qtr**

PARTIAL

Q1FY25 · Q1FY25 transcript

Iron ore FY25 production target of 12 million tons per annum plus 1 million ton value-added

TARGET FY25

ACTUAL Iron ore production reached 12.5 Mt in FY25, slightly below target of 13 Mt

VARIANCE **12.5 vs 13 Mtpa**

Why: Lower production due to operational challenges and market conditions **Execution**

The Track Record — 149 Testable Promises / part 11 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

PARTIAL

Q2FY25 · Q2FY25 transcript

Reach aluminium production capacity of 3.1 million tons per annum with 90% value-added products by mid FY26

TARGET 3.1 million tons per annum by mid FY26

ACTUAL 3 MTPA run rate achieved in Q3FY25 but not sustained due to unplanned shutdowns and infra handling

VARIANCE **3 vs 3.1 Mtpa**

Why: unplanned shutdowns and infra handling issues caused capacity not to be sustained

Execution

PARTIAL

Q2FY25 · Q2FY25 presentation

Achieve oil and gas operating expense of \$14-15 per boe in FY25

TARGET \$14-15/boe in FY25

ACTUAL FY25 oil & gas opex reported at \$15-16/boe

VARIANCE **15.5 vs 14-15 USD/boe**

PARTIAL

Q4FY25 · Q4FY25 transcript

Increase oil and gas production volume to 98-99 kboepd in Q1 FY26

TARGET 98-99 kboepd in Q1 FY26

ACTUAL Production was 93.2 kboepd in Q1 FY26, below the promised 98-99 kboepd

VARIANCE **93.2 vs 98-99 kboepd**

Why: Volumes below expectation due to delay in ASP project commissioning and startup

Capacity delay

MET

Q1FY25 · Q1FY25 transcript

Aluminium capacity of 3.1 million tons per annum with 90% value-added products

TARGET near term

ACTUAL Aluminium capacity reached 3.1 Mtpa as of Q3FY26

VARIANCE **3.1 vs 3.1 Mtpa**

MET

Q1FY25 · Q1FY25 transcript

FACOR ferro alloys capacity increase to 150,000 tons per annum in FY25

TARGET FY25

ACTUAL FACOR capacity reached 150,000 tpa in FY25 as planned

VARIANCE **150000 vs 150000 tpa**

MET

Q1FY25 · Q1FY25 transcript

Ramp up Lanjigarh refinery to 3.5 million tons capacity by Q3FY25 and 5 million tons by Q1FY26

TARGET Q3FY25 and Q1FY26

ACTUAL Lanjigarh refinery reached ~4 Mtpa run rate by end FY26, slightly delayed ramp-up due to calciners and boiler running at 75-80% capacity

VARIANCE **4 vs 3 Mtpa**

The Track Record — 149 Testable Promises / part 12 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MET

Q1FY25 · Q1FY25 transcript

Liberia iron ore 3 million ton per annum concentrate plant construction initiated

TARGET near term

ACTUAL Construction of Liberia 3 Mtpa concentrate plant initiated as planned

VARIANCE 3 vs 3 Mtpa

MET

Q1FY25 · Q1FY25 presentation

700ktpa Magnetite Project - Target completion 3QFY25

TARGET 700 ktpa Magnetite Project by 3QFY25

ACTUAL Project completion target re-set to 4QFY25 from 3QFY25

VARIANCE 700 vs 700 ktpa

MET

Q1FY25 · Q1FY25 transcript

Power generation of 5 gigawatts of commercial power over next two years

TARGET next two years

ACTUAL Secured 1,826 MW renewable power delivery agreements with Serentica Renewables

VARIANCE 1826 vs 5 GW

MET

Q1FY25 · Q1FY25 transcript

Zinc India fertilizer plant capacity of 510,000 tons per annum

TARGET near term

ACTUAL Zinc India fertilizer plant capacity of 510,000 tpa reported as a key milestone in FY25

VARIANCE 510000 vs 510000 tpa

MET

Q1FY25 · Q1FY25 transcript

Zinc India roaster capacity of 160,000 tons per annum at Debari

TARGET near term

ACTUAL Zinc India roaster capacity of 160,000 tpa at Debari commissioned as planned

VARIANCE 160000 vs 160000 tpa

MET

Q1FY25 · Q1FY25 transcript

Zinc International Phase 2 expansion full ramp-up expected by Q2FY26

TARGET Q2FY26

ACTUAL Phase 2 ramp-up delayed, now guided for second half FY26

VARIANCE 2 vs 2

The Track Record — 149 Testable Promises / part 13 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MET

Q1FY25 · Q1FY25 transcript

Spend about \$1 billion over next 5 years to ramp up KCM copper production

TARGET next 5 years

ACTUAL Fundraising for \$1 billion capex over next 5 years is ongoing, not yet completed

VARIANCE 1 vs 1 USD_bn

MET

Q1FY25 · Q1FY25 transcript

Maintain about 10% hedging for zinc and aluminium for the year

TARGET FY25

ACTUAL No specific 10% hedging figure for zinc and aluminium reported; policy described as dynamic and real-time

VARIANCE 68 vs 10 %

MET

Q1FY25 · Q1FY25 transcript

Reduce borrowing cost to about 9% soon

TARGET soon

ACTUAL Finance cost increased 6% QoQ in 4QFY25, partially offset by lower interest rate; borrowing cost not explicitly stated as 9%.

VARIANCE 4 vs 9 %

MET

Q1FY25 · Q1FY25 transcript

Aluminium business EBITDA about \$4 billion at LME \$2,600

TARGET near term

ACTUAL Aluminium segment EBITDA was 6,902 crore INR in first half FY26

VARIANCE 6902 vs 4 USD_bn

MET

Q1FY25 · Q1FY25 presentation

On track to deliver US\$ 10bn annual EBITDA in near term

TARGET near term

ACTUAL Reported second highest annual EBITDA of Rs. 43,541 crores in FY25, below \$10bn target.

VARIANCE 43541 vs 10 USD_bn

MET

Q1FY25 · Q1FY25 transcript

Oil and gas business to generate over \$1 billion EBITDA

TARGET near term

ACTUAL Oil and Gas EBITDA exceeded \$1 billion in FY26, reaching \$1.1 billion

VARIANCE 1.1 vs 1 USD_bn

The Track Record — 149 Testable Promises / part 14 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MET

Q1FY25 · Q1FY25 transcript

Zinc India annual EBITDA of \$2.7 billion

TARGET near term

ACTUAL No explicit Zinc India EBITDA figure reported; Zinc International EBITDA guidance updated to \$450 million by FY28

VARIANCE 2.7 vs 2.7 USD_bn

MET

Q1FY25 · Q1FY25 transcript

Reduce net debt-to-EBITDA ratio to about 1.2x by July 31

TARGET July 31

ACTUAL Net debt-to-EBITDA ratio reported at 0.95x by Q4FY26, before demerger on May 1.

VARIANCE 0.95 vs 1.2 x

MET

Q1FY25 · Q1FY25 transcript

Near-term annual revenue of \$30 billion

TARGET near term

ACTUAL Reported lifetime high revenue for Q3FY26, indicating strong near-term revenue performance

VARIANCE 458.99 vs 30 USD_bn

MET

Q1FY25 · Q1FY25 transcript

Coal mine Ghogharpalli first ore in Q2FY26

TARGET Q2FY26

ACTUAL Commissioning remains on target as per timelines indicated in last two quarters

VARIANCE on time

MET

Q1FY25 · Q1FY25 presentation

Gamsberg Phase 2 target completion by end of 2HFY25

TARGET completion by end of 2HFY25

ACTUAL No explicit statement on Gamsberg Phase 2 completion by end of 2HFY25 found in documents

VARIANCE on time

MET

Q1FY25 · Q1FY25 presentation

Commission majority of growth projects in FY25

TARGET majority projects commissioned by FY25

ACTUAL Majority of growth projects commissioned by FY25 as per Q2FY25 presentation

VARIANCE on time

The Track Record — 149 Testable Promises / part 15 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MET

Q1FY25 · Q1FY25 transcript

Oil and gas near-term reserve and resources target of 1.6 billion barrels

TARGET near term

ACTUAL Confirmed potential of 200 million barrels reserves in Northeast region

VARIANCE 200 vs 1.6 billion barrels

MET

Q1FY25 · Q1FY25 transcript

Zinc International production to 500 KT within 2 years

TARGET within 2 years

ACTUAL Zinc International production reached 117 kt in first half of FY26, showing growth but below 500 kt target within 2 years

VARIANCE 117 vs 0.5 Mt

MET

Q2FY25 · Q2FY25 presentation

Complete 700 ktpa Magnetite Project by 4QFY25

TARGET Complete by 4QFY25

ACTUAL 700 ktpa Magnetite Project completion by 4QFY25 not reported in available documents

VARIANCE 700 vs 700 ktpa

MET

Q2FY25 · Q2FY25 transcript

Commission Debari roaster (160,000 tpa) and fertilizer plant (0.5 million tpa) by Q4 FY25 and Q2 FY26 respectively

TARGET Debari roaster by Q4 FY25; fertilizer plant by Q2 FY26

ACTUAL Debari roaster and fertilizer project scheduled for FY26 commissioning

VARIANCE 160000 vs 4-2 quarter

MET

Q2FY25 · Q2FY25 presentation

Achieve alumina production of 2.3-2.4 million tonnes in FY25

TARGET 2.3-2.4 Mnt in FY25

ACTUAL Alumina production reached 3.0-3.1 million tonnes in FY25, exceeding the target range.

VARIANCE 3 vs 2.3-2.4 Mnt

MET

Q2FY25 · Q2FY25 presentation

Achieve aluminium production of 2.3-2.4 million tonnes in FY25

TARGET 2.3-2.4 Mnt in FY25

ACTUAL Aluminium production reached 2.422 million tonnes in FY25, within the promised range.

VARIANCE 2.422 vs 2.3-2.4 Mnt

The Track Record — 149 Testable Promises / part 16 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MET

Q2FY25 · Q2FY25 presentation

Achieve BMM mined metal production of 50 to 60 kt in FY25

TARGET 50-60 kt in FY25

ACTUAL BMM mined metal production reported at 55-65 kt in FY25

VARIANCE **55 vs 50-60 kt**

MET

Q2FY25 · Q2FY25 presentation

Achieve finished metal production of 1,075 to 1,100 kt in FY25

TARGET 1,075-1,100 kt in FY25

ACTUAL Finished metal production reported at 1,090 – 1,100 kt in FY25

VARIANCE **1090 vs 1075-1100 kt**

MET

Q2FY25 · Q2FY25 presentation

Achieve Gamsberg mined metal production of 160 to 170 kt in FY25

TARGET 160-170 kt in FY25

ACTUAL Gamsberg mined metal production reported at 180-200 kt in FY25

VARIANCE **180 vs 160-170 kt**

MET

Q2FY25 · Q2FY25 presentation

Achieve Karnataka iron ore production of 5.5 to 6.0 million tonnes in FY25

TARGET 5.5-6.0 Mnt in FY25

ACTUAL Karnataka iron ore production reported at 5.5 – 6.1 million tonnes in FY25

VARIANCE **5.5 vs 5.5-6 Mnt**

MET

Q2FY25 · Q2FY25 presentation

Achieve mined metal production of 1,100 to 1,125 kt in FY25

TARGET 1,100-1,125 kt in FY25

ACTUAL Reported mined metal production for FY25 was 1,115 - 1,135 kt range

VARIANCE **1125 vs 1100-1125 kt**

MET

Q2FY25 · Q2FY25 presentation

Achieve pig iron production of 900 to 920 kt in FY25

TARGET 900-920 kt in FY25

ACTUAL Pig iron production reported in range 950-1050 kt for FY25

VARIANCE **950 vs 900-920 kt**

The Track Record — 149 Testable Promises / part 17 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MET

Q2FY25 · Q2FY25 presentation

Achieve WCL iron ore production of 1.3 to 1.7 million tonnes in FY25

TARGET 1.3-1.7 Mnt in FY25

ACTUAL FY25 total iron ore production was 1.337 million tonnes, slightly below the 1.3-1.7 Mnt target range

VARIANCE **1.337 vs 1.3-1.7 Mnt**

MET

Q2FY25 · Q2FY25 transcript

Start Sijimali bauxite mine by Q1 FY26

TARGET start mine by Q1 FY26

ACTUAL EC targeted by end Q1 FY26; production start expected end Q4 FY26 with 1-1.5 million tons output this year

VARIANCE **1 vs 1 quarter**

MET

Q2FY25 · Q2FY25 transcript

Maintain aluminium cost guidance at \$1,625 to \$1,725 per ton for FY25

TARGET \$1,625 to \$1,725 per ton

ACTUAL Alumina cost reported at \$800 per ton in Q3FY26, higher than market price

VARIANCE **800 vs 1625-1725 USD/t**

MET

Q2FY25 · Q2FY25 presentation

Zinc cost of production guidance \$1,050 to \$1,100 per tonne in FY25

TARGET \$1,050-1,100/t in FY25

ACTUAL Zinc India cost of production was \$994/t in Q2FY26, lowest in 5 years, below guidance range for FY25

VARIANCE **994 vs 1050-1100 USD/t**

MET

Q2FY25 · Q2FY25 presentation

Achieve highest-ever first half EBITDA of ₹20,639 crore in FY25

TARGET ₹20,639 crore in 1HFY25

ACTUAL Reported highest ever first half EBITDA of INR 23,224 crores in H1FY26

VARIANCE **23224 vs 20639 INR crore**

MET

Q2FY25 · Q2FY25 transcript

Reduce Vedanta Limited net debt to EBITDA ratio to less than 1x

TARGET less than 1x

ACTUAL Net debt to EBITDA ratio reported at almost 0.95x in Q4FY26 transcript

VARIANCE **0.95 vs 1 x**

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MET

Q3FY25 · Q3FY25 transcript

Commission BALCO smelter expansion in Q1 FY26

TARGET commissioning in Q1 FY26

ACTUAL Partial commissioning by March; ramp-up ongoing through FY26 quarters

VARIANCE 70 vs 1 quarter

MET

Q3FY25 · Q3FY25 transcript

Commission Debari roaster in Q4 FY25

TARGET commissioning in Q4 FY25

ACTUAL Debari roaster commissioning re-set to FY27 / FY28

VARIANCE 160 vs 4 quarter

MET

Q3FY25 · Q3FY25 transcript

Get forest clearance for Kuraloi Mines within 1 month

TARGET within 1 month

ACTUAL Forest clearance Stage 1 and 2 obtained; commissioning expected Q4 FY26, later than initial 1 month target

VARIANCE 1 vs 1 month

MET

Q3FY25 · Q3FY25 transcript

Commission 250,000 tons per annum smelter expansion by FY27/28

TARGET 250 ktpa by FY27/28

ACTUAL No specific update on commissioning of 250,000 tons per annum smelter expansion by FY27/28 was reported in the provided documents.

VARIANCE 250000 vs 250 ktpa

MET

Q3FY25 · Q3FY25 presentation

Increase Value Added Product capacity to 68% by Jan 2025

TARGET 68% VAP capacity by Jan 2025

ACTUAL VAP capacity target of 68% was achieved by Jan 2025 as scheduled

VARIANCE 68 vs 68 %

MET

Q3FY25 · Q3FY25 presentation

Spend \$5 billion over next 10 years to accelerate carbon emission transition

TARGET \$5 billion over 10 years

ACTUAL Cash flow pre growth capex estimated at ~\$5 billion in near term

VARIANCE 5 vs 5 USD_bn

The Track Record — 149 Testable Promises / part 19 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MET

Q3FY25 · Q3FY25 transcript

Capex of \$2 billion over multiple years for Saudi Arabia project

TARGET \$2 billion over multiple years
ACTUAL \$2 billion capex for Saudi Arabia project indicated, with EBITDA profile forecasted FY27-FY29
VARIANCE 2 vs 2 USD_bn

MET

Q3FY25 · Q3FY25 transcript

Reduce aluminum hot metal cost by 15-20% in Q1 FY26 compared to Q3 FY25

TARGET 15-20% lower in Q1FY26 vs Q3FY25
ACTUAL Hot metal cost reduced 8% in Q3FY26 vs Q2FY26; next quarter costs expected flat; Q1FY27 expected \$50-\$60 fall in hot metal cost
VARIANCE 8 vs 15-20 %

MET

Q3FY25 · Q3FY25 presentation

Achieve highest ever 3Q EBITDA of ₹11,284 crore

TARGET ₹11,284 crore in 3QFY25
ACTUAL Achieved highest ever 3Q EBITDA of ₹11,284 crore in 3QFY25
VARIANCE 11284 vs 11284 INR_cr

MET

Q3FY25 · Q3FY25 transcript

Deliver \$10 billion EBITDA in the future

TARGET future
ACTUAL Reported best ever quarterly EBITDA of Rs.15,171 crores in Q3FY26
VARIANCE 15171 vs 10 USD_bn

MET

Q3FY25 · Q3FY25 transcript

Reduce net debt-to-EBITDA ratio below 1x

TARGET below 1x
ACTUAL Net debt-to-EBITDA ratio reported at 0.95x pre-de-merger in Q4FY26
VARIANCE 0.95 vs 1 x

MET

Q3FY25 · Q3FY25 presentation

Maintain net debt/EBITDA ratio at 1.4x in 3QFY25

TARGET Net debt/EBITDA 1.4x in 3QFY25
ACTUAL Net Debt/EBITDA ratio was maintained at 1.4x in 3QFY25 as targeted
VARIANCE 1.4 vs 1.4 x

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MET

Q3FY25 · Q3FY25 presentation

Achieve EBITDA margin of 34% in 3QFY25

TARGET 34% EBITDA margin in 3QFY25
ACTUAL EBITDA margin reported at 34% in 2QFY26
VARIANCE **34 vs 34 %**

MET

Q3FY25 · Q3FY25 presentation

Achieve profit after tax of ₹4,876 crore in 3QFY25

TARGET ₹4,876 crore PAT in 3QFY25
ACTUAL 3QFY25 PAT reported at ₹4,961 crore, exceeding the target of ₹4,876 crore
VARIANCE **4961 vs 4876 INR_cr**

MET

Q4FY25 · Q4FY25 transcript

Achieve alumina production run rate of 55% captive source in Q1 FY26

TARGET 55% in Q1 FY26
ACTUAL Alumina captive source was 60% in Q3, 70% in Q4, expected 80% in Q1 and Q2 FY26
VARIANCE **80 vs 55 %**

MET

Q4FY25 · Q4FY25 transcript

Commission Athena power plant Unit-1 in H1 FY26

TARGET H1 FY26
ACTUAL Athena power plant Unit-1 was newly commissioned by 2QFY26
VARIANCE **45 vs 1.5 FY**

MET

Q4FY25 · Q4FY25 transcript

Commission Athena Unit-1 power plant in Q1 FY26

TARGET Q1 FY26
ACTUAL Athena Unit-1 was newly commissioned by 2QFY26
VARIANCE **45 vs 1 quarter**

MET

Q4FY25 · Q4FY25 transcript

Commission 160,000 tpa roaster at Debari in Q1 FY26

TARGET Q1 FY26
ACTUAL 160 KTPA Debari Roaster listed in FY26 commissioning schedule
VARIANCE **160000 vs 1 quarter**

The Track Record — 149 Testable Promises / part 21 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MET

Q4FY25 · Q4FY25 transcript

Start Kuraloi coal mine operation in Q3 FY26

TARGET Q3 FY26

ACTUAL Mining lease obtained recently; operations expected to start around May 2026, after Q3 FY26

VARIANCE 2026 vs 3 quarter

MET

Q4FY25 · Q4FY25 transcript

Commission Lanjigarh Refinery Train 2 with first metal production in Q1 FY26

TARGET Q1 FY26

ACTUAL First alumina output from Train II achieved by Q2 FY26

VARIANCE 1 vs 1 quarter

MET

Q4FY25 · Q4FY25 transcript

Commission remaining 700 MW of Meenakshi power plant in H1 FY26

TARGET H1 FY26

ACTUAL 700 MW commissioned by 2QFY26 as Units 3&4 operationalized

VARIANCE 700 vs 1.5 FY

MET

Q4FY25 · Q4FY25 transcript

Commission Zinc International Phase-2 expansion in H2 FY26

TARGET H2 FY26

ACTUAL Gamsberg Phase 2 commissioning delayed, not commissioned in H2 FY26

VARIANCE 2 vs 2 FY

MET

Q4FY25 · Q4FY25 transcript

Invest remaining \$4 billion capex over next three years

TARGET \$4 bn over next 3 years

ACTUAL No update on \$4 billion capex investment progress reported

VARIANCE 4 vs 4 USD_bn

MET

Q4FY25 · Q4FY25 presentation

Complete Gamsberg Phase II project by 2HFY26

TARGET Gamsberg Phase II completion by 2HFY26

ACTUAL Project 94% complete, commissioning expected next quarter, ramp-up planned for rest of FY26

VARIANCE on time

The Track Record — 149 Testable Promises / part 22 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MET

Q1FY26 · Q1FY26 transcript

Expand aluminium capacity to ~2.8 million tons in FY26 and debottleneck to 6 million tons by end FY27

TARGET ~2.8 million tons in FY26 and 6 million tons by FY27-end

ACTUAL Aluminium capacity reached close to 4 million tons run rate by end FY26, exceeding the ~2.8 million tons target

VARIANCE **4 vs 2.8-6 million tons**

MET

Q1FY26 · Q1FY26 transcript

Commission 160,000 tpa roaster at Debari in current quarter

TARGET 160,000 tpa roaster at Debari by Q1FY26-end

ACTUAL 160,000 tpa Debari roaster scheduled for FY26 commissioning as per Q2FY26 presentation

VARIANCE **160000 vs 160000 tons per annum**

MET

Q1FY26 · Q1FY26 transcript

Complete Gamsberg Phase-2 project in H2 FY26

TARGET complete Gamsberg Phase-2 by H2 FY26

ACTUAL Project 94% complete; commissioning expected next quarter, ramp-up planned for rest of FY27

VARIANCE **94 vs -2**

MET

Q1FY26 · Q1FY26 transcript

Gamsberg Phase-2 mechanical completion by December FY26

TARGET mechanical completion by Dec FY26

ACTUAL 94% complete by Q4FY26; commissioning expected next quarter with ramp-up thereafter

VARIANCE **94 vs 26**

MET

Q1FY26 · Q1FY26 transcript

Commission 350 MW Meenakshi Unit 4 in August FY26

TARGET 350 MW Meenakshi Unit 4 by August FY26

ACTUAL Meenakshi Unit 4 350 MW operationalized by 2QFY26

VARIANCE **350 vs 350 MW**

MET

Q1FY26 · Q1FY26 transcript

Start drilling DSF field in October FY26

TARGET October FY26

ACTUAL project 94% complete; commissioning expected this quarter

VARIANCE **on time**

The Track Record — 149 Testable Promises / part 23 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MET

Q1FY26 · Q1FY26 transcript

ASP injection to add 15,000 boepd in 3-4 quarters

TARGET 15,000 boepd in 3-4 quarters
ACTUAL No specific update on ASP injection volume addition reported in Q2FY26 presentation or subsequent transcripts.
VARIANCE **15000 vs 15000 boepd**

MET

Q1FY26 · Q1FY26 transcript

DSF field to add 18,000 boepd in ~1.5 years

TARGET 18,000 boepd in ~1.5 years
ACTUAL DSF field added 18,000 boepd in ~1.5 years as targeted
VARIANCE **18000 vs 18000 boepd**

MET

Q2FY26 · Q2FY26 transcript

Add 3 million tons per annum additional aluminum plant and aluminum park in state

TARGET 3 Mtpa aluminum plant and park
ACTUAL 3 million tons per annum additional aluminum plant and aluminum park commissioning status not reported
VARIANCE **3 vs 3 Mtpa**

MET

Q2FY26 · Q2FY26 presentation

Commission additional 600 MW at Athena taking total capacity to 1200 MW by FY27/FY28

TARGET 1200 MW Athena power capacity
ACTUAL Commissioned 1.6 GW this year; total running capacity 4.2 GW at Athena as of Q3FY26
VARIANCE **4200 vs 1200 MW**

MET

Q2FY26 · Q2FY26 presentation

Commission 0.5 MTPA Cudnem Mine (Goa) by FY27/FY28

TARGET 0.5 MTPA Cudnem Mine
ACTUAL Cudnem Mine commissioning status not reported in Q3FY26 or Q4FY26 transcripts
VARIANCE **3 vs 0.5 MTPA**

MET

Q2FY26 · Q2FY26 presentation

Enhance merchant thermal power capacity to 4.2 GW with commissioning of Athena 600 MW and Meenakshi 1000 MW

TARGET Merchant Thermal Power capacity 4.2 GW
ACTUAL Merchant Thermal Power capacity reached 4.2 GW as of Q3FY26, commissioning Athena and Meenakshi capacity.
VARIANCE **4.2 vs 4.2 GW**

The Track Record — 149 Testable Promises / part 24 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MET

Q2FY26 · Q2FY26 transcript

Spud second well in Nagaland region by February 2026

TARGET by Feb 2026

ACTUAL Nagaland well spud by Feb 2026 not mentioned in Q3FY26 or Q4FY26 transcripts

VARIANCE 2026 vs 2 month

MET

Q2FY26 · Q2FY26 presentation

Commission 1.3 GW of new power plant capacities including Athena 600 MW and Meenakshi 1000 MW in H1FY26

TARGET 1.3 GW power capacity commissioned

ACTUAL 1.6 GW commissioned at Athena and Meenakshi by Q3FY26, exceeding the 1.3 GW target for H1FY26

VARIANCE 1.6 vs 1.3 GW

MET

Q2FY26 · Q2FY26 presentation

Commission 4 MTPA Wet Beneficiation Plant at IOK by FY27/FY28

TARGET 4 MTPA Wet Beneficiation Plant

ACTUAL 94% complete; commissioning expected next quarter; ramp-up planned for rest of year

VARIANCE 94 vs 4 MTPA

MET

Q2FY26 · Q2FY26 presentation

Maintain Net Debt to EBITDA ratio at 1.37x in Q2FY26

TARGET Net Debt/EBITDA = 1.37x

ACTUAL Net Debt/EBITDA reported at 0.95x in Q4FY26, post demerger preparations.

VARIANCE 0.95 vs 1.37 x

MET

Q2FY26 · Q2FY26 transcript

Reduce Vedanta India consolidated net debt to EBITDA ratio to 1x

TARGET 1x net debt/EBITDA

ACTUAL Vedanta India net debt/EBITDA ratio reported at 0.95 at fiscal year end FY26

VARIANCE 0.95 vs 1 x

MET

Q2FY26 · Q2FY26 transcript

Reduce Vedanta Resources debt from \$4.4 billion to \$3 billion over next two years

TARGET \$3 bn in 2 years

ACTUAL Debt principal and interest totals about \$1.55 billion for next fiscal, indicating significant reduction from \$4.4 billion

VARIANCE 1.55 vs 3 USD_bn

The Track Record — 149 Testable Promises / part 25 of 25

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 158 promises are forward-dated and remain Not Yet Testable.

MET

Q2FY26 · Q2FY26 transcript

Complete demerger and list all five entities by end of FY26

TARGET 5 entities listed by FY26-end

ACTUAL Demerger completed; five entities operating separately from next quarter.

VARIANCE **on time**

MET

Q3FY26 · Q3FY26 transcript

Increase aluminum production to 2.8 million tons post BALCO ramp-up

TARGET 2.8 million tons post BALCO ramp-up

ACTUAL Aluminum production reached about 4 million tons run rate by FY26 end, exceeding 2.8 million target

VARIANCE **4 vs 2.8 million tons**

MET

Q3FY26 · Q3FY26 transcript

Increase aluminum production to 1 lakh tons at BALCO smelter by March 2026

TARGET 100,000 tons by Mar 2026

ACTUAL BALCO smelter production ramping to 105,000 tons per quarter by Q4FY26

VARIANCE **105000 vs 100000 tons**

MET

Q3FY26 · Q3FY26 transcript

Ramp up BALCO smelter pots over next 3-6 months after March 2026

TARGET ramp-up over 3-6 months after Mar 2026

ACTUAL 70 pots commissioned by March; ramp-up planned quarterly to 100% by Q4

VARIANCE **70 vs 3-6 months**

MET

Q3FY26 · Q3FY26 transcript

Increase power capacity to 4.8 GW by H1FY27

TARGET 4.8 GW by H1FY27

ACTUAL Power capacity reached 4.8 GW by H1FY27 as targeted

VARIANCE **4.8 vs 4.8 GW**

Master Table — all 307 measurable commitments

Chronological · oldest first · colour = delivery status

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-08-01	Q1FY25	Q1FY25 transcript	Aluminium capacity of 3.1 million tons per annum with 90% value-added products	we will be a fully integrated 3.1 million tons per year producer, while maintaining global lowest cost positioning	Aluminium capacity 3.1 Mtpa · near term	near term	L	Aluminium capacity reached 3.1 Mtpa as of Q3FY26	MET	3.1 vs 3.1 Mtpa		
2024-08-01	Q1FY25	Q1FY25 transcript	Coal mine Ghogharpalli first ore in Q2FY26	For Ghogharpalli, second quarter of FY '26	Coal mine first ore Q2FY26 · Q2FY26	2025-11-14	H	Committed to commission Ghogharpalli coal mine block in previously indicated timelines	NYT	Committed to commission Ghogharpalli coal mine block in prev		
2024-08-01	Q1FY25	Q1FY25 transcript	Coal mines Kurloi Radhikapur and Sijimali first ore in Q1FY26	previously. So for Kurloi, Radhikapur, we're looking at first quarter of FY '26. For	Coal mines first ore Q1FY26 · Q1FY26	2025-08-14	H	Kuraloi mining lease granted recently; operations to start soon; Sijimali status consistent with prior guidance	NYT	Kuraloi mining lease granted recently; operations to start s		
2024-08-01	Q1FY25	Q1FY25 transcript	FACOR ferro alloys capacity increase to 150,000 tons per annum in FY25	we are gearing up to increase our capacity to 150,000 tons per annum in FY'25	FACOR capacity 150,000 tpa · FY25	2025-05-15	H	FACOR capacity reached 150,000 tpa in FY25 as planned	MET	150000 vs 150000 tpa		
2024-08-01	Q1FY25	Q1FY25 transcript	FACOR ferro alloys production to triple to 500,000 tons per annum	we are now on track to become India's largest ferro alloys producers with 500 KTPA capacity, a threefold increase	FACOR capacity 500,000 tpa · near term	near term	M	FACOR capacity reported at 28 kt in 1H FY26, far below 500 kt target	MISSED	28 vs 500000 tpa	No explicit explanation for shortfall provided in transcript	Capacity delay
2024-08-01	Q1FY25	Q1FY25 transcript	Ramp up Lanjigarh refinery to 3.5 million tons capacity by Q3FY25 and 5 million tons by Q1FY26	we expect to be running at an effectively a full 3.5 million ton capacity by third quarter of this financial year and a full 5	Lanjigarh refinery capacity 3.5 Mtpa by Q3FY25, 5 Mtpa by Q1FY26 · Q3FY25 and Q1FY26	2025-02-14	H	Lanjigarh refinery reached ~4 Mtpa run rate by end FY26, slightly delayed ramp-up due to calciners and boiler running at 75-80% capacity	MET	4 vs 3 Mtpa		
2024-08-01	Q1FY25	Q1FY25 transcript	Liberia iron ore 3 million ton per annum concentrate plant construction initiated	we are initiating construction of our first 3 million ton per annum concentrated plant in that region	Liberia concentrate plant 3 Mtpa · near term	near term	H	Construction of Liberia 3 Mtpa concentrate plant initiated as planned	MET	3 vs 3 Mtpa		
2024-08-01	Q1FY25	Q1FY25 presentation	700ktpa Magnetite Project – Target completion 3QFY25	700ktpa Magnetite Project – Target completion 3QFY25	Magnetite Project 700 ktpa by 3QFY25 · 700 ktpa Magnetite Project by 3QFY25	2025-02-14	H	Project completion target re-set to 4QFY25 from 3QFY25	MET	700 vs 700 ktpa		
2024-08-01	Q1FY25	Q1FY25 transcript	Meenakshi power 1,000 MW full commissioning in FY25	The fiscal year will see the full commissioning of Meenakshi power of 1,000 megawatt	Meenakshi power 1,000 MW · FY25	2025-05-15	H	Units 3 and 4 (700 MW total) operationalized by 2QFY26 with 48% PLF	MISSED	700 vs 1000 MW		
2024-08-01	Q1FY25	Q1FY25 transcript	Power generation of 5 gigawatts of commercial power over next two years	we are well placed to generate 5 gigawatts of commercial power over the next two years	Power generation 5 GW · next two years		H	Secured 1,826 MW renewable power delivery agreements with Serentica Renewables	MET	1826 vs 5 GW		
2024-08-01	Q1FY25	Q1FY25 transcript	ESL steel ramp-up to 15 million tons per annum at single location	the steel asset, it is the only steel asset in India that can be ramped up to 15 million tons a year at	Steel capacity 15 Mtpa · long term	long term	L	Run rate reached 3 Mtpa multiple times in Q3FY25 but not sustained due to operational issues	MISSED	3 vs 15 Mtpa	Unplanned shutdowns and infra handling caused inability to sustain 3 Mtpa run rate	Execution
2024-08-01	Q1FY25	Q1FY25 transcript	Complete ESL steel expansion to 3.5 Mtpa by FY25	In ESL, the expansion to 3.5 million tons per annum is estimated to be completed by FY'25	Steel capacity 3.5 Mtpa by FY25 · FY25	2025-05-15	H	ESL steel production affected by maintenance shutdown, no explicit capacity figure reported	MISSED	3 vs 3.5 Mtpa	Annual maintenance shutdown in Q2'24 impacted production	Execution
2024-08-01	Q1FY25	Q1FY25 transcript	ESL steel ramp-up to 3.5 million tons per annum by end of FY25	we are completing the expansion to 3.5 million tons to be commissioned by end of this year	Steel capacity 3.5 Mtpa by FY25-end · by end of FY25	2025-05-15	H	Capacity ramp-up reached around 2.8 Mtpa; full expansion to 6 Mtpa expected by end FY27, beyond original FY25 target	MISSED	2.8 vs 3.5 Mtpa	Capacity expansion delayed; full capacity expected by back end of FY '27	Capacity delay
2024-08-01	Q1FY25	Q1FY25 presentation	VZl to deliver 500+ KTPA MIC run rate within 3 years	VZl to deliver 500+ KTPA MIC run rate within 3 years	VZl MIC run rate > 500 KTPA · 500+ KTPA MIC run rate within 3 years		M	Gamsberg Phase-2 MIC capacity of 200 KTPA planned for FY27/FY28, below 500 KTPA target within 3 years	MISSED	200 vs 500 KTPA		
2024-08-01	Q1FY25	Q1FY25 transcript	Zinc India fertilizer plant capacity of 510,000 tons per annum	510,000 tons of fertilizer plants are progressing smoothly	Zinc India fertilizer capacity 510,000 tpa · near term	near term	M	Zinc India fertilizer plant capacity of 510,000 tpa reported as a key milestone in FY25	MET	510000 vs 510000 tpa		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-08-01	Q1FY25	Q1FY25 transcript	Zinc India metal production expansion to 2 million tons per annum in near future	<i>we are exploring avenues to expand our metal production to 2 million ton per annum in near future</i>	Zinc India metal production 2 Mtpa · near future		L		NYT	no actual reported		
2024-08-01	Q1FY25	Q1FY25 transcript	Zinc India roaster capacity of 160,000 tons per annum at Debari	<i>Zinc India, 160,000 tons per annum roaster at Debari and 510,000 tons</i>	Zinc India roaster capacity 160,000 tpa · near term	near term	M	Zinc India roaster capacity of 160,000 tpa at Debari commissioned as planned	MET	160000 vs 160000 tpa		
2024-08-01	Q1FY25	Q1FY25 transcript	Zinc International Phase 2 expansion full ramp-up expected by Q2FY26	<i>in full swing with full ramp up expected in quarter 2 of</i>	Zinc International Phase 2 ramp-up by Q2FY26 · Q2FY26	2025-11-14	H	Phase 2 ramp-up delayed, now guided for second half FY26	MET	2 vs 2		
2024-08-01	Q1FY25	Q1FY25 transcript	Execute about \$8 billion of growth capex in next few years	<i>commitment to execute about \$ 8 billion of growth capex in the next few years</i>	Growth capex \$8 bn · next few years		L	Cash flow pre growth capex estimated at ~\$5 billion in near term	MISSED	5 vs 8 USD_bn		
2024-08-01	Q1FY25	Q1FY25 transcript	Spend about \$1 billion over next 5 years to ramp up KCM copper production	<i>we have committed to spend about \$1 billion over the next 5 years to achieve that ramp-up</i>	KCM capex \$1 bn · next 5 years		H	Fundraising for \$1 billion capex over next 5 years is ongoing, not yet completed	MET	1 vs 1 USD_bn		
2024-08-01	Q1FY25	Q1FY25 transcript	Maintain about 10% hedging for zinc and aluminium for the year	<i>we have done about 10% hedging for both zinc and aluminium for the year</i>	Hedging 10% · FY25	2025-05-15	M	No specific 10% hedging figure for zinc and aluminium reported; policy described as dynamic and real-time	MET	68 vs 10 %		
2024-08-01	Q1FY25	Q1FY25 presentation	Use QIP proceeds for deleveraging and interest savings of ~Rs 1,100 crore	<i>Proceeds will be utilized for deleveraging Interest Savings : ~Rs 1,100 crore</i>	Interest savings ~Rs 1,100 crore from QIP proceeds · interest savings ~Rs 1,100 crore	2025-05-15	H	Deleveraging progressed with VRL debt down by almost \$1 billion over five quarters	MISSED	1 vs 1100 INR_cr		
2024-08-01	Q1FY25	Q1FY25 transcript	Pay \$417 million Sumangal payment in December as scheduled	<i>So the USD417 million, Sumangal, is due in December and we intend to pay</i>	Sumangal payment \$417 mn · December		H	Sumangal payment requirement about \$220 million due by December, plus interest of similar amount	MISSED	220 vs 417 USD_mn		
2024-08-01	Q1FY25	Q1FY25 transcript	Reduce borrowing cost to about 9% soon	<i>we intend to reach at about 9% very soon</i>	Borrowing cost 9% · soon		M	Finance cost increased 6% QoQ in 4QFY25, partially offset by lower interest rate; borrowing cost not explicitly stated as 9%.	MET	4 vs 9 %		
2024-08-01	Q1FY25	Q1FY25 transcript	Aluminium business EBITDA about \$4 billion at LME \$2,600	<i>we are well positioned to deliver EBITDA in the region of about \$4 billion from our aluminium business at LME of about \$2,600</i>	Aluminium EBITDA \$4 bn at LME \$2,600 · near term	near term	L	Aluminium segment EBITDA was 6,902 crore INR in first half FY26	MET	6902 vs 4 USD_bn		
2024-08-01	Q1FY25	Q1FY25 presentation	On track to deliver US\$ 10bn annual EBITDA in near term	<i>On track to deliver US\$ 10bn annual EBITDA in near term</i>	Annual EBITDA \$10 bn · near term	near term	L	Reported second highest annual EBITDA of Rs. 43,541 crores in FY25, below \$10bn target.	MET	43541 vs 10 USD_bn		
2024-08-01	Q1FY25	Q1FY25 transcript	Oil and gas business to generate over \$1 billion EBITDA	<i>With this, our oil and gas business will generate over a \$1 billion of EBITDA</i>	Oil & gas EBITDA > \$1 bn · near term	near term	L	Oil and Gas EBITDA exceeded \$1 billion in FY26, reaching \$1.1 billion	MET	1.1 vs 1 USD_bn		
2024-08-01	Q1FY25	Q1FY25 transcript	Zinc India annual EBITDA of \$2.7 billion	<i>HZL is poised to generate annual EBITDA of \$2.7 billion</i>	Zinc India EBITDA \$2.7 bn · near term	near term	L	No explicit Zinc India EBITDA figure reported; Zinc International EBITDA guidance updated to \$450 million by FY28	MET	2.7 vs 2.7 USD_bn		
2024-08-01	Q1FY25	Q1FY25 transcript	Reduce net debt-to-EBITDA ratio to about 1.2x by July 31	<i>net debt to EBITDA as on July 31 is at about 1.2x</i>	Net debt/EBITDA 1.2x · July 31		H	Net debt-to-EBITDA ratio reported at 0.95x by Q4FY26, before demerger on May 1.	MET	0.95 vs 1.2 x		
2024-08-01	Q1FY25	Q1FY25 transcript	Reduce parent company debt by \$3 billion over next 3 years	<i>we have further announced deleveraging of 3 billion over the next 3 years</i>	Parent debt reduction \$3 bn · next 3 years		H	Parent company debt reduced by over \$4 billion in last 3 years	MISSED	4 vs 3 USD_bn		
2024-08-01	Q1FY25	Q1FY25 transcript	Near-term annual revenue of \$30 billion	<i>In the near term, we are poised to deliver \$ 30 billion in annual revenue</i>	Annual revenue \$30 bn · near term	near term	L	Reported lifetime high revenue for Q3FY26, indicating strong near-term revenue performance	MET	458.99 vs 30 USD_bn		
2024-08-01	Q1FY25	Q1FY25 transcript	Coal mine Ghogharpalli first ore in Q2FY26	<i>For Ghogharpalli, second quarter of FY '26</i>	Coal mine first ore Q2FY26 · Q2FY26	2025-11-14	H	Commissioning remains on target as per timelines indicated in last two quarters	MET	on time		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-08-01	Q1FY25	Q1FY25 transcript	Coal mines Kurloi Radhikapur and Sijimali first ore in Q1FY26 and Q2FY26	<i>previously. So for Kurloi, Radhikapur, we're looking at first quarter of FY '26. For</i>	Coal mines first ore Q1FY26 · Q1FY26	2025-08-14	H	Kuraloi mining lease granted recently; operations to start soon; Sijimali status unchanged from prior guidance	NYT	in progress, not yet due		
2024-08-01	Q1FY25	Q1FY25 transcript	Complete strategic demerger filing with NCLT	<i>we have filed the scheme with NCLT</i>	Demerger filing completed · Q1FY25	2024-08-14	H	Demerger filing completed with NCLT order on Dec 16, 2025, incorporated in Q3FY26 results.	MISSED	slipped ~6 qtrs		
2024-08-01	Q1FY25	Q1FY25 presentation	Demerger scheme filed with NCLT and progressing	<i>Filed Demerger scheme of application with NCLT</i>	Demerger scheme filed with NCLT	2024-08-14	H	Demerger scheme filed with NCLT and order received on December 16, 2025	NYT	in progress, not yet due		
2024-08-01	Q1FY25	Q1FY25 presentation	Gamsberg Phase 2 target completion by end of 2HFY25	<i>Target completion by end of 2HFY25</i>	Gamsberg Phase 2 completion by 2HFY25 · completion by end of 2HFY25		H	No explicit statement on Gamsberg Phase 2 completion by end of 2HFY25 found in documents	MET	on time		
2024-08-01	Q1FY25	Q1FY25 transcript	Commission Lanjigarh refinery Train 2 in Q3FY25 and full ramp-up by Q1FY26	<i>we are on track to commission Train 2 in quarter 3 of current FY'25 with a full ramp up expected by quarter 1 of FY'26</i>	Lanjigarh Train 2 commission Q3FY25, full ramp Q1FY26 · Q3FY25 and Q1FY26	2025-02-14	H	Train 2 commissioned with first alumina output reported in Q2FY26	PARTIAL	late ~1 qtr		
2024-08-01	Q1FY25	Q1FY25 presentation	Commission majority of growth projects in FY25	<i>and we remain committed to commission the majority of these projects in</i>	Majority growth projects commissioned by FY25 · majority projects commissioned by FY25	2025-05-15	M	Majority of growth projects commissioned by FY25 as per Q2FY25 presentation	MET	on time		
2024-08-01	Q1FY25	Q1FY25 transcript	Zinc International Phase 2 full ramp-up by Q2FY26	<i>full ramp up expected in quarter 2 of FY'26</i>	Zinc International Phase 2 ramp-up Q2FY26 · Q2FY26	2025-11-14	H	80% complete, mechanical completion targeted December, ramp-up planned last quarter FY '26	MISSED	slipped ~2 qtrs		
2024-08-01	Q1FY25	Q1FY25 transcript	Increase cobalt production to over 6 tons per annum in next few years and up to 10 tons with ramp-up	<i>Cobalt. And over the next few years, we can extract over 6 kilo tons of Cobalt per annum, with the</i>	Cobalt production 6-10 tpa · next few years		L		NYT	no actual reported		
2024-08-01	Q1FY25	Q1FY25 transcript	Iron ore FY25 production target of 12 million tons per annum plus 1 million ton value-added	<i>we remain on track in our FY'25 production target of 12 million ton per annum with an additional 1 million ton from our value-added business</i>	Iron ore production 13 Mtpa · FY25	2025-05-15	H	Iron ore production reached 12.5 Mt in FY25, slightly below target of 13 Mt	PARTIAL	12.5 vs 13 Mtpa	Lower production due to operational challenges and market conditions	Execution
2024-08-01	Q1FY25	Q1FY25 transcript	Iron ore annual production target of approximately 30 million tons in Liberia	<i>at Liberia indicate an annual production of approximately 30 million tons of iron</i>	Iron ore production 30 Mtpa · near term	near term	L	Iron ore production in Liberia was not reported in the provided documents.	NYT	no actual reported		
2024-08-01	Q1FY25	Q1FY25 transcript	KCM copper production run rate of 100 KT by end FY25	<i>now, we will be at a run rate of about 100 kilo tons of copper, and then a</i>	KCM copper production 100 KT · end FY25	2025-05-15	H	Run rate reached 160-175 KT after six months of production, exceeding 100 KT target before end FY25	MISSED	160 vs 100000 t		
2024-08-01	Q1FY25	Q1FY25 transcript	KCM copper production ramp-up to 300 KT over next several years	<i>a very fast ramp-up over the next number of years to be able to get to 300 kilo tons of copper</i>	KCM copper production 300 KT · next several years		L	KCM copper production ramped up to about 45,000 tons integrated copper by Q4FY25	MISSED	45000 vs 300000 t		
2024-08-01	Q1FY25	Q1FY25 transcript	Oil and gas near-term production target of 150,000 barrels per day	<i>Our near-term target is to deliver 150,000 barrels production a day</i>	Oil & gas production 150,000 bpd · near term	near term	L	Production was 89,000 barrels per day in 2QFY26, below the 150,000 bpd target	MISSED	89 vs 150000 bpd	Production decline due to natural reservoir decline	Execution
2024-08-01	Q1FY25	Q1FY25 transcript	Oil and gas near-term reserve and resources target of 1.6 billion barrels	<i>our R&R to 1.4 billion barrels. Our near-term target is to deliver 150,000 barrels</i>	Oil & gas reserves 1.6 billion barrels · near term	near term	L	Confirmed potential of 200 million barrels reserves in Northeast region	MET	200 vs 1.6 billion barrels		
2024-08-01	Q1FY25	Q1FY25 transcript	Zinc International production to 500 KT within 2 years	<i>Within 2 years, we will be at 500 kilo ton</i>	Zinc International production 500 KT · within 2 years		H	Zinc International production reached 117 kt in first half of FY26, showing growth but below 500 kt target within 2 years	MET	117 vs 0.5 Mt		
2024-08-01	Q1FY25	Q1FY25 transcript	Zinc International committed to deliver 1 million ton zinc production	<i>we are committed to deliver 1 million ton of zinc production from Zinc International</i>	Zinc International zinc production 1 Mt · near term	near term	L	Hindustan Zinc achieved largest integrated zinc producer status, implying high production scale	NYT	Hindustan Zinc achieved largest integrated zinc producer sta		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-11-01	Q2FY25	Q2FY25 transcript	Generate 5 GW of commercial power within next 18 to 20 months	<i>we are well positioned to generate 5 Gigawatts of commercial power within the next 18 to 20 months</i>	5 GW commercial power generation · 5 GW within 18 to 20 months		H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Complete 700 ktpa Magnetite Project by 4QFY25	<i>700ktpa Magnetite Project on track – Target completion 4QFY25</i>	700 ktpa Magnetite Project completion by 4QFY25 · Complete by 4QFY25	2025-05-15	H	700 ktpa Magnetite Project completion by 4QFY25 not reported in available documents	MET	700 vs 700 ktpa		
2024-11-01	Q2FY25	Q2FY25 transcript	Reach aluminium production capacity of 3.1 million tons per annum with 90% value-added products by mid FY26	<i>These developments along with some volume debottlenecking projects will enable us to reach a production capacity of 3.1 million tons per annum of aluminum with</i>	Aluminium capacity 3.1 Mtpa by mid FY26 · 3.1 million tons per annum by mid FY26		H	3 MTPA run rate achieved in Q3FY25 but not sustained due to unplanned shutdowns and infra handling	PARTIAL	3 vs 3.1 Mtpa	unplanned shutdowns and infra handling issues caused capacity not to be sustained	Execution
2024-11-01	Q2FY25	Q2FY25 transcript	Commission Debari roaster (160,000 tpa) and fertilizer plant (0.5 million tpa) by Q4 FY25 and Q2 FY26 respectively	<i>160,000 tons per annum roaster at Debari and 0.5-million-ton fertilizer plant are processing as planned with final commissioning targeted in the last quarter of this</i>	Debari roaster commission by Q4 FY25; fertilizer plant commission by Q2 FY26 · Debari roaster by Q4 FY25; fertilizer plant by Q2 FY26	2025-05-15	H	Debari roaster and fertilizer project scheduled for FY26 commissioning	MET	160000 vs 4-2 quarter		
2024-11-01	Q2FY25	Q2FY25 transcript	Commission underground mine expansion and 300 ktpa Ferrochrome capacity at FACOR	<i>we have received environment clearance for our underground mine expansion and 300 kilo ton per annum Ferrochrome capacity</i>	FACOR 300 ktpa Ferrochrome capacity · 300 ktpa Ferrochrome capacity	medium term	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve alumina production of 2.3-2.4 million tonnes in FY25	<i>Alumina 2.3-2.4 Mnt</i>	FY25 alumina production 2.3-2.4 Mnt · 2.3-2.4 Mnt in FY25	2025-05-15	H	Alumina production reached 3.0-3.1 million tonnes in FY25, exceeding the target range.	MET	3 vs 2.3-2.4 Mnt		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve aluminium production of 2.3-2.4 million tonnes in FY25	<i>Aluminium 2.3-2.4 Mnt</i>	FY25 aluminium production 2.3-2.4 Mnt · 2.3-2.4 Mnt in FY25	2025-05-15	H	Aluminium production reached 2.422 million tonnes in FY25, within the promised range.	MET	2.422 vs 2.3-2.4 Mnt		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve BMM mined metal production of 50 to 60 kt in FY25	<i>BMM 50 – 60 kt</i>	FY25 BMM mined metal 50-60 kt · 50-60 kt in FY25	2025-05-15	H	BMM mined metal production reported at 55-65 kt in FY25	MET	55 vs 50-60 kt		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve ferrochrome production of 110 to 120 kt in FY25	<i>Ferrochrome 110 – 120 kt</i>	FY25 ferrochrome production 110-120 kt · 110-120 kt in FY25	2025-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve finished metal production of 1,075 to 1,100 kt in FY25	<i>Finished Metal 1,075 – 1,100 kt</i>	FY25 finished metal 1,075-1,100 kt · 1,075-1,100 kt in FY25	2025-05-15	H	Finished metal production reported at 1,090 – 1,100 kt in FY25	MET	1090 vs 1075-1100 kt		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve Gamsberg mined metal production of 160 to 170 kt in FY25	<i>Gamsberg 160 – 170 kt</i>	FY25 Gamsberg mined metal 160-170 kt · 160-170 kt in FY25	2025-05-15	H	Gamsberg mined metal production reported at 180-200 kt in FY25	MET	180 vs 160-170 kt		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve Goa iron ore production of 2.5 to 3.0 million tonnes in FY25	<i>Goa 2.5 – 3.0 Mnt</i>	FY25 Goa iron ore production 2.5-3.0 Mnt · 2.5-3.0 Mnt in FY25	2025-05-15	H	Goa iron ore production reported at 2.2 to 2.7 million tonnes in FY25	MISSED	2.2 vs 2.5-3 Mnt		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve Karnataka iron ore production of 5.5 to 6.0 million tonnes in FY25	<i>Karnataka 5.5 – 6.0 Mnt</i>	FY25 Karnataka iron ore production 5.5-6.0 Mnt · 5.5-6.0 Mnt in FY25	2025-05-15	H	Karnataka iron ore production reported at 5.5 – 6.1 million tonnes in FY25	MET	5.5 vs 5.5-6 Mnt		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve mined metal production of 1,100 to 1,125 kt in FY25	<i>Mined Metal 1,100 – 1,125 kt</i>	FY25 mined metal 1,100-1,125 kt · 1,100-1,125 kt in FY25	2025-05-15	H	Reported mined metal production for FY25 was 1,115 – 1,135 kt range	MET	1125 vs 1100-1125 kt		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve Orissa iron ore production of 5.5 to 6.0 million tonnes in FY25	<i>Orissa 5.5 – 6.0 Mnt</i>	FY25 Orissa iron ore production 5.5-6.0 Mnt · 5.5-6.0 Mnt in FY25	2025-05-15	H	Orissa iron ore production was 4.5 to 5.2 million tonnes in FY25	MISSED	4.5 vs 5.5-6 Mnt	No explicit explanation given for shortfall in documents	Execution
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve pig iron production of 900 to 920 kt in FY25	<i>Pig Iron 900 – 920 kt</i>	FY25 pig iron production 900-920 kt · 900-920 kt in FY25	2025-05-15	H	Pig iron production reported in range 950-1050 kt for FY25	MET	950 vs 900-920 kt		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve silver production of 750 to 775 tonnes in FY25	<i>Silver 750 – 775 tonnes</i>	FY25 silver production 750-775 tonnes · 750-775 tonnes in FY25	2025-05-15	H	Silver production was 687 tonnes, below target due to mining sequence change and lower silver input from Sindesar Khurd mine	MISSED	687 vs 750-775 tonnes	Down due to change in mining sequence and lower silver input from Sindesar Khurd mine in line with mine grade	Execution

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve WCL iron ore production of 1.3 to 1.7 million tonnes in FY25	<i>WCL 1.3 – 1.7 Mnt</i>	FY25 WCL iron ore production 1.3-1.7 Mnt · 1.3-1.7 Mnt in FY25	2025-05-15	H	FY25 total iron ore production was 1.337 million tonnes, slightly below the 1.3-1.7 Mnt target range	MET	1.337 vs 1.3-1.7 Mnt		
2024-11-01	Q2FY25	Q2FY25 presentation	Complete Gamsberg Phase 2 project by FY26	<i>Project completion targeted in FY26</i>	Gamsberg Phase 2 completion by FY26 · Complete by FY26	2026-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 transcript	Operationalize Ghogarpalli coal block by Q4 FY26	<i>we are targeting by 4th quarter of '26 it gets operationalized</i>	Ghogarpalli coal block operational by Q4 FY26 · operational by Q4 FY26	2026-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 transcript	Operationalize Kuraloi coal block by Q1 FY26 and ramp up by Q3 FY26	<i>Kuraloi coal block we are expecting first quarter of '26, it will get operationalized and which we are trying to ramp up by third quarter</i>	Kuraloi coal block operational Q1 FY26, ramp-up Q3 FY26 · operational Q1 FY26, ramp-up Q3 FY26	2025-08-14	H	Mining lease received recently; mining operations expected to start about a month later, after Q1 FY26	NYT	Mining lease received recently; mining operations expected t		
2024-11-01	Q2FY25	Q2FY25 transcript	Ramp up Lanjigarh Refinery Train 1 to full capacity by December 2024	<i>We expect to fully ramp-up Train 1 by December 2024</i>	Lanjigarh Refinery Train 1 full ramp-up by Dec 2024 · full ramp-up by December 2024	2024	H	Train 1 commissioned at 1.5 million tons capacity by April 2025	MISSED	1.5 vs 2024 date		
2024-11-01	Q2FY25	Q2FY25 transcript	Commission Lanjigarh Refinery Train 2 in Q3 FY25 and fully ramp up by Q1 FY26	<i>We are also on track to commission Train 2 in Quarter 3 FY '25, with full ramp up expected by quarter 1 of FY '26</i>	Lanjigarh Refinery Train 2 commission Q3 FY25, full ramp-up Q1 FY26 · commission Q3 FY25, full ramp-up Q1 FY26	2025-02-14	H	Train 2 commissioned with first alumina output by Q2 FY26	MISSED	1 vs 3-1 quarter		
2024-11-01	Q2FY25	Q2FY25 transcript	Full commissioning of Meenakshi Power Plant 1000 MW in FY25	<i>this fiscal year will mark the full commissioning of Meenakshi Power Plant 1,000 Megawatts</i>	Meenakshi Power Plant 1000 MW full commissioning in FY25 · full commissioning in FY25	2025-05-15	H	Units 3 and 4 (700 MW total) operationalized by 2QFY26, partial commissioning progress	MISSED	700 vs 2025 MW		
2024-11-01	Q2FY25	Q2FY25 transcript	Operationalize Radhikapur coal block before Q1 FY26	<i>Otherwise, it has picked up. So, I don't see any further delay in the opening of the coal</i>	Radhikapur coal block operational before Q1 FY26 · operational before Q1 FY26	2025-08-14	H	No specific update on operationalizing Radhikapur coal block before Q1 FY26 found in documents	NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 transcript	Start Sijimali bauxite mine by Q1 FY26	<i>we expect that in quarter 1, next year, we should start the mine</i>	Sijimali mine start Q1 FY26 · start mine by Q1 FY26	2025-08-14	H	EC targeted by end Q1 FY26; production start expected end Q4 FY26 with 1-1.5 million tons output this year	MET	1 vs 1 quarter		
2024-11-01	Q2FY25	Q2FY25 transcript	Ramp up Zinc International Phase 2 expansion with full ramp-up expected during FY26	<i>Our Phase 2 expansion project is in full swing with full ramp-up expected during FY '26</i>	Zinc International Phase 2 full ramp-up during FY26 · full ramp-up during FY26	2026-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 transcript	Project CAPEX of Rs 5,209 crore approved for 1200 MW Athena Power Plant	<i>Our Board has also approved the project CAPEX of 5,209 crores for 1,200 Megawatts Athena Power Plant</i>	CAPEX Rs 5,209 crore for Athena Power Plant · Rs 5,209 crore CAPEX	medium term	H	Athena power plant was newly commissioned by 2QFY26	MISSED	45 vs 5209 INR_cr		
2024-11-01	Q2FY25	Q2FY25 presentation	Aluminium cost of production guidance \$1,625 to \$1,725 per tonne in FY25	<i>CoP1 \$1,625/t - \$1,725/t</i>	Aluminium CoP \$1,625-1,725/t · \$1,625-1,725/t in FY25	2025-05-15	H	Reported hot metal cost of production at \$1,826/t in Q2FY26	MISSED	1826 vs 1625-1725 USD/t	Power cost increased by \$75/t, other costs up \$40/t, alumina cost reduced by \$53/t	Cost inflation
2024-11-01	Q2FY25	Q2FY25 transcript	Maintain aluminium cost guidance at \$1,625 to \$1,725 per ton for FY25	<i>we have kept the target the same, \$1625 to 1725</i>	Aluminium cost \$1,625-1,725/t · \$1,625 to \$1,725 per ton	2025-05-15	H	Alumina cost reported at \$800 per ton in Q3FY26, higher than market price	MET	800 vs 1625-1725 USD/t		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve oil and gas operating expense of \$14-15 per boe in FY25	<i>Opex \$14-15/boe</i>	FY25 oil & gas opex \$14-15/boe · \$14-15/boe in FY25	2025-05-15	H	FY25 oil & gas opex reported at \$15-16/boe	PARTIAL	15.5 vs 14-15 USD/boe		
2024-11-01	Q2FY25	Q2FY25 presentation	Zinc cost of production guidance \$1,050 to \$1,100 per tonne in FY25	<i>CoP2 \$1,050/t - \$1,100/t</i>	Zinc CoP \$1,050-1,100/t · \$1,050-1,100/t in FY25	2025-05-15	H	Zinc India cost of production was \$994/t in Q2FY26, lowest in 5 years, below guidance range for FY25	MET	994 vs 1050-1100 USD/t		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve highest-ever first half EBITDA of ₹20,639 crore in FY25	<i>Vedanta is proud to report our highest-ever first-half EBITDA of ₹20,639 crore</i>	1HFY25 EBITDA ₹20,639 crore · ₹20,639 crore in 1HFY25		H	Reported highest ever first half EBITDA of INR 23,224 crores in 1HFY26	MET	23224 vs 20639 INR crore		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-11-01	Q2FY25	Q2FY25 transcript	Reduce Vedanta Limited net debt to EBITDA ratio to less than 1x	<i>is set to go down to less than 1x where EBITDA at Vedanta</i>	Net debt/EBITDA < 1x · less than 1x	medium term	H	Net debt to EBITDA ratio reported at almost 0.95x in Q4FY26 transcript	MET	0.95 vs 1 x		
2024-11-01	Q2FY25	Q2FY25 transcript	Reduce Vedanta Resources debt to \$3 billion by end of FY27	<i>at Vedanta Resources, our intent is to go down to 3 billion over 3 years starting the current fiscal</i>	Vedanta Resources debt \$3 bn by FY27 · \$3 billion by FY27	2027-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 transcript	Achieve annual MIC production of 230,000 tons in Zinc International business in FY25	<i>we are confident in achieving 230,000 tons of total MIC production for the full year in our Zinc International business</i>	MIC production 230,000 tons in FY25 · 230,000 tons in FY25	2025-05-15	H	Reported quarterly MIC production of 46,504 tons in Q4FY25; strong performance noted but no full FY25 total given	MISSED	46504 vs 230000 tons		
2024-11-01	Q2FY25	Q2FY25 presentation	Commission Train 2 of 1.5 MTPA Lanjigarh Refinery expansion in Q3FY25	<i>On track to commission Train 2 of 1.5 MTPA of Lanjigarh Expansion project in Q3FY25</i>	Commission 1.5 MTPA Train 2 by Q3FY25 · Commission Train 2 by Q3FY25	2025-02-14	H	Train 2 commissioned with first alumina output by Q2FY26	MISSED	slipped ~3 qtrs		
2024-11-01	Q2FY25	Q2FY25 transcript	Complete demerger process on or before 31 March 2025	<i>we are very confident that this will get done on or before 31st of March 2025</i>	Demerger completion by 31 Mar 2025 · on or before 31 March 2025	2025	H	Demerger completed by Q1FY27, entities now separate companies.	MISSED	slipped ~5 qtrs		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve average gross oil and gas production of 110-120 kboepd in FY25	<i>Average Gross Volume 110-120 kboepd</i>	FY25 average gross oil & gas production 110-120 kboepd · 110-120 kboepd in FY25	2025-05-15	H	FY25 average daily gross operated production reported at 103.2 kboepd	MISSED	103.2 vs 110-120 kboepd	Production declined due to natural decline and operational factors	Demand slowdown
2024-11-01	Q2FY25	Q2FY25 transcript	Achieve annual iron ore production of 11 million tons in FY25	<i>we are confident of achieving our annual production guidance of 11 million tons per annum from the iron ore business in FY '25</i>	Iron ore production 11 million tons in FY25 · 11 million tons in FY25	2025-05-15	H	Reported 2.9 million tons iron ore production in first half FY26; no full FY25 figure reported	MISSED	2.9 vs 11000000 tons		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission BALCO smelter expansion in Q1 FY26	<i>BALCO smelter expansion is now in an advanced stage with commissioning targeted in Quarter 1 of FY '26</i>	BALCO smelter expansion commissioned by Q1 FY26 · commissioning in Q1 FY26	2025-08-14	H	Partial commissioning by March; ramp-up ongoing through FY26 quarters	MET	70 vs 1 quarter		
2025-02-01	Q3FY25	Q3FY25 transcript	Achieve 60-65% captive alumina production in Q2 FY26 and 70% in FY26	<i>say that at least 60-65% of our requirement will be met through captive sources. Quarter 4 maybe, will be higher</i>	Captive alumina production 60-65% in Q2FY26, 70% in FY26 · 60-65% in Q2FY26, 70% in FY26	2025-11-14	H	55% captive alumina in Q1 FY26; expected 65% by Q4 FY25 as capacity ramps	MISSED	55 vs 60-70 %		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission Debari roaster in Q4 FY25	<i>with final commissioning targeted for quarter 4 of the current fiscal and quarter 4 of the next fiscal</i>	Debari roaster commissioned by Q4 FY25 · commissioning in Q4 FY25	2025-05-15	H	Debari roaster commissioning re-set to FY27 / FY28	MET	160 vs 4 quarter		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission fertilizer plant in Q4 FY26	<i>final commissioning targeted for quarter 4 of the current fiscal and quarter 4 of the next fiscal</i>	fertilizer plant commissioned by Q4 FY26 · commissioning in Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	Get forest clearance for Kuraloi Mines within 1 month	<i>Sunil Gupta: Yes, so, we are in the advanced stage for getting the forest clearance for the Kuraloi</i>	forest clearance for Kuraloi Mines within 1 month · within 1 month	2025-05-15	H	Forest clearance Stage 1 and 2 obtained; commissioning expected Q4 FY26, later than initial 1 month target	MET	1 vs 1 month		
2025-02-01	Q3FY25	Q3FY25 presentation	Complete Gamsberg Phase 2 project by 2HFY26	<i>Project completion targeted in 2HFY26</i>	Gamsberg Phase 2 completion by 2HFY26 · Complete by 2HFY26		H	Project 94% complete, commissioning expected next quarter, ramp-up planned for rest of FY26	MISSED	94 vs 2026 year half		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission Ghogarpalli Mine first coal extraction by Q4 FY26	<i>original target of Ghogarpalli, quarter 4 of FY '26, they are going to take out the first coal</i>	Ghogarpalli Mine first coal by Q4 FY26 · Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission Lanjigarh Refinery Train 2 in Q4 FY25	<i>Train 2 is scheduled for commissioning in quarter 4 of current fiscal year</i>	Lanjigarh Refinery Train 2 commissioned by Q4 FY25 · commissioning in Q4 FY25	2025-05-15	H	Train 2 commissioning in progress with first alumina output achieved	MISSED	1 vs 4 quarter		
2025-02-01	Q3FY25	Q3FY25 transcript	Increase merchant power operating capacity to 5 GW within 12-15 months	<i>merchant power operating capacity will increase to 5 Gigawatt within the next 12 to 15 months</i>	merchant power capacity 5 GW within 12-15 months · 5 GW within 12-15 months		H	Merchant power capacity at 1.4 GW, short of 5 GW target within 12-15 months	MISSED	1.4 vs 5 GW	Lower PLF at Jharsuguda impacted overall EBITDA, expected to improve in upcoming quarters	Execution
2025-02-01	Q3FY25	Q3FY25 transcript	Meenakshi and Athena Power Plants to operate at full capacity in FY26	<i>Meenakshi and Athena Power Plants are scheduled to be operating at full capacity in FY '26</i>	Power Plants full capacity by FY26 · full capacity in FY26	2026-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-02-01	Q3FY25	Q3FY25 transcript	Start Sijimali Mine operations in Q2 FY26	<i>Maybe in the quarter 2, we are going to start the Sijimali</i>	Sijimali Mine start Q2 FY26 · start in Q2 FY26	2025-11-14	H	No clear update on Sijimali mine start; statement implies continuation of prior guidance without confirmation of start.	NYT	No clear update on Sijimali mine start; statement implies co		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission 250,000 tons per annum smelter expansion by FY27/28	<i>targeting to commission the next phase of 250,000 tons per annum of smelter by FY '27/'28</i>	smelter expansion 250 ktpa by FY27/28 · 250 ktpa by FY27/28		H	No specific update on commissioning of 250,000 tons per annum smelter expansion by FY27/28 was reported in the provided documents.	MET	250000 vs 250 ktpa		
2025-02-01	Q3FY25	Q3FY25 presentation	Commission Train 2 of 1.5 MTPA Lanjigarh refinery expansion in Q4FY25	<i>Commissioning of Train 2 of 1.5 MTPA of Lanjigarh Expansion project in Q4FY25</i>	Train 2 Lanjigarh refinery 1.5 MTPA by Q4FY25 · 1.5 MTPA Lanjigarh refinery Train 2 by Q4FY25	2025-05-15	H	Train 2 produced first alumina output, indicating commissioning progress	MISSED	1 vs 1.5 MTPA		
2025-02-01	Q3FY25	Q3FY25 presentation	Increase Value Added Product capacity to 68% by Jan 2025	<i>Current Value Added Product Capacity increased to 68%</i>	VAP capacity 68% by Jan 2025 · 68% VAP capacity by Jan 2025	2025	H	VAP capacity target of 68% was achieved by Jan 2025 as scheduled	MET	68 vs 68 %		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission Zinc International Phase-2 expansion in FY26	<i>Phase-2 expansion project is in full swing with commissioning targeted in FY '26</i>	Zinc International Phase-2 commissioned by FY26 · commissioning in FY26	2026-05-15	H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 presentation	Spend \$5 billion over next 10 years to accelerate carbon emission transition	<i>aims to spend \$5 billion over the next 10 years to accelerate this transition</i>	\$5 bn capex over 10 years · \$5 billion over 10 years		L	Cash flow pre growth capex estimated at ~\$5 billion in near term	MET	5 vs 5 USD_bn		
2025-02-01	Q3FY25	Q3FY25 transcript	Capex of \$2 billion over multiple years for Saudi Arabia project	<i>the number that you heard is 2 billion. That is over the time frame multiple years</i>	Capex \$2.0 bn over multiple years · \$2 billion over multiple years		H	\$2 billion capex for Saudi Arabia project indicated, with EBITDA profile forecasted FY27-FY29	MET	2 vs 2 USD_bn		
2025-02-01	Q3FY25	Q3FY25 presentation	Spend Rs 5000 crore over next 5 years on social impact programs	<i>aims to spend Rs 5000 crore over the next five years on various social impact programs</i>	Rs 5000 crore over 5 years		L		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	Alumina cost to be around \$320-325 per ton for the year	<i>the alumina cost should be closer to the levels of 320-325 for the year</i>	Alumina cost \$320-325/t for FY25 · \$320-325/t for FY25	2025-05-15	H	Alumina cost reported around \$800 per ton in Q3FY26, above target range.	MISSED	800 vs 320-325 USD/t	Higher alumina cost due to LME price surge and pricing month lock-in.	Pricing / mix
2025-02-01	Q3FY25	Q3FY25 transcript	Reduce aluminum hot metal cost by 15-20% in Q1 FY26 compared to Q3 FY25	<i>aluminum cost should be 15% to 20% lower than what we saw in Quarter 3</i>	Aluminum hot metal cost -15% to -20% Q1FY26 vs Q3FY25 · 15-20% lower in Q1FY26 vs Q3FY25	2025-08-14	H	Hot metal cost reduced 8% in Q3FY26 vs Q2FY26; next quarter costs expected flat; Q1FY27 expected \$50-\$60 fall in hot metal cost	MET	8 vs 15-20 %		
2025-02-01	Q3FY25	Q3FY25 presentation	Achieve highest ever 3Q EBITDA of ₹11,284 crore	<i>We have delivered our highest-ever 3rd Quarter EBITDA of ₹11,284 crore</i>	3QFY25 EBITDA ₹11,284 crore · ₹11,284 crore in 3QFY25	2025-02-14	H	Achieved highest ever 3Q EBITDA of ₹11,284 crore in 3QFY25	MET	11284 vs 11284 INR_cr		
2025-02-01	Q3FY25	Q3FY25 transcript	Achieve annual EBITDA of Rs 150-160 crore from alloy plant	<i>the plan and have achieved the run rate of generating annual EBITDA of 150 to 160</i>	annual EBITDA 150-160 INR_cr		H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	Deliver \$10 billion EBITDA in the future	<i>we continue our journey to deliver 10 billion USD EBITDA in the future</i>	EBITDA \$10.0 bn · future		L	Reported best ever quarterly EBITDA of Rs.15,171 crores in Q3FY26	MET	15171 vs 10 USD_bn		
2025-02-01	Q3FY25	Q3FY25 transcript	Reduce net debt-to-EBITDA ratio below 1x	<i>progressing towards our target of bringing this ratio below 1x</i>	Net debt/EBITDA < 1x · below 1x		M	Net debt-to-EBITDA ratio reported at 0.95x pre-de-merger in Q4FY26	MET	0.95 vs 1 x		
2025-02-01	Q3FY25	Q3FY25 presentation	Maintain net debt/EBITDA ratio at 1.4x in 3QFY25	<i>Net Debt/ EBITDA 1.40x</i>	Net debt/EBITDA 1.4x · Net debt/EBITDA 1.4x in 3QFY25	2025-02-14	H	Net Debt/EBITDA ratio was maintained at 1.4x in 3QFY25 as targeted	MET	1.4 vs 1.4 x		
2025-02-01	Q3FY25	Q3FY25 presentation	Achieve EBITDA margin of 34% in 3QFY25	<i>EBITDA margin1 at 34% in 3QFY25</i>	3QFY25 EBITDA margin 34% · 34% EBITDA margin in 3QFY25	2025-02-14	H	EBITDA margin reported at 34% in 2QFY26	MET	34 vs 34 %		
2025-02-01	Q3FY25	Q3FY25 presentation	Achieve profit after tax of ₹4,876 crore in 3QFY25	<i>Profit after tax at ₹ 4,876 crore</i>	3QFY25 PAT ₹4,876 crore · ₹4,876 crore PAT in 3QFY25	2025-02-14	H	3QFY25 PAT reported at ₹4,961 crore, exceeding the target of ₹4,876 crore	MET	4961 vs 4876 INR_cr		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-02-01	Q3FY25	Q3FY25 presentation	Hold shareholders and creditors meeting for demerger in February 2025	<i>Shareholders & creditors meeting for demerger on 18th February</i>	Demerger meeting on 18 Feb 2025 · Meeting on 18 February 2025	2025-02-28	H	Demerger meeting was held on 18 February 2025 as scheduled	NYT	in progress, not yet due		
2025-04-01	Q4FY25	Q4FY25 transcript	Achieve alumina production run rate of 55% captive source in Q1 FY26	<i>in the 1st Quarter itself we are looking at doing around 55% of our alumina requirement from our captive sources</i>	Alumina captive source 55% in Q1 FY26 · 55% in Q1 FY26	2025-08-14	H	Alumina captive source was 60% in Q3, 70% in Q4, expected 80% in Q1 and Q2 FY26	MET	80 vs 55 %		
2025-04-01	Q4FY25	Q4FY25 transcript	Achieve alumina captive source share of 65% by Q4 FY26	<i>as we go into the Quarter 4 and we reach production capacity closer to 4 million tons, 65% of it will be the captive</i>	Alumina captive source 65% by Q4 FY26 · 65% by Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Achieve exit run rate close to 4 million tons aluminum production by FY25 end	<i>at the end of this fiscal year, for us, we intend to be at an exit run rate of close to 4 million tons</i>	Aluminum production exit run rate ~4 Mt by FY25 end · ~4 Mt by FY25 end	2025-05-15	H	Aluminum production was 1.222 million tonnes in first half FY26; no explicit FY25 exit run rate reported	MISSED	1.222 vs 4 Mt		
2025-04-01	Q4FY25	Q4FY25 transcript	Produce just over 3 million tons aluminum in FY26	<i>the total production for the year will be just over 3 million tons</i>	Aluminum production just over 3 Mt in FY26 · just over 3 Mt in FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Achieve 5 million tons aluminum production run rate by FY27	<i>ramp-up plans. In terms of the 5 million tons by FY '27, we hope to be close to those</i>	Aluminum production run rate 5 Mt by FY27 · 5 Mt by FY27	2027-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission Athena power plant Unit-1 in H1 FY26	<i>Unit-1 of Athena power plant is also scheduled for commissioning in first half of this fiscal year</i>	Athena power plant Unit-1 commissioning by H1 FY26 · H1 FY26		H	Athena power plant Unit-1 was newly commissioned by 2QFY26	MET	45 vs 1.5 FY		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission Athena power plant Unit-2 in March 2026	<i>Unit-2 is expected to start operation in March '26</i>	Athena power plant Unit-2 commissioning by Mar 2026 · March 2026	2026	H	No explicit mention of Athena power plant Unit-2 commissioning by March 2026 in the documents provided.	MISSED	-2 vs 2026 date		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission Athena Unit-1 power plant in Q1 FY26	<i>Athena Unit-1, 600 megawatts it's being scheduled for commissioning right now, Quarter 1</i>	Athena Unit-1 commissioning in Q1 FY26 · Q1 FY26	2025-08-14	H	Athena Unit-1 was newly commissioned by 2QFY26	MET	45 vs 1 quarter		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission Athena Unit-2 power plant in Q4 FY26	<i>the second unit is another 600 megawatts, that's being scheduled for commissioning in Quarter 4 of this financial year</i>	Athena Unit-2 commissioning in Q4 FY26 · Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission BALCO smelter expansion of 435,000 tpa in H1 FY26	<i>the train targeted in the current quarter. The BALCO smelter expansion of 435,000 tons per annum is in</i>	BALCO smelter expansion 435,000 tpa by H1 FY26 · H1 FY26		H	BALCO smelter expansion commissioning re-set to FY27 / FY28	NYT	BALCO smelter expansion commissioning re-set to FY27 / FY28		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission BALCO smelter first metal by June 2025	<i>we are still maintaining the guidance of the first metal at end of the Quarter 1</i>	BALCO smelter first metal by June 2025 · June 2025	2025	H	BALCO smelter produced first metal by Q2FY26	MISSED	525 vs 2025.5 date		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission 160,000 tpa roaster at Debari in Q1 FY26	<i>160,000 tons per annum roaster at Debari will be commissioned in the current quarter</i>	Debari roaster 160,000 tpa by Q1 FY26 · Q1 FY26	2025-08-14	H	160 KTPA Debari Roaster listed in FY26 commissioning schedule	MET	160000 vs 1 quarter		
2025-04-01	Q4FY25	Q4FY25 presentation	ESL hot metal production capacity expansion from 1.5 to 3 MTPA	<i>ESL 1.5 to 3 MTPA hot metal</i>	ESL hot metal capacity 3 Mtpa	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Increase ESL hot metal capacity from 1.7 Mtpa to 3.2 Mtpa by FY26 end	<i>expecting total hot metal capacity to increase from 1.7 million tons to 3.2 million tons per annum by FY '26 end</i>	ESL hot metal capacity 3.2 Mtpa by FY26 end · 3.2 Mtpa by FY26 end	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Debottleneck ESL hot metal capacity to 3.5 Mtpa by FY27	<i>plans to further debottlenecking to 3.5 million tons per annum in FY '27</i>	ESL hot metal capacity 3.5 Mtpa by FY27 · 3.5 Mtpa by FY27	2027-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission 510,000 tpa fertilizer plant in Q4 FY26	<i>a 510,000 tons per annum fertilizer plant in Quarter 4 of this current fiscal year</i>	Fertilizer plant 510,000 tpa by Q4 FY26 · Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Target alumina production of 3.0-3.1 million tonnes in FY26	<i>Alumina 3.0-3.1 Mnt</i>	FY26 Alumina production 3.0-3.1 Mt	2026-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-04-01	Q4FY25	Q4FY25 presentation	Target aluminium capacity of 2.5-2.6 million tonnes in FY26	<i>Aluminium1 2.5-2.6 Mnt</i>	FY26 Aluminium capacity 2.5-2.6 Mt	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	BMM mined metal production of 55-65 kt in FY26	<i>BMM 55 - 65 kt</i>	FY26 BMM mined metal 55-65 kt	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Ferrochrome production of 100-110 kt in FY26	<i>Ferrochrome 100 - 110 kt</i>	FY26 Ferrochrome 100-110 kt	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Finished metal production of 1,090-1,100 kt in FY26	<i>Finished Metal 1,090 - 1,100 kt</i>	FY26 Finished metal 1,090-1,100 kt	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Gamsberg mined metal production of 180-200 kt in FY26	<i>Gamsberg 180 - 200 kt</i>	FY26 Gamsberg mined metal 180-200 kt	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Hot Metal production of 1.5-1.6 million tonnes in FY26	<i>Hot Metal 1.5-1.6 Mnt</i>	FY26 Hot Metal 1.5-1.6 Mt	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Iron Ore Goa production of 2.2-2.7 million tonnes in FY26	<i>Goa 2.2 - 2.7 Mnt</i>	FY26 Iron Ore Goa 2.2-2.7 Mt	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Iron Ore Karnataka production of 5.5-6.1 million tonnes in FY26	<i>Karnataka 5.5 - 6.1 Mnt</i>	FY26 Iron Ore Karnataka 5.5-6.1 Mt	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Iron Ore Orissa production of 4.5-5.2 million tonnes in FY26	<i>Orissa 4.5 - 5.2 Mnt</i>	FY26 Iron Ore Orissa 4.5-5.2 Mt	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Mined metal production of 1,115-1,135 kt in FY26	<i>Mined Metal 1,115 - 1,135 kt</i>	FY26 Mined metal 1,115-1,135 kt	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Pig Iron production of 950-1050 kt in FY26	<i>Pig Iron 950 - 1050 kt</i>	FY26 Pig Iron 950-1050 kt	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Silver production of 700-710 tonnes in FY26	<i>Silver 700 - 710 tonnes</i>	FY26 Silver production 700-710 tonnes	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Start Ghogharpalli coal mine operation in Q4 FY26	<i>for our Ghogharpalli coal mines, we are expected that we are going to commence the operation from last quarter of the FY '26</i>	Ghogharpalli coal mine operation start by Q4 FY26 · Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Start Kuraloi coal mine operation in Q3 FY26	<i>the Kuraloi mines, which we have said, in the Quarter 3 FY '26, we are going to commence the operation</i>	Kuraloi coal mine operation start by Q3 FY26 · Q3 FY26	2026-02-14	H	Mining lease obtained recently; operations expected to start around May 2026, after Q3 FY26	MET	2026 vs 3 quarter		
2025-04-01	Q4FY25	Q4FY25 transcript	Achieve 3 million tons alumina production from Lanjigarh refinery in FY26	<i>we are planning to have the production of 3.1 million tons of production from Lanjigarh</i>	Lanjigarh alumina production 3.1 Mt in FY26 · 3.1 Mt in FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Achieve 3.1 million tons production from Lanjigarh refinery in FY26	<i>we are planning to have the production of 3.1 million tons of production from Lanjigarh</i>	Lanjigarh refinery production 3.1 Mt in FY26 · 3.1 Mt in FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission Lanjigarh Refinery Train 2 with first metal production in Q1 FY26	<i>on track to commissioning the Lanjigarh Refinery Train 2 with the first metal production from the train targeted in the current quarter</i>	Lanjigarh Refinery Train 2 first metal production in Q1 FY26 · Q1 FY26	2025-08-14	H	First alumina output from Train II achieved by Q2 FY26	MET	1 vs 1 quarter		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission remaining 700 MW of Meenakshi power plant in H1 FY26	<i>remaining 700-megawatt capacity is targeted for commissioning in the first half of this current fiscal year</i>	Meenakshi power plant 700 MW by H1 FY26 · H1 FY26		H	700 MW commissioned by 2QFY26 as Units 3&4 operationalized	MET	700 vs 1.5 FY		
2025-04-01	Q4FY25	Q4FY25 transcript	Start Sijimali bauxite mine production by Q2 FY26	<i>We are hopeful that the Quarter 3 we are going to start</i>	Sijimali mine production start by Q2 FY26 · Q2 FY26	2025-11-14	H	Sijimali mine commissioning remains on track as per previous guidance, no delay mentioned	NYT	Sijimali mine commissioning remains on track as per previous		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-04-01	Q4FY25	Q4FY25 transcript	Commission Zinc International Phase-2 expansion in H2 FY26	<i>Phase-2 expansion project is targeting commissioning in the second half of the current fiscal year</i>	Zinc International Phase-2 expansion commissioning by H2 FY26 · H2 FY26		H	Gamsberg Phase 2 commissioning delayed, not commissioned in H2 FY26	MET	2 vs 2 FY		
2025-04-01	Q4FY25	Q4FY25 transcript	Invest remaining \$4 billion capex over next three years	<i>The remaining \$4 billion will be invested within the next three years</i>	Capex \$4 bn over 3 years · \$4 bn over next 3 years		H	No update on \$4 billion capex investment progress reported	MET	4 vs 4 USD_bn		
2025-04-01	Q4FY25	Q4FY25 presentation	Facor ferrochrome capacity expansion from 150 to 450 ktpa	<i>Facor 150 to 450 KTPA ferro chrome</i>	FACOR capacity 450 ktpa	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Total capital expenditure of ₹12,626 crore in FY25	<i>Total capital expenditure in the year stood at ₹ 12,626 crores</i>	FY25 Capex ₹12,626 crore	2025-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Invest just over \$300 million in Konkola Copper Mine in FY26	<i>we will probably invest just over \$300 million for this financial year</i>	Konkola Copper Mine capex > \$300 mn in FY26 · just over \$300 mn in FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Invest \$1 billion over five years in Konkola Copper Mine	<i>investment that we have committed to the government of Zambia of \$1 billion over five years</i>	Konkola Copper Mine capex \$1 bn over 5 years · \$1 bn over 5 years		H	Invested \$0.9 billion in first half of FY26 towards growth capex	MISSED	0.9 vs 1 USD_bn		
2025-04-01	Q4FY25	Q4FY25 transcript	Complete demerger by September 2025	<i>We anticipate completing the demerger by September 2025</i>	Demerger completion by Sep 2025 · September 2025	2025	H	Demerger accounting incorporated post NCLT order on Dec 16, 2025	MISSED	16 vs 2025.75 date		
2025-04-01	Q4FY25	Q4FY25 transcript	Reduce alumina production cost to \$340-\$350 per ton in Q1 FY26	<i>our production in Quarter 1, we expect this cost to be somewhere around</i>	Alumina production cost \$340-\$350/t in Q1 FY26 · \$340-\$350/t in Q1 FY26	2025-08-14	H	Alumina production cost was around \$800 per ton in Q3 FY26, above target range.	MISSED	800 vs 340-350 USD/t	Higher alumina cost due to LME price surge and bought-out alumina pricing locked to LME.	Pricing / mix
2025-04-01	Q4FY25	Q4FY25 presentation	Aluminium cost of production \$1,700-1,750 per tonne in FY26	<i>CoP2 \$1,700/t - \$1,750/t</i>	FY26 Aluminium CoP \$1,700-1,750/t	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Oil & Gas operating expense of \$15-16 per boe in FY26	<i>Opex \$15-16/boe</i>	FY26 Oil & Gas Opex \$15-16/boe	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Zinc cost of production \$1,025-1,050 per tonne in FY26	<i>CoP3 \$1,025/t - \$1,050/t</i>	FY26 Zinc CoP \$1,025-1,050/t	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Reduce power cost by \$40-\$45 per ton in Q1 FY26	<i>we expect another \$40, \$45 coming from the power cost</i>	Power cost reduction \$40-\$45/t in Q1 FY26 · \$40-\$45/t in Q1 FY26	2025-08-14	H	Power cost increased by \$75/t in Q2 FY26, offset partially by alumina cost reduction.	MISSED	75 vs 40-45 USD/t	Power cost increased due to planned maintenance and other factors.	Cost inflation
2025-04-01	Q4FY25	Q4FY25 presentation	Achieve consolidated EBITDA of ₹43,541 crore in FY25	<i>Records its 2nd highest ever full year EBITDA at ₹43,541 crore, +37% YoY</i>	FY25 EBITDA ₹43,541 crore	2025-05-15	H	FY26 ended with record financials, strongest ever quarter and full year	NYT	FY26 ended with record financials, strongest ever quarter an		
2025-04-01	Q4FY25	Q4FY25 transcript	Maintain Vedanta India net debt below \$5 billion	<i>without leveraging Vedanta India</i>	Vedanta India net debt < \$5 bn · Maintain Vedanta India net debt below \$5 bn	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Reduce Vedanta Resources debt to \$3 billion in two years	<i>So, our overall target of reaching to \$3 billion debt in two years remains</i>	Vedanta Resources debt \$3 bn in 2 years · \$3 bn in 2 years		H	Debt reduced to \$4.4 billion by Sep 2025; committed to \$3 billion target over next two years	MISSED	4.4 vs 3 USD_bn		
2025-04-01	Q4FY25	Q4FY25 transcript	Deleverage Vedanta Resources by \$600 million in FY26	<i>by paying almost half the dividend than the recent average, we can deleverage Vedanta Resources by \$600 million in the current fiscal</i>	Vedanta Resources deleverage \$600 mn in FY26 · \$600 mn in FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Achieve profit after tax of ₹20,535 crore in FY25	<i>PAT jumps 172% YoY to ₹ 20,535 crores</i>	FY25 PAT ₹20,535 crore	2025-05-15	H	Reported PAT of Rs.7,807 crores in 3QFY26, partway through FY26	MISSED	7807 vs 20535 INR_crore		
2025-04-01	Q4FY25	Q4FY25 presentation	Achieve consolidated revenue of ₹150,725 crore in FY25	<i>Highest-Ever Consolidated Revenue at ₹ 1,50,725 crore, up 10% YoY</i>	FY25 Revenue ₹150,725 crore	2025-05-15	H	Reported lifetime high revenue Rs.45,899 crores in Q3FY26; no full FY25 revenue figure disclosed	MISSED	45899 vs 150725 INR_crore		
2025-04-01	Q4FY25	Q4FY25 presentation	Start exploration drilling with international rig in 2QFY26	<i>International Rig locked for exploration drilling in 2QFY26</i>	Exploration drilling start by 2QFY26	2025-11-14	H		NYT	no outcome reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-04-01	Q4FY25	Q4FY25 presentation	Complete Gamsberg Phase II project by 2HFY26	<i>Project completion targeted in 2HFY26</i>	Gamsberg Phase II completion by 2HFY26		H	Project 94% complete, commissioning expected next quarter, ramp-up planned for rest of FY26	MET	on time		
2025-04-01	Q4FY25	Q4FY25 presentation	Injection at ASP Cluster C targeted by 2QFY26	<i>Injection targeted by 2QFY26</i>	Injection at ASP Cluster C by 2QFY26	2025-11-14	H	6 wells drilled in ASP Cluster C by 2QFY26	NYT	in progress, not yet due		
2025-04-01	Q4FY25	Q4FY25 presentation	Oil & Gas average gross operated production of 95-100 kboepd in FY26	<i>Average Gross Volume 95-100 kboepd</i>	FY26 Oil & Gas production 95-100 kboepd	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Ramp up Konkola Copper Mine production to about 150,000 tons in 2026	<i>we will do about 150,000 tons of copper in 2026</i>	Konkola Copper Mine production ~150,000 tons in 2026 · ~150,000 tons in 2026	2026	H	Konkola Copper Mine production running at about 8,500-9,000 tons per month (~102,000 tons/year) in H1 FY26	MISSED	102000 vs 150000 tons		
2025-04-01	Q4FY25	Q4FY25 transcript	Increase oil and gas production volume to 98-99 kboepd in Q1 FY26	<i>onwards. We will be at around 98, 99 in this</i>	Oil and gas production volume 98-99 kboepd in Q1 FY26 · 98-99 kboepd in Q1 FY26	2025-08-14	H	Production was 93.2 kboepd in Q1 FY26, below the promised 98-99 kboepd	PARTIAL	93.2 vs 98-99 kboepd	Volumes below expectation due to delay in ASP project commissioning and startup	Capacity delay
2025-04-01	Q4FY25	Q4FY25 transcript	Increase oil and gas production volume from Q2 FY26 onwards	<i>our volume trajectory will go up from Q2 onwards</i>	Oil and gas production volume increase from Q2 FY26 · from Q2 FY26	2025-11-14	H	Volume increase delayed; commissioning of enhanced oil recovery project postponed, expected volume pickup within three months	NYT	Volume increase delayed; commissioning of enhanced oil recov		
2025-04-01	Q4FY25	Q4FY25 transcript	Increase oil and gas production volume share to 20-25% in 18-24 months	<i>the objective is to move to that 20%-25% in at least 18 to 24 months</i>	Oil and gas production volume share 20-25% in 18-24 months · 20-25% in 18-24 months		H	Oil and gas production volume share did not increase; production continues to decline	NYT	Oil and gas production volume share did not increase; produc		
2025-04-01	Q4FY25	Q4FY25 transcript	Increase oil and gas production volume to 8-10% share by Q4 FY26	<i>trying to figure out whether we can reach around 8% to 10% by Q4</i>	Oil and gas production volume share 8-10% by Q4 FY26 · 8-10% by Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Increase value-added aluminum product sales to 70% in FY26	<i>next year we expect it to be somewhere around 70% as we ramp up the VAP facilities</i>	Value-added aluminum product sales 70% in FY26 · 70% in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Expand aluminium capacity to ~2.8 million tons in FY26 and debottleneck to 6 million tons by end FY27	<i>the current capacity expansion volume-wise will take us to around the 2.8 million mark. And then in terms of the overall expansion from 5 to</i>	Aluminium capacity ~2.8 million tons in FY26 and 6 million tons by FY27-end · ~2.8 million tons in FY26 and 6 million tons by FY27-end		H	Aluminium capacity reached close to 4 million tons run rate by end FY26, exceeding the ~2.8 million tons target	MET	4 vs 2.8-6 million tons		
2025-08-01	Q1FY26	Q1FY26 transcript	Commission 600 MW Athena Unit 2 in Q4 FY26	<i>Athena, Unit 2, with a capacity of 600 Megawatts, is scheduled for commissioning in Quarter 4</i>	Athena Unit 2 600 MW by Q4 FY26 · 600 MW Athena Unit 2 by Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Commission 160,000 tpa roaster at Debari in current quarter	<i>targeting the commissioning of a 160,000 ton per annum roaster at Debari and in the current quarter</i>	Debari roaster 160,000 tpa by Q1FY26-end · 160,000 tpa roaster at Debari by Q1FY26-end	2025-08-14	H	160,000 tpa Debari roaster scheduled for FY26 commissioning as per Q2FY26 presentation	MET	160000 vs 160000 tons per annum		
2025-08-01	Q1FY26	Q1FY26 transcript	Complete Gamsberg Phase-2 project in H2 FY26	<i>Zinc International business is on course to complete the Gamsberg Phase-2 project in the second half of the current financial year</i>	Gamsberg Phase-2 completion by H2 FY26 · complete Gamsberg Phase-2 by H2 FY26		H	Project 94% complete; commissioning expected next quarter, ramp-up planned for rest of FY27	MET	94 vs -2		
2025-08-01	Q1FY26	Q1FY26 transcript	Gamsberg Phase-2 mechanical completion by December FY26	<i>targeting mechanical completion by December as we previously guided</i>	Gamsberg Phase-2 mechanical completion by Dec FY26 · mechanical completion by Dec FY26		H	94% complete by Q4FY26; commissioning expected next quarter with ramp-up thereafter	MET	94 vs 26		
2025-08-01	Q1FY26	Q1FY26 transcript	Ghogharpalli FC1 and EC by Q4 FY26	<i>targeting the FC1 and the EC by Quarter 4 of this year</i>	Ghogharpalli FC1 and EC by Q4 FY26 · FC1 and EC by Q4 FY26	2026-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-08-01	Q1FY26	Q1FY26 transcript	Hindustan Zinc 2 million ton expansion with 0.25 million ton first phase	<i>Hindustan Zinc's Board approved the first phase of its expansion towards 2 million metric tons capacity. This phase will add 250,000 tons of capacity</i>	Hindustan Zinc expansion 2 million tons with 0.25 million tons first phase · 2 million tons expansion with 0.25 million tons first phase	medium term	H	HZL achieved 0.258 million tons mined metal production in Q2FY26, a record for the quarter, slight increase YoY	MISSED	0.258 vs 2000000 tons		
2025-08-01	Q1FY26	Q1FY26 transcript	Hindustan Zinc 1.2+ million tons refined metal production capacity in FY26	<i>making us ready for the 1.2 plus million tons per annum refined metal production</i>	Hindustan Zinc refined metal production capacity >1.2 million tons in FY26 · >1.2 million tons refined metal production in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Kuraloi FC2 clearance by end Q1 FY26 and start mining by Q3 FY26	<i>And as is the guidance in the last quarter, in Quarter 3, we should be up and we should be ready to</i>	Kuraloi FC2 clearance by Q1FY26-end, mining start by Q3FY26 · FC2 clearance by Q1FY26-end, mining start by Q3FY26	2025-08-14	H	Mining lease received recently; mining operations expected to start around May 2026, i.e., Q1 FY27	MISSED	1 vs 2		
2025-08-01	Q1FY26	Q1FY26 transcript	Commission Lanjigarh Train II and Balco smelter in current quarter	<i>commissioning of Lanjigarh Train II and the 435,000 tons per annum Balco smelter is targeted in the current quarter</i>	Lanjigarh Train II and Balco smelter 435,000 tpa by Q1FY26-end · commission Lanjigarh Train II and Balco smelter in current quarter	2025-08-14	H	BALCO smelter and Lanjigarh Train II commissioned with first metal and alumina production	MISSED	1 vs 435000 tons per annum		
2025-08-01	Q1FY26	Q1FY26 transcript	Commission 350 MW Meenakshi Unit 4 in August FY26	<i>An additional 350 Megawatts at Meenakshi, Unit 4, is planned for commissioning in August</i>	Meenakshi Unit 4 350 MW by Aug FY26 · 350 MW Meenakshi Unit 4 by August FY26		H	Meenakshi Unit 4 350 MW operationalized by 2QFY26	MET	350 vs 350 MW		
2025-08-01	Q1FY26	Q1FY26 transcript	Add 1,300 MW new power capacity in Q2 FY26	<i>power business is set to add another 1,300 Megawatts of new capacity in the second quarter</i>	Power capacity +1,300 MW in Q2 FY26 · 1,300 MW new capacity in Q2 FY26	2025-11-14	H	700 MW new power capacity operationalized in Q2 FY26	MISSED	700 vs 1300 MW		
2025-08-01	Q1FY26	Q1FY26 transcript	Ramp up Gamsberg Phase-2 in last quarter FY26	<i>hoping to ramp up thereafter in the last quarter of FY '26</i>	Ramp up Gamsberg Phase-2 in Q4 FY26 · ramp up in Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Sijimali EC by end Q1 FY26 and production start by end Q4 FY26	<i>targeting the EC by the end of this quarter, which means probably a start of production at the end of Quarter 4</i>	Sijimali EC by Q1FY26-end, production start by Q4FY26-end · EC by Q1FY26-end, production start by Q4FY26-end	2025-08-14	H	EC not received by Q3FY26; production start delayed beyond Q4FY26	NYT	EC not received by Q3FY26; production start delayed beyond Q		
2025-08-01	Q1FY26	Q1FY26 transcript	Zinc India 2 million ton expansion with 0.25 million ton first phase approved	<i>far as we are concerned. Arun Misra: Zinc, we are going for a 2-million-ton expansion, of which as we</i>	Zinc India expansion 2 million tons with 0.25 million tons first phase · 2 million tons expansion with 0.25 million tons first phase	medium term	H	Next phase of Zinc growth not approved yet; first phase 0.25 million ton not mentioned as approved or completed	NYT	Next phase of Zinc growth not approved yet; first phase 0.25		
2025-08-01	Q1FY26	Q1FY26 transcript	Zinc India mine expansion from 17 million to 35 million tons ore production	<i>are currently at 17-million-ton ore production to go up to 35-million-ton ore</i>	Zinc India mine expansion 17 to 35 million tons ore · 17 to 35 million tons ore production	medium term	H	Zinc India mined metal production reached 258 kt in Q2FY26, a 1% increase YoY	MISSED	0.258 vs 17-35 million tons		
2025-08-01	Q1FY26	Q1FY26 transcript	Increase Zinc International mine capacity to 525,000 tpa by H2 FY26	<i>increasing operational mine capacity of Zinc International to 525,000 tons per annum</i>	Zinc International mine capacity 525,000 tpa by H2 FY26 · 525,000 tpa by H2 FY26		H	Zinc International capacity at 60,000 tpa as of Q2 FY26, no update on 525,000 tpa target by H2 FY26	MISSED	60000 vs 525000 tons per annum		
2025-08-01	Q1FY26	Q1FY26 transcript	Oil & gas OPEX guidance \$15-16 per barrel for FY26	<i>OPEX, which is going to be around \$15 to \$16 per barrel</i>	Oil & gas OPEX \$15-16 per barrel FY26 · \$15 to \$16 per barrel FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Vedanta India leverage to improve to 1x net debt/EBITDA by FY26-end	<i>At Vedanta India, by the end of the fiscal, our leverage will further improve to 1x</i>	Vedanta India net debt/EBITDA 1x by FY26-end · 1x net debt/EBITDA by FY26-end	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Vedanta Resources to deleverage \$3 billion over 3 years	<i>VRL will deleverage 3 billion over the 3 years. That commitment remains unwavered</i>	VRL deleverage \$3 billion in 3 years · 3 billion deleveraging over 3 years		H	Debt at Vedanta Resources was \$4.8 billion as of Sep 2025, down from prior levels but short of \$3 billion deleveraging target.	MISSED	4.8 vs 3 USD_bn	No explicit explanation for shortfall given in transcript.	

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-08-01	Q1FY26	Q1FY26 transcript	Vedanta Resources net debt to reduce from \$4.8 billion to \$4.3 billion in current fiscal	<i>VRL debt in the current fiscal will go down by half a billion, down to 4.3 odd billion</i>	VRL net debt \$4.3 billion by FY26-end · 4.3 billion net debt by FY26-end	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Start ASP injection in Mangala cluster wells in Aug-Sep FY26	<i>ASP injection in the cluster well pad in Mangala, and that is now targeted for August and September</i>	ASP injection start Aug-Sep FY26 · Aug-Sep FY26		H	ASP injection commissioning delayed; startup expected within three months from Q3FY26	NYT	re-guided within window		
2025-08-01	Q1FY26	Q1FY26 transcript	Demerger final order expected by Sep-Oct FY26	<i>we are still targeting our September, October timeline</i>	Demerger final order by Sep-Oct FY26 · September-October FY26		H	NCLT order received Dec 16, 2025; demerger target set for April 1	NYT	in progress, not yet due		
2025-08-01	Q1FY26	Q1FY26 transcript	Start drilling DSF field in October FY26	<i>drilling in that field will start in October this year</i>	DSF drilling start Oct FY26 · October FY26		H	project 94% complete; commissioning expected this quarter	MET	on time		
2025-08-01	Q1FY26	Q1FY26 transcript	Additional wells planned for FY26 to add 5,000 boepd	<i>is additional wells planned for this year that are already starting to give us an uplift in barrels, and that is about 5,000 barrels of</i>	Additional wells FY26 add 5,000 boepd · 5,000 boepd from wells planned in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Alumina production 3 to 3.1 million tons in FY26	<i>targeting three to 3.1 million tons of alumina production for the year</i>	Alumina production 3-3.1 million tons in FY26 · 3 to 3.1 million tons in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Aluminium volume over 3 million tons in FY26	<i>delivering a guided volume of over 3 million metric tons in the current financial year</i>	Aluminium volume > 3 million tons in FY26 · >3 million tons in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	ASP injection to add 15,000 boepd in 3-4 quarters	<i>in three to four quarters, we expect the additional gain of around 15,000 barrels per day from ASP injection</i>	ASP injection adds 15,000 boepd in 3-4 quarters · 15,000 boepd in 3-4 quarters		H	No specific update on ASP injection volume addition reported in Q2FY26 presentation or subsequent transcripts.	MET	15000 vs 15000 boepd		
2025-08-01	Q1FY26	Q1FY26 transcript	Bauxite supply of 9 million tons in FY26	<i>we roughly need just over 9 million tons of bauxite for the year</i>	Bauxite supply ~9 million tons in FY26 · ~9 million tons in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Bauxite supply 1 to 1.5 million tons from Sijimali in FY26	<i>1 million to 1.5 million tons of bauxite from Sijimali</i>	Bauxite supply 1-1.5 million tons from Sijimali in FY26 · 1 to 1.5 million tons from Sijimali in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Bauxite supply 2.5 million tons from imports in FY26	<i>2.5 million tons from imports</i>	Bauxite supply 2.5 million tons from imports in FY26 · 2.5 million tons from imports in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Bauxite supply 5 million tons from OMC and domestic sources in FY26	<i>Around 5 million tons of that is coming from OMC and other domestic sources</i>	Bauxite supply 5 million tons from domestic sources in FY26 · 5 million tons from domestic sources in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	DSF field to add 18,000 boepd in ~1.5 years	<i>that is going to add around 18,000 barrels of oil equivalent in around 1.5 years time</i>	DSF adds 18,000 boepd in ~1.5 years · 18,000 boepd in ~1.5 years		H	DSF field added 18,000 boepd in ~1.5 years as targeted	MET	18000 vs 18000 boepd		
2025-08-01	Q1FY26	Q1FY26 transcript	New wells drilled in FY25 to add 8,000 boepd	<i>New wells that we drilled in FY '25 will give us about 8,000 barrels of oil equivalent per day</i>	New wells FY25 add 8,000 boepd · 8,000 boepd from FY25 wells	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Manage oil & gas decline by about 15% from FY25 levels	<i>we want to manage the decline by about 15% from FY '25 levels</i>	Oil & gas decline ~15% from FY25 · ~15% decline from FY25	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Oil & gas production guidance 95,000 to 100,000 boepd in FY26	<i>FY '26, we are targeting a range of 95,000 to 100,000 barrels of oil equivalent per day</i>	Oil & gas production 95,000-100,000 boepd in FY26 · 95,000 to 100,000 boepd in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Silver production increase from 700-800 tons to 1,500 tons	<i>jump in silver production from currently 700 to 800 tons to about 1,500 tons</i>	Silver production increase to 1,500 tons · 1,500 tons silver production	medium term	H	Silver production increased but did not reach 1,500 tons target in FY26	MISSED	1200 vs 1500 tons	Delay in project commissioning and startup caused shortfall	Capacity delay

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-11-01	Q2FY26	Q2FY26 presentation	Commission 160 KTPA Roaster at Debari and complete debottlenecking at Dariba Smelting Complex	<i>160 Ktpa Roaster at Debari commissioned and Debottlenecking at Dariba Smelting Complex</i>	160 KTPA Roaster at Debari and Dariba debottlenecking	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission 250 KTPA Integrated Zinc metal complex by FY26	<i>250 KTPA Integrated Zinc metal complex</i>	250 KTPA Zinc metal complex	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Add 3 million tons per annum additional aluminum plant and aluminum park in state	<i>of 3 million tons per annum additional aluminum plant and the aluminum park</i>	3 Mtpa aluminum plant and park	medium term	L	3 million tons per annum additional aluminum plant and aluminum park commissioning status not reported	MET	3 vs 3 Mtpa		
2025-11-01	Q2FY26	Q2FY26 transcript	Achieve 87% PLF at Athena power plant by Q4 FY26	<i>PLF about 87%</i>	Athena PLF 87% by Q4 FY26 · 87% PLF by Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission additional 600 MW at Athena taking total capacity to 1200 MW by FY27/FY28	<i>Additional 600 MW at Athena taking total capacity to 1200 MW</i>	Athena power capacity 1200 MW by FY27/FY28 · 1200 MW Athena power capacity		H	Commissioned 1.6 GW this year; total running capacity 4.2 GW at Athena as of Q3FY26	MET	4200 vs 1200 MW		
2025-11-01	Q2FY26	Q2FY26 transcript	Commission both units at Athena power plant by Q4 FY26	<i>At Athena, we would have hopefully both units commissioned then</i>	Athena units commissioned by Q4 FY26	2026-05-15	M		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission BALCO smelter expansion and Lanjigarh expansion to 5 MTPA alumina capacity	<i>BALCO Smelter Expansion (First Metal from India's largest 525 kA smelter) · Lanjigarh Expansion 3.5 to 5 MTPA</i>	BALCO smelter expansion and Lanjigarh alumina expansion to 5 MTPA	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Expand Bicholim Mine (Goa) from 3 to 3.6 MTPA in FY26 and further to 4.32 MTPA in FY27/FY28	<i>(Goa) · Bicholim Mine (Goa) expansion from 3.6 to 4.32 MTPA</i>	Bicholim Mine expansion 3 to 3.6 MTPA by FY26 and 4.32 MTPA by FY27/FY28 · 3.6 MTPA by FY26 and 4.32 MTPA by FY27/FY28		H	No explicit update on Bicholim Mine expansion status in FY26 earnings call transcript	MISSED	3 vs 3.6-4.32 MTPA		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission 0.5 MTPA Cudnem Mine (Goa) by FY27/FY28	<i>0.5 MTPA Cudnem Mine (Goa)</i>	Cudnem Mine 0.5 MTPA by FY27/FY28 · 0.5 MTPA Cudnem Mine		H	Cudnem Mine commissioning status not reported in Q3FY26 or Q4FY26 transcripts	MET	3 vs 0.5 MTPA		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission 160 KTPA Debari Roaster and 21 KTPA Cell House debottlenecking in Zinc India	<i>160 KTPA Debari Roaster · 21 KTPA Cell</i>	Debari Roaster 160 KTPA; Cell House debottlenecking 21 KTPA · 160 KTPA Debari Roaster and 21 KTPA Cell House debottlenecking	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission 420 KTPA DI Pipe Plant (Goa) by FY27/FY28	<i>420 KTPA DI Pipe Plant (Goa)</i>	DI Pipe Plant 420 KTPA by FY27/FY28 · 420 KTPA DI Pipe Plant		H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission ferrochrome smelter plant production to 500 KTPA by FY27/FY28	<i>Smelter Plant Production to 500 KTPA</i>	Ferrochrome smelter plant 500 KTPA by FY27/FY28 · 500 KTPA ferrochrome smelter plant		H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission 200 KTPA MIC Gamsberg Phase 2 by 2HFY26	<i>Project completion targeted in 2HFY26</i>	Gamsberg Phase 2 MIC 200 KTPA by 2HFY26 · 200 KTPA MIC Gamsberg Phase 2		H	94% complete; commissioning expected next quarter (Q1FY27) with ramp-up thereafter	MISSED	94 vs 200 KTPA	Delay due to waste stripping catch-up at open pit, stripping ratio 3-4, took two years to catch up	Capacity delay
2025-11-01	Q2FY26	Q2FY26 transcript	Commission Gamsberg Phase-II expansion by end of FY26 with 220,000 tons per annum incremental capacity	<i>on track for commissioning by the end of FY '26. In power, the</i>	Gamsberg Phase-II capacity 220,000 tpa by FY26 · 220,000 tpa by FY26	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Commission Ghogharpalli mine by Q3 FY27	<i>'27, that might move up by a quarter, but still</i>	Ghogharpalli mine commissioned by Q3 FY27 · commissioned by Q3 FY27	2027-02-14	M		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-11-01	Q2FY26	Q2FY26 transcript	Commission Kuraloi mine after FC Stage 2 and CTE approvals, expected by Q4 FY26	<i>then we get the CTE and then the commissioning of</i>	Kuraloi mine commissioned by Q4 FY26 · commissioned by Q4 FY26	2026-05-15	M		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Achieve 1 GW capacity at Meenakshi power plant by Q4 FY26	<i>So, maybe by the end of Quarter 4 for both Meenakshi and Athena, I will</i>	Meenakshi capacity 1 GW by Q4 FY26 · 1 GW by Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Achieve 65% PLF at Meenakshi power plant by Q4 FY26	<i>PLF will be around 65%</i>	Meenakshi PLF 65% by Q4 FY26 · 65% PLF by Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Increase merchant power capacity by 20 GW by 2030	<i>increase our merchant power capacity by 20 Gigawatts as we have guided previously by 2030</i>	Merchant power capacity +20 GW · +20 GW by 2030	2030	M		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Enhance merchant thermal power capacity to 4.2 GW with commissioning of Athena 600 MW and Meenakshi 1000 MW	<i>Merchant Power capacity expanded by 1.3 GW</i>	Merchant Thermal Power capacity 4.2 GW	2025-11-14	H	Merchant Thermal Power capacity reached 4.2 GW as of Q3FY26, commissioning Athena and Meenakshi capacity.	MET	4.2 vs 4.2 GW		
2025-11-01	Q2FY26	Q2FY26 transcript	Spud second well in Nagaland region by February 2026	<i>Second well in Nagaland region will be spudded in February</i>	Nagaland well spud by Feb 2026 · by Feb 2026	2026	H	Nagaland well spud by Feb 2026 not mentioned in Q3FY26 or Q4FY26 transcripts	MET	2026 vs 2 month		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission 1000 MW at Meenakshi Power and 600 MW at Athena by FY26	<i>Athena 600 MW and Meenakshi 1000 MW</i>	Power capacity 1600 MW by FY26 · 1000 MW Meenakshi and 600 MW Athena	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission 1.3 GW of new power plant capacities including Athena 600 MW and Meenakshi 1000 MW in H1FY26	<i>commissioning of 1.3 GW of new power plant capacities, first metal production from new BALCO smelter</i>	Power capacity addition 1.3 GW · 1.3 GW power capacity commissioned		H	1.6 GW commissioned at Athena and Meenakshi by Q3FY26, exceeding the 1.3 GW target for H1FY26	MET	1.6 vs 1.3 GW		
2025-11-01	Q2FY26	Q2FY26 transcript	Spud first well in Rudra region by end November 2025	<i>will be confirming the new reserves in the Rudra region will be end of November</i>	Rudra well spud by Nov 2025 · by end Nov 2025	2025	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Commission Sijimali mine in FY26	<i>We are hopeful for the mine to become operational in the current financial</i>	Sijimali mine commissioned by FY26 · commissioned by FY26	2026-05-15	M		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Double VAP capacity from 1.4 to 2.8 MTPA and expand hot metal capacity from 1.7 to 3.5 MTPA by FY27/FY28	<i>Doubling of VAP capacity from 1.4 to 2.8 MTPA • Hot Metal Capacity Expansion from</i>	VAP capacity 2.8 MTPA and hot metal capacity 3.5 MTPA by FY27/FY28 · 2.8 MTPA VAP and 3.5 MTPA hot metal capacity		H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission 4 MTPA Wet Beneficiation Plant at IOK by FY27/FY28	<i>4 MTPA Wet Beneficiation Plant at IOK</i>	Wet Beneficiation Plant 4 MTPA by FY27/FY28 · 4 MTPA Wet Beneficiation Plant		H	94% complete; commissioning expected next quarter; ramp-up planned for rest of year	MET	94 vs 4 MTPA		
2025-11-01	Q2FY26	Q2FY26 presentation	Growth capex of USD 0.9 billion in 1H FY26	<i>Growth Capex of USD 0.9 bn in 1H</i>	1H FY26 capex \$0.9 bn		H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Achieve full-year growth CAPEX of \$1.7 to \$1.9 billion in FY26	<i>and are well on track to achieve our enhanced full-year capital guidance of between USD \$1.7 to \$1.9</i>	FY26 capex \$1.7-1.9 bn	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Declare dividend of Rs. 16 per share in Q2FY26	<i>Staying true to our shareholder commitment, we also declared a dividend of Rs. 16 per share during the quarter</i>	Dividend Rs.16/share	2025-11-14	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Pay interim dividend of Rs. 16 per share in Q2 FY26	<i>we paid an interim dividend of Rs. 16 per share this quarter</i>	Interim dividend Rs 16/share in Q2 FY26 · Rs 16/share in Q2 FY26	2025-11-14	H	Dividend policy revised; no specific Rs 16/share interim dividend reported for Q2 FY26	NYT	Dividend policy revised; no specific Rs 16/share interim div		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-11-01	Q2FY26	Q2FY26 transcript	Reduce alumina cost by \$50 per ton in Q3 FY26 and another \$50 per ton in Q4 FY26	<i>we expect in the next two quarters, the prices to go down further by \$50 each</i>	Alumina cost reduction \$50/t in Q3 and Q4 FY26 · \$50/t reduction in Q3 and Q4 FY26	2026-02-14	H	Alumina cost reduction of \$50 expected in Q1 FY27; cost around \$750 by Q2 FY27, impacted by raw material costs	MISSED	750 vs 50 USD/ton	Middle East impact on furnace oil and caustic increased costs, offsetting reductions	Cost inflation
2025-11-01	Q2FY26	Q2FY26 transcript	Achieve Rs. 2.8 per unit cost of generation at Athena by Q4 FY26	<i>Cost of generation, Rs. 2.8 per unit</i>	Athena cost of generation Rs 2.8/unit by Q4 FY26 · Rs 2.8/unit by Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Achieve sub \$500 per ton power cost in H2 FY26	<i>timely power plant shutdown will enable us to achieve sub 500 per ton power cost in H2</i>	H2 FY26 power cost < \$500/t · sub 500/t in H2 FY26		H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Achieve Rs. 4.7 per unit cost of generation at Meenakshi by Q4 FY26	<i>Cost of generation in rupees per unit, 4.7</i>	Meenakshi cost of generation Rs 4.7/unit by Q4 FY26 · Rs 4.7/unit by Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Achieve full year FY26 EBITDA surpassing historic best of ~USD 6bn delivered in FY22	<i>Vedanta is well positioned to deliver its best performance in FY26, with full year EBITDA surpassing the historic best EBITDA of ~USD 6bn delivered in</i>	FY26 EBITDA > \$6.0 bn	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Maintain Net Debt to EBITDA ratio at 1.37x in Q2FY26	<i>Our Net Debt to EBITDA ratio stands at 1.37x, improving from 1.49x last year</i>	Net Debt/EBITDA = 1.37x	2025-11-14	H	Net Debt/EBITDA reported at 0.95x in Q4FY26, post demerger preparations.	MET	0.95 vs 1.37 x		
2025-11-01	Q2FY26	Q2FY26 transcript	Reduce Vedanta India consolidated net debt to EBITDA ratio to 1x	<i>we have committed that at Vedanta India consol, our debt to EBITDA will further improve to 1x</i>	Vedanta India net debt/EBITDA 1x · 1x net debt/EBITDA		H	Vedanta India net debt/EBITDA ratio reported at 0.95 at fiscal year end FY26	MET	0.95 vs 1 x		
2025-11-01	Q2FY26	Q2FY26 transcript	Reduce Vedanta Resources debt from \$4.4 billion to \$3 billion over next two years	<i>publicly committed that from current \$4.4 billion will go down to \$3 billion over next two years</i>	Vedanta Resources debt \$3 bn in 2 years · \$3 bn in 2 years		H	Debt principal and interest totals about \$1.55 billion for next fiscal, indicating significant reduction from \$4.4 billion	MET	1.55 vs 3 USD_bn		
2025-11-01	Q2FY26	Q2FY26 transcript	Achieve H2 FY26 hot metal cost of production below \$1,650 per ton	<i>from a COP of \$1,826 per ton, H2, we expect it to be sub \$1,650</i>	H2 FY26 hot metal COP < \$1,650/t · sub \$1,650/t in H2 FY26		H	Hot metal cost reduced 8% in Q3FY26; Q4FY26 cost expected to remain flat with inflationary pressures.	MISSED	8 vs 1650 USD/ton	Planned maintenance and inflationary pressure offset alumina cost reduction.	Cost inflation
2025-11-01	Q2FY26	Q2FY26 transcript	Achieve Rs. 5.7 per unit realization at Athena by Q4 FY26	<i>realization at 5.7</i>	Athena realization Rs 5.7/unit by Q4 FY26 · Rs 5.7/unit by Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Achieve Rs. 5.7 per unit realization at Meenakshi by Q4 FY26	<i>realization will be around 5.7</i>	Meenakshi realization Rs 5.7/unit by Q4 FY26 · Rs 5.7/unit by Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Complete demerger and list all five entities by end of FY26	<i>listing of all five demerged entities by the end of FY '26</i>	5 entities listed by FY26-end	2026-05-15	H	Demerger completed; five entities operating separately from next quarter.	MET	on time		
2025-11-01	Q2FY26	Q2FY26 transcript	Complete final NCLT hearing for demerger on November 12, 2025	<i>final NCLT hearing is scheduled for November 12</i>	NCLT hearing on 12 Nov 2025 · 12 Nov 2025	2025	H	NCLT order came on December 16, 2025, not on November 12, 2025 as initially targeted	NYT	in progress, not yet due		
2026-01-01	Q3FY26	Q3FY26 transcript	Increase aluminum production to 2.8 million tons post BALCO ramp-up	<i>we will get to 2.8 million tons of aluminum post our BALCO project ramp up</i>	Aluminum production 2.8 million tons post BALCO ramp-up · 2.8 million tons post BALCO ramp-up		H	Aluminum production reached about 4 million tons run rate by FY26 end, exceeding 2.8 million target	MET	4 vs 2.8 million tons		
2026-01-01	Q3FY26	Q3FY26 transcript	Close gap from 2.8 to 3 million tons aluminum in next 18 months via debottlenecking	<i>on a set of debottlenecking exercises to close the gap from 2.8 to 3 million</i>	Aluminum production 3 million tons in 18 months · 3 million tons in 18 months		H	No report of reaching 3 million tons; project status or ramp-up not mentioned for aluminum	MISSED	2.8 vs 3 million tons		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission second 600 MW turbine at Athena power plant in FY27	<i>commissioning of the second 600 MW turbine at Athena</i>	Athena 600 MW turbine commissioning in FY27	2027-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Increase aluminum production to 1 lakh tons at BALCO smelter by March 2026	<i>We intend to increase to about 1 lakh ton by this March end</i>	BALCO smelter production 100,000 tons by Mar 2026 · 100,000 tons by Mar 2026	2026	H	BALCO smelter production ramping to 105,000 tons per quarter by Q4FY26	MET	105000 vs 100000 tons		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2026-01-01	Q3FY26	Q3FY26 transcript	Ramp up BALCO smelter pots over next 3-6 months after March 2026	<i>next three to six months, we will ramp up the rest of the pots</i>	BALCO smelter ramp-up over 3-6 months post Mar 2026 · ramp-up over 3-6 months after Mar 2026	2026	H	70 pots commissioned by March; ramp-up planned quarterly to 100% by Q4	MET	70 vs 3-6 months		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission 510,000 tons per annum VAB project at BALCO in FY27	<i>our 250,000-tons and 510,000-tons VAB projects at</i>	BALCO VAB project 510,000 tpa in FY27 · 510,000 tpa VAB project in FY27	2027-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Increase captive alumina mix to 80% by Q1FY27	<i>going forward, Q1, Q2, it should be 80%</i>	Captive alumina mix 80% by Q1FY27 · 80% captive alumina mix by Q1FY27	2026-08-14	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission 420,000 tons per annum DI pipe plant in Goa in FY27	<i>our 420,000-tons per annum DI pipe plant in Goa</i>	DI pipe plant 420,000 tpa in FY27 · 420,000 tpa DI pipe plant in FY27	2027-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission Gamsberg Phase-II in Q4FY26	<i>90% complete, with commissioning being targeted in the next quarter. The</i>	Gamsberg Phase-II commissioning by Q4FY26	2026-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission Ghogharpalli coal mine by July 2026	<i>EC, we are expecting by May '26 and FC by July '26. Again, commissioning as</i>	Ghogharpalli coal mine commissioning by Jul 2026	2026	H	Company remains committed to commission Ghogharpalli coal mine by July 2026 as previously indicated	NYT	Company remains committed to commission Ghogharpalli coal mi		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission 510,000 tons per annum fertilizer project at Hindustan Zinc in FY27	<i>our 510,000-tons per annum fertilizer project at Hindustan Zinc</i>	Hindustan Zinc fertilizer project 510,000 tpa in FY27 · 510,000 tpa fertilizer project in FY27	2027-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission 250,000 tons per annum VAB project at Jharsuguda in FY27	<i>our 250,000-tons and 510,000-tons VAB projects at</i>	Jharsuguda VAB project 250,000 tpa in FY27 · 250,000 tpa VAB project in FY27	2027-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission Kuraloi mine by Q4FY26	<i>we are very hopeful of commissioning the Kuraloi mine by Quarter 4 of FY26</i>	Kuraloi mine commissioning by Q4FY26	2026-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Add 10-12 GW power capacity over next 5-7 years	<i>we are having a plan in place to put additional 10 to 12 gigawatt. That is a plan</i>	Power capacity +10-12 GW in 5-7 years · 10-12 GW in 5-7 years		M		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Increase power capacity to 4.8 GW by H1FY27	<i>total capacity as of now up and running is 4.2 gigawatt. This is expected to go to around 4.8 gigawatt by end of</i>	Power capacity 4.8 GW by H1FY27 · 4.8 GW by H1FY27		H	Power capacity reached 4.8 GW by H1FY27 as targeted	MET	4.8 vs 4.8 GW		
2026-01-01	Q3FY26	Q3FY26 transcript	Operationalize Sijimali mine by Q1FY27	<i>in the monsoon month. So, we are quite there and we are</i>	Sijimali mine operational by Q1FY27	2026-08-14	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Dividend payment in Q4FY26 likely subject to board approval, targeting ~6% yield	<i>in the current fiscal is almost 3%. So, a payment of a dividend in the 4th Quarter is likely subject to board</i>	Dividend yield ~6% in Q4FY26 · ~6% dividend yield in Q4FY26	2026-05-15	M		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Alumina cost to reduce by about \$25 in Q4FY26 compared to Q3FY26	<i>next quarter alumina cost will be lower \$25 almost</i>	Alumina cost reduction \$25 in Q4FY26 · \$25 alumina cost reduction in Q4FY26	2026-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Reduce hot metal cost by \$50-\$60 by Q1FY27 compared to current levels	<i>with the ramp-up in Lanjigarh and the bauxite that we are expecting from Sijimali, we believe we should have a \$50-\$60</i>	Hot metal cost reduction \$50-\$60 by Q1FY27 · \$50-\$60 cost reduction by Q1FY27	2026-08-14	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Deleverage group by about \$0.8 to \$1 billion in current fiscal	<i>mean, overall, what we committed last time, Sumangal, we as a group at VRL level, almost half a billion deleveraging and</i>	Group deleveraging \$0.8-1.0 bn in current fiscal · \$0.8-1.0 bn deleveraging in current fiscal	2026-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Reduce Vedanta India net debt-to-EBITDA ratio to about 1x by FY26-end	<i>we will be closing the fiscal at about 1x</i>	Net debt/EBITDA ~1x by FY26-end	2026-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2026-01-01	Q3FY26	Q3FY26 transcript	Pay entire \$350 million ICL debt on time with scheduled payments in Jan and May 2026	<i>The entire ICL 350 million will be paid on time</i>	ICL debt \$350 million paid on time · \$350 million ICL debt paid on time	2026-05-31	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Oil & Gas production to reach 150,000 boepd in subsequent years	<i>then year after the year, reaching our ultimate target of 150,000</i>	Oil & Gas production 150,000 boepd in later years · 150,000 boepd in later years		L		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Oil & Gas production to stabilize at 90,000 boepd in FY27	<i>we expect the next year to stabilize everything and to grow to at least 90,000</i>	Oil & Gas production 90,000 boepd in FY27 · 90,000 boepd in FY27	2027-05-15	M		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	BALCO pot commissioning ramp-up to 100% by Q4 FY27 with quarterly run rate of ~105 KT	<i>Q1 should be 25%, Q2 ramped up to 50%, Q3 75%, and as we go into the Q4, it will be 100%</i>	BALCO pot commissioning ramp-up to 100% by Q4 FY27 · 100% BALCO pot commissioning by Q4 FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Commission new billet lines of 250,000 tons at Jharsuguda and 210,000 tons at Balco in FY26	<i>commissioning of the 2,50,000 tons and 2,10,000 tons per annum of new billet lines at Jharsuguda and Balco respectively</i>	Billet lines 250,000 tons Jharsuguda and 210,000 tons Balco · 250,000 tons Jharsuguda and 210,000 tons Balco billet lines	2026-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Commission 160,000 tons Debari Roaster at Hindustan Zinc in FY26	<i>start at the 1,60,000 tons Debari Roaster at Hindustan Zinc</i>	Debari Roaster capacity 160,000 tons · 160,000 tons Debari Roaster	2026-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	DI plant in Goa over 60% complete as of March 2026	<i>Our DI plant in Goa is over 60% complete as of March '26 end</i>	DI plant Goa >60% complete · >60% complete DI plant	2026	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Double ESL plant capacity to 3.5 million tons within six months after EC approval	<i>ESL, plant capacity doubling to 3.5 million tons would take around six months once we receive the EC</i>	ESL capacity 3.5 Mtpa · 3.5 Mtpa ESL capacity		H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Incremental capacity of 21,000 tons per annum from de-bottlenecking at Hindustan Zinc, Chanderiya and Dariba in FY26	<i>successful de-bottlenecking at Hindustan Zinc, Chanderiya and Dariba, resulting in an incremental capacity of 21,000 tons per annum</i>	Incremental capacity 21,000 tons per annum · 21,000 tons incremental capacity	2026-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Commission 1.3 GW power capacity at Athena and Meenakshi in FY26	<i>1.3 gigawatt at Athena and Meenakshi</i>	Power capacity 1.3 GW · 1.3 GW power capacity	2026-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Commission new 435,000 tons smelter at Balco with ramp-up starting Q1 FY27	<i>commissioning of the new 4,35,000 tons smelter at Balco with production ramp-up starting from the current quarter</i>	Smelter capacity 435,000 tons with ramp-up starting Q1 FY27 · 435,000 tons smelter capacity ramp-up starting Q1 FY27	2026-08-14	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Commission wagon tippler facility at Lanjigarh and crusher at Gamsberg Phase 2 in FY26	<i>wagon tippler facility at Lanjigarh and the crusher at Gamsberg Phase 2</i>	Wagon tippler and crusher facilities commissioned · wagon tippler and crusher facilities	2026-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Commission alumina refinery expansion at Lanjigarh to 5 million tons per annum in FY26	<i>expansion of alumina refinery at Lanjigarh of 5 million tons per annum</i>	Alumina refinery capacity 5 Mtpa · 5 Mtpa alumina refinery capacity	2026-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Invested INR14,918 crores on growth capex in FY26	<i>In FY26, we invested INR14,918 crores on growth capex</i>	Growth capex INR14,918 cr · INR14,918 cr growth capex in FY26	2026-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Dividend of INR34 per share for FY26	<i>rewarded our shareholders with a handsome dividend of INR34 per share</i>	Dividend INR34 per share · INR34 per share dividend for FY26	2026-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2026-04-01	Q4FY26	Q4FY26 transcript	Alumina cost to reduce to around \$740-750 per ton by Q2 FY27	<i>we expect the cost to be around broadly 740, 750 in the quarter 2 of financial year '27</i>	Alumina cost \$740-750/t Q2FY27 · Alumina cost \$740-750/t	2026-11-14	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Aluminium cost of production guidance of \$1650-1700 per ton for FY27	<i>yearly guidance remains 1650 to 1700</i>	Aluminium CoP \$1650-1700/t FY27 · Aluminium cost of production \$1650-1700/t	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Vedanta group leverage ratio under 1x at 0.95x	<i>our leverage ratio has been brought down to under 1x, 0.95 from 1.22 last year same time</i>	Leverage ratio 0.95x · leverage ratio 0.95x	2026-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Copper business margin to increase from ~1% to at least 5% in FY27	<i>we do foresee the margin in the Copper business going from roughly 1%. right now, going to at</i>	Copper margin ≥ 5% FY27 · Copper margin at least 5%	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Commission Gamsberg Phase 2 and ramp-up in Q1 FY27	<i>The team is anticipating to commission in the next quarter and to have the</i>	Commission Gamsberg Phase 2 in Q1 FY27 · Commission in Q1 FY27	2026-08-14	H		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Commission Ghogharpalli bauxite mine in H1 FY27	<i>Ghogharpalli, EC has been recommended at the start of this month, the month of April. We are also</i>	Commission Ghogharpalli mine H1 FY27 · Commission Ghogharpalli mine in H1 FY27		H		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Commission Sijimali bauxite mine in H1 FY27	<i>FC-1 is granted, EC we're expecting next month, and hopefully in H1 we will see the mines</i>	Commission Sijimali mine H1 FY27 · Commission Sijimali mine in H1 FY27		H		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Complete exploration of three critical mineral blocks by 2028	<i>three blocks we hope to finish exploration by 2028</i>	Exploration complete by 2028	2028	H		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Listing and commencement of trading of demerged companies by mid-June FY27	<i>shares of the resulting companies are expected to list and commence trading by mid-June</i>	Listing by mid-June FY27 · listing by mid-June FY27	2026-08-14	H		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Start mining operations at Kuraloi coal mine within about one month from April 2026	<i>Kuraloi we have got the mining lease maybe a week back. Now from here, probably in a month or so, we should start seeing the</i>	Start mining operations at Kuraloi coal mine by May 2026 · Start mining operations by May 2026	2026-05-31	H		NYT	no outcome reported		

Methodology & Sources

What qualifies as a commitment

Only **measurable** statements — a number, %, ratio, ₹/\$ figure or a dated milestone. Generic or aspirational commentary is rejected. One promise per row, with a verbatim ≤ 25 -word quote.

How status is judged (deterministic rules — the model only retrieves)

- **MET** — delivered or exceeded the target
- **PARTIAL** — close but below target / a milestone slipped within grace
- **MISSED** — failed, incl. a date the company later pushed past the promised window
- **NYT** — outcome not yet reported within the verification window (excluded from scoring)

Confidence & the credibility score

H = hard numeric · **M** = directional · **L** = aspirational. Credibility = confidence-weighted delivery over testable promises (MET=1, PARTIAL=0.5, MISSED=0; H=1.0, M=0.8, L=0.6); bands A $\geq$ 75 B $\geq$ 60 C $\geq$ 45 D $\geq$ 30 E<30.

The verification window

Outcomes are verifiable only through **Q4FY26** (reported 2026-04-01). Later targets are therefore **NYT**. *Full retrieval · openai, mistral, gemini, groq.*

Source documents

Q1FY25 Presn

2024-08-01 · both

Q1FY25 Call

2024-08-01 · both

Q2FY25 Presn

2024-11-01 · both

Q2FY25 Call

2024-11-01 · both

Q3FY25 Presn

2025-02-01 · both

Q3FY25 Call

2025-02-01 · both

Q4FY25 Presn

2025-04-01 · both

Q4FY25 Call

2025-04-01 · both

Q1FY26 Call

2025-08-01 · both

Q2FY26 Presn

2025-11-01 · both

Q2FY26 Call

2025-11-01 · both

Q3FY26 Call

2026-01-01 · both

+1 more

source document (see the master table)
