

VEDL Lie Detector

Every **measurable** management commitment — extracted from the earnings calls and investor decks, then verified against reported actuals across **Q2FY25-Q1FY27**.



DELIVERY VS. DEADLINES

Delivery  54
Timelines  26

Live · complete

208

Measurable commitments tracked

109

Testable now · 63 delivered / partial

46

Missed — incl. slipped deadlines

99

Not yet testable (later periods)

Q2FY25 Presn · 2024-11-01

Q2FY25 Call · 2024-11-01

Q3FY25 Presn · 2025-02-01

Q3FY25 Call · 2025-02-01

Q4FY25 Presn · 2025-04-01

Q4FY25 Call · 2025-04-01

Q1FY26 Presn · 2025-08-01


Q1FY26 Call · 2025-08-01

Verification window: through Q1FY27
(reported 2026-07-01)


Executive Dashboard

A mixed delivery record — chiefly capacity delay; 99 later targets still not yet testable.


STATUS OF ALL 208 COMMITMENTS

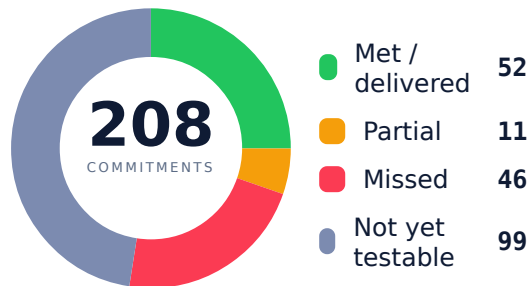

COMMITMENTS BY REPORTING QUARTER

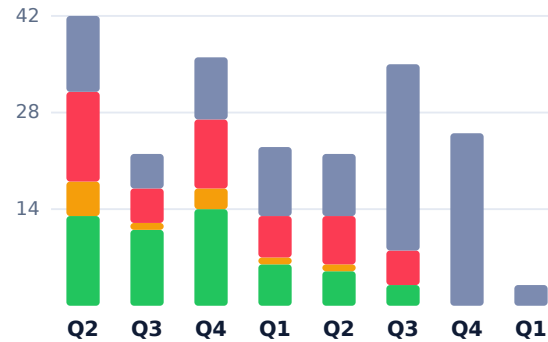

ROOT CAUSE OF MISSES & SHORTFALLS



A mixed delivery record — chiefly capacity delay; 99 later targets still not yet testable.

Of the 8 dated commitments that came due, 0 landed on time and 8 slipped right. The slippage timeline is overleaf.

CREDIBILITY SIGNALS — WHERE THE RECORD SHOWS


- 49% of the verdict rests on hard Tier-1 (binary) outcomes.
- Wide beats on 13/23 guided metrics — a conservative bar.
- 11% of explained misses blamed on external factors.

02 Deadline Slippage & Execution Momentum

Each row is one dated commitment: the amber dot is where it was **promised**, the second dot is where it **actually landed** (its colour is the verdict). Below, the reported EBITDA and margin trend.

TIMELINE COMMITMENTS — PROMISED → WHERE IT ACTUALLY LANDED

● Promised date ● Where it landed — dot colour is the verdict (green met · amber partial · red missed) --- the slip

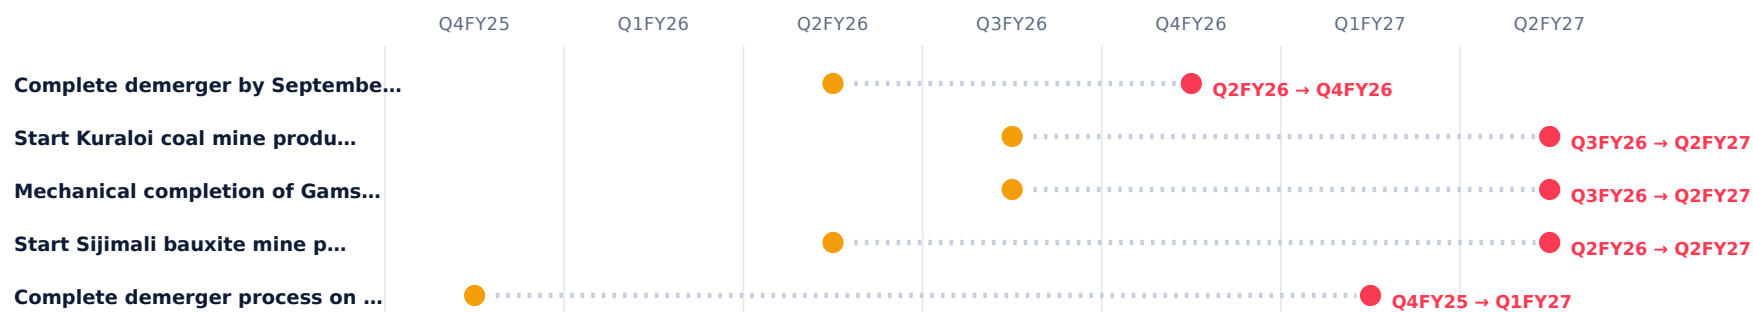

Showing the 5 largest slips · +3 more timeline commitments in the master table

EXECUTION MOMENTUM — EBITDA (₹ CR) & MARGIN



0.95x

Net debt / EBITDA · Q4

₹39,789 cr

Revenue · Q4

The Track Record — 109 Testable Promises / part 1 of 19

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MISSED

Q2FY25 · Q2FY25 transcript

Reach 3.1 Mtpa aluminium capacity with 90% value-added products by FY26

TARGET 3.1 Mtpa by FY26**ACTUAL** Aluminium capacity reached 2.456 Mtpa; 90% value-added products by FY26**VARIANCE** **2.46 vs 3.1 Mtpa****MISSED**

Q2FY25 · Q2FY25 presentation

Complete Gamsberg Phase 2 by FY26

TARGET FY26 completion**ACTUAL** Gamsberg Phase 2 re-set to Q2FY27**VARIANCE** **2 vs 26****MISSED**

Q2FY25 · Q2FY25 transcript

Commission Lanjigarh Refinery Train 2 in Q3 FY '25 with full ramp-up by Q1 FY '26

TARGET Commission Q3FY25, ramped Q1FY26**ACTUAL** Train 2 commissioned in Q2FY26**VARIANCE** **1 vs 3****MISSED**

Q2FY25 · Q2FY25 transcript

Fully commission 1,000 MW Meenakshi Power Plant in FY25

TARGET 1,000 MW commissioned in FY25**ACTUAL** 700 MW commissioned in FY26; 1,000 MW not fully commissioned**VARIANCE** **700 vs 1,000 MW****MISSED**

Q2FY25 · Q2FY25 transcript

Complete demerger process on or before 31 March 2025

TARGET Completed by 31 Mar 2025**ACTUAL** demerger completed, effective 1 May 2026**VARIANCE** **slipped ~5 qtrs****MISSED**

Q2FY25 · Q2FY25 presentation

FY25 FACOR ferrochrome production of 110-120 kt

TARGET 110-120 kt in FY25**ACTUAL** FY26 FACOR ferrochrome production reached 101 kt**VARIANCE** **101 vs 110-120 kt**

The Track Record — 109 Testable Promises / part 2 of 19

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MISSED

Q2FY25 · Q2FY25 presentation

FY25 Iron Ore Goa production of 2.5-3.0 Mnt

TARGET 2.5-3.0 Mnt in FY25

ACTUAL FY25 Iron Ore Goa production reached 1.6 Mnt

VARIANCE **1.6 vs 2.5-3 Mnt**

MISSED

Q2FY25 · Q2FY25 presentation

FY25 Iron Ore Karnataka production of 5.5-6.0 Mnt

TARGET 5.5-6.0 Mnt in FY25

ACTUAL FY25 Karnataka iron ore production reached 5.0 Mnt

VARIANCE **5 vs 5.5-6 Mnt**

MISSED

Q2FY25 · Q2FY25 presentation

FY25 Oil & Gas average gross operated production of 110-120 kboepd

TARGET 110-120 kboepd in FY25

ACTUAL FY25 Oil & Gas gross operated production reached 103.2 kboepd

VARIANCE **103.2 vs 110-120 kboepd**

MISSED

Q2FY25 · Q2FY25 presentation

FY25 Zinc India silver production of 750-775 tonnes

TARGET 750-775 t in FY25

ACTUAL FY25 Zinc India silver production reached 687 tonnes

VARIANCE **687 vs 750-775 tonnes**

Why: change in mining sequence and lower silver input from Sindesar Khurd mine

Execution

MISSED

Q2FY25 · Q2FY25 presentation

FY25 Zinc International BMM production of 50-60 kt

TARGET 50-60 kt in FY25

ACTUAL FY26 Zinc International BMM production reached 40 kt

VARIANCE **40 vs 50-60 kt**

MISSED

Q2FY25 · Q2FY25 transcript

Operationalize Ghogarpalli coal block by Q4 FY '26

TARGET Operational by Q4FY26

ACTUAL re-set to 2HFY27

VARIANCE **2 vs 4**

Why: EC recommended in April; targeting FC in current quarter

Capacity delay

The Track Record — 109 Testable Promises / part 3 of 19

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MISSED

Q2FY25 · Q2FY25 transcript

Achieve 11 Mtpa iron ore production in FY '25

TARGET 11 Mt iron ore in FY25

ACTUAL Iron ore production reached 10.1 Mt in FY25

VARIANCE **10.1 vs 11 Mt**

MISSED

Q3FY25 · Q3FY25 transcript

First coal from Ghogarpalli Mine in Q4FY26

TARGET First coal from Ghogarpalli by Q4FY26

ACTUAL re-set to 2H FY27

VARIANCE **2 vs 4**

MISSED

Q3FY25 · Q3FY25 presentation

Commission Train 2 of 1.5 MTPA Lanjigarh expansion in Q4FY25

TARGET 1.5 MTPA Train 2 commissioned in Q4FY25

ACTUAL First alumina output from Train 2 in Q2FY26

VARIANCE **-2 vs 1.5 Mtpa**

MISSED

Q3FY25 · Q3FY25 transcript

Operate Meenakshi and Athena power plants at full capacity in FY26

TARGET 5 GW merchant power capacity by FY26

ACTUAL commissioned 1.6 GW at Athena & Meenakshi by Q3FY26

VARIANCE **1.6 vs 5 GW**

MISSED

Q3FY25 · Q3FY25 transcript

Start Sijimali Mine in Q2FY26

TARGET Sijimali Mine start by Q2FY26

ACTUAL re-set to 1H FY27

VARIANCE **1 vs 2**

MISSED

Q3FY25 · Q3FY25 presentation

Zinc India CoP to remain 4-year low in FY25

TARGET Zinc India FY25 CoP 4-year low

ACTUAL Zinc India Q4FY26 CoP reached 4-year low of \$903/t

VARIANCE **903 vs 25**

The Track Record — 109 Testable Promises / part 4 of 19

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MISSED

Q4FY25 · Q4FY25 transcript

Commission Athena Unit-2 (600MW) in Q4FY26

TARGET 600MW by Q4FY26

ACTUAL Athena Unit-2 not commissioned by Q4FY26; 200MW PPA started Feb'26

VARIANCE 5 vs 600 MW

MISSED

Q4FY25 · Q4FY25 transcript

Deleverage Vedanta Resources by \$600mn in FY26

TARGET \$600mn deleveraging in FY26

ACTUAL Deleveraged \$700mn in FY26

VARIANCE 700 vs 600 USD_mn

MISSED

Q4FY25 · Q4FY25 transcript

Complete demerger by September 2025

TARGET Demerger by Sep 2025

ACTUAL Demerger completed before Q4FY26 earnings call

VARIANCE slipped ~2 qtrs

MISSED

Q4FY25 · Q4FY25 transcript

Start Kuraloi coal mine production by Q3FY26

TARGET Kuraloi mine start by Q3FY26

ACTUAL mining lease received; production start re-set to 1HFY27

VARIANCE slipped ~3 qtrs

MISSED

Q4FY25 · Q4FY25 transcript

Full ramp-up of Sijimali bauxite mine by Q4FY26

TARGET Full ramp-up by Q4FY26

ACTUAL re-set to 1HFY27

VARIANCE slipped ~2 qtrs

MISSED

Q4FY25 · Q4FY25 transcript

Start Sijimali bauxite mine production by Q2FY26

TARGET Sijimali mine start by Q2FY26

ACTUAL re-set to 1HFY27

VARIANCE slipped ~4 qtrs

The Track Record — 109 Testable Promises / part 5 of 19

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MISSED

Q2FY26 · Q2FY26 presentation

Iron Ore Goa production guidance of 2.2-2.7 Mnt in FY26

TARGET 2.2-2.7 Mnt Goa iron ore in FY26
ACTUAL FY26 Goa iron ore production reached 1.6 Mnt
VARIANCE **1.6 vs 2.2-2.7 Mnt**

MISSED

Q2FY26 · Q2FY26 presentation

Iron Ore Karnataka production guidance of 5.5-6.1 Mnt in FY26

TARGET 5.5-6.1 Mnt Karnataka iron ore in FY26
ACTUAL FY26 Karnataka iron ore production reached 5.0 Mnt
VARIANCE **5 vs 5.5-6.1 Mnt**

MISSED

Q4FY25 · Q4FY25 presentation

FY26 Oil & Gas average gross volume guidance of 95-100 kboepd

TARGET 95-100 kboepd
ACTUAL FY26 Oil & Gas gross volume averaged 87.2 kboepd
VARIANCE **87.2 vs 95-100 kboepd**

Why: natural decline **Supply chain**

MISSED

Q4FY25 · Q4FY25 presentation

FY26 Pig Iron production guidance of 950-1,050 kt

TARGET 950-1,050 kt
ACTUAL FY26 Pig Iron production reached 895 kt
VARIANCE **895 vs 950-1,050 kt**

MISSED

Q4FY25 · Q4FY25 presentation

FY26 Zinc India silver production guidance of 700-710 tonnes

TARGET 700-710 t
ACTUAL FY26 Zinc India silver production reached 627 tonnes
VARIANCE **627 vs 700-710 t**

MISSED

Q2FY26 · Q2FY26 presentation

Zinc International BMM MIC production guidance of 55-65 kt in FY26

TARGET 55-65 kt BMM MIC in FY26
ACTUAL FY26 BMM MIC production reached 40 kt
VARIANCE **40 vs 55-65 kt**

The Track Record — 109 Testable Promises / part 6 of 19

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MISSED

Q4FY25 · Q4FY25 transcript

OALP/DSP contribution to Oil & Gas production to reach 8-10% by Q4FY26

TARGET 8-10% share by Q4FY26
ACTUAL OALP/DSP share of gross operated production reached 3.8% in FY26
VARIANCE **3.8 vs 8-10 %**

MISSED

Q1FY26 · Q1FY26 presentation

Alumina capacity expansion to 5 MTPA by FY26 and 6 MTPA by FY28

TARGET 5 MTPA by FY26, 6 MTPA by FY28
ACTUAL Lanjigarh refinery alumina capacity exit run rate reached 4 MTPA by FY26
VARIANCE **4 vs 5-6 MTPA**

MISSED

Q1FY26 · Q1FY26 transcript

Complete Gamsberg Phase-2 project in H2FY26 (525 Ktpa mine capacity)

TARGET 525 Ktpa
ACTUAL Gamsberg Phase-2 94% complete; re-set to 1HFY27
VARIANCE **94 vs 525 Ktpa**

Why: Waste stripping at open pit took longer to catch up **Capacity delay**

MISSED

Q1FY26 · Q1FY26 transcript

Commission Lanjigarh Train II and Balco smelter (435 Ktpa) in Q2FY26

TARGET 435 Ktpa
ACTUAL First alumina from Lanjigarh Train II; first metal from Balco smelter commissioned
VARIANCE **3 vs 435 Ktpa**

MISSED

Q1FY26 · Q1FY26 transcript

Add 1.3 GW power capacity in Q2FY26

TARGET 1.3 GW
ACTUAL commissioned 700 MW in Q2FY26
VARIANCE **700 vs 1,300 MW**

MISSED

Q1FY26 · Q1FY26 transcript

Mechanical completion of Gamsberg Phase-2 by Dec 2025

TARGET Dec 2025
ACTUAL mechanical completion not achieved; ramp-up re-set to Q2FY27
VARIANCE **slipped ~3 qtrs**

The Track Record — 109 Testable Promises / part 7 of 19

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MISSED

Q1FY26 · Q1FY26 transcript

Start production at Sijimali bauxite mine by Q4FY26

TARGET Q4FY26
ACTUAL re-set to 1H FY27
VARIANCE **slipped ~2 qtrs**

MISSED

Q2FY26 · Q2FY26 transcript

Commission Gamsberg Phase-II expansion (220 Ktpa) by end-FY26

TARGET 220 Ktpa by FY26-end
ACTUAL Gamsberg Phase-II re-set to Q2FY27
VARIANCE **2 vs 220 Ktpa**

MISSED

Q2FY26 · Q2FY26 transcript

Reduce aluminium hot metal cost to below \$1,650 per ton in H2 FY26

TARGET H2FY26 aluminium CoP < \$1,650/t
ACTUAL FY26 yearly hot metal cost reached \$1,752/t
VARIANCE **1,752 vs 1,650 USD_per_t**

MISSED

Q2FY26 · Q2FY26 transcript

Commission Kuraloi mine in Q4 FY26

TARGET Kuraloi commissioned by Q4FY26
ACTUAL re-set to 1H FY27
VARIANCE **slipped ~2 qtrs**

MISSED

Q2FY26 · Q2FY26 presentation

Zinc India silver production guidance of 670-690 tonnes in FY26

TARGET 670-690 t silver in FY26
ACTUAL FY26 Zinc India silver production reached 627 tonnes
VARIANCE **627 vs 670-690 tonnes**

MISSED

Q3FY26 · Q3FY26 presentation

Commission BALCO smelter expansion (435 KTPA) by Q4FY26

TARGET 435 KTPA by Q4FY26
ACTUAL commissioning initiated; 70 pots by Q4FY26; full 435 KTPA ramp to Q4FY27
VARIANCE **70 vs 435 KTPA**

Why: delay through partner substitution and resource augmentation **Capacity delay**

The Track Record — 109 Testable Promises / part 8 of 19

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MISSED

Q3FY26 · Q3FY26 presentation

Ramp up Gamsberg Phase 2 to 200 KTPA MIC by 1HFY27

TARGET 200 KTPA MIC by 1HFY27

ACTUAL re-set to Q2FY27

VARIANCE **2 vs 200 KTPA**

Why: waste stripping catch-up delayed open-pit schedule

Capacity delay

MISSED

Q3FY26 · Q3FY26 presentation

Commission Kuraloi coal mine by Q4FY26

TARGET Commissioned by Q4FY26

ACTUAL re-set to 1HFY27

VARIANCE **1 vs 4**

Why: mining lease received a week back; mining operations to start in a month

Capacity delay

MISSED

Q3FY26 · Q3FY26 presentation

Expand Lanjigarh refinery to 5 MTPA by 1HFY27

TARGET 5 MTPA by 1HFY27

ACTUAL Lanjigarh refinery exit run rate reached 4 MTPA by end FY26

VARIANCE **4 vs 5 MTPA**

Why: Calciners and boiler running at 75-80% capacity; rated capacity expected Q1FY27

Capacity delay

MISSED

Q3FY26 · Q3FY26 presentation

Commission hot acid leaching plant by Q4FY26

TARGET Commissioned by Q4FY26

ACTUAL re-set to 1HFY27

VARIANCE **1 vs 4**

Capacity delay

PARTIAL

Q2FY25 · Q2FY25 presentation

FY25 aluminium cost of production \$1,625-1,725/t

TARGET \$1,625-1,725/t in FY25

ACTUAL FY26 lowest yearly hot metal cost at 1,752 \$/t

VARIANCE **1,752 vs 1,625-1,725 USD/t**

PARTIAL

Q2FY25 · Q2FY25 presentation

FY25 Oil & Gas opex of \$14-15/boe

TARGET \$14-15/boe in FY25

ACTUAL FY25 Oil & Gas opex reported at \$15.5/boe

VARIANCE **15.5 vs 14-15 USD/boe**

The Track Record — 109 Testable Promises / part 9 of 19

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

PARTIAL

Q2FY25 · Q2FY25 transcript

Reduce VRL debt to ~\$4.5 billion by early Q1 FY26

TARGET	VRL debt ~\$4.5 bn by early Q1FY26
ACTUAL	VRL debt stood at \$4.7 billion at FY26 end
VARIANCE	4.7 vs 4.5 USD_bn

PARTIAL

Q2FY25 · Q2FY25 transcript

Reduce VRL debt to \$4.6 billion by FY25-end

TARGET	VRL debt ≤ \$4.6 bn by FY25-end
ACTUAL	VRL debt stood at \$4.7 bn by FY26-end
VARIANCE	4.7 vs 4.6 USD_bn

PARTIAL

Q2FY25 · Q2FY25 presentation

FY25 Zinc India finished metal production of 1,075-1,100 kt

TARGET	1,075-1,100 kt in FY25
ACTUAL	FY26 Zinc India finished metal production reached 1,048 kt
VARIANCE	1,048 vs 1,075-1,100 kt

PARTIAL

Q3FY25 · Q3FY25 transcript

FY25 capex of ₹15,000-16,000 crore

TARGET	₹15,000-16,000 crore capex in FY25
ACTUAL	FY25 growth capex reached ₹14,918 crore
VARIANCE	14,918 vs 15,000-16,000 INR_cr

PARTIAL

Q4FY25 · Q4FY25 transcript

Invest \$300mn in KCM in FY26

TARGET	\$300mn capex in FY26
ACTUAL	\$290 million invested in KCM in FY26
VARIANCE	290 vs 300 USD_mn

PARTIAL

Q4FY25 · Q4FY25 presentation

FY26 Zinc India finished metal production guidance of 1,090-1,100 kt

TARGET	1,090-1,100 kt
ACTUAL	FY26 Zinc India finished metal production reached 1,048 kt
VARIANCE	1,048 vs 1,090-1,100 kt

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

PARTIAL

Q4FY25 · Q4FY25 presentation

FY26 Zinc India mined metal production guidance of 1,115-1,135 kt

TARGET 1,115-1,135 kt

ACTUAL FY26 Zinc India mined metal production reached 1,114 kt

VARIANCE 1,114 vs 1,115-1,135 kt

PARTIAL

Q1FY26 · Q1FY26 transcript

Aluminium hot metal cost of \$1,700-1,750/t for FY26

TARGET \$1,700-1,750/t

ACTUAL FY26 aluminium hot metal cost reached 1,752 \$/t

VARIANCE 1,752 vs 1,700-1,750 USD/t

PARTIAL

Q2FY26 · Q2FY26 presentation

Aluminium CoP guidance of \$1,700-1,750/t in FY26

TARGET \$1,700-1,750/t CoP in FY26

ACTUAL FY26 aluminium CoP reached 1,752 \$/t

VARIANCE 1,752 vs 1,700-1,750 USD_per_t

MET

Q3FY25 · Q3FY25 transcript

Commission 160,000 tpa roaster at Debari in Q4FY25

TARGET 160,000 tpa roaster commissioned by Q4FY25

ACTUAL Debari roaster re-set to 1HFY26

VARIANCE 1,60,000 vs 160 ktpa

MET

Q2FY25 · Q2FY25 presentation

Commission Train 2 of 1.5 MTPA Lanjigarh refinery expansion in Q3FY25

TARGET 1.5 MTPA by Q3FY25

ACTUAL Train 2 commissioned in Q2FY26 with first alumina output

VARIANCE 1.5 vs 1.5 Mtpa

MET

Q2FY25 · Q2FY25 presentation

FY25 Zinc India cost of production \$1,050-1,100/t

TARGET \$1,050-1,100/t in FY25

ACTUAL FY25 Zinc India CoP reached \$903/t

VARIANCE 903 vs 1,050-1,100 USD/t

The Track Record — 109 Testable Promises / part 11 of 19

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MET

Q2FY25 · Q2FY25 presentation

FY25 Zinc International cost of production \$1,300-1,400/t

TARGET \$1,300-1,400/t in FY25

ACTUAL FY25 Zinc International CoP reported at \$1,350/t

VARIANCE **1,350 vs 1,300-1,400 USD/t**

MET

Q2FY25 · Q2FY25 transcript

Reduce Vedanta Limited net debt/EBITDA to <1x

TARGET Net debt/EBITDA <1x

ACTUAL Vedanta Limited net debt/EBITDA reached 0.95x in Q4FY26

VARIANCE **0.95 vs 1 x**

MET

Q2FY25 · Q2FY25 transcript

Deleverage VRL by \$3 billion over three years starting FY25

TARGET \$3 bn deleveraging over 3 years from FY25

ACTUAL Deleveraged \$1 bn of the \$3 bn target by Mar'25

VARIANCE **1 vs 3 USD_bn**

MET

Q2FY25 · Q2FY25 presentation

FY25 alumina production of 2.3-2.4 Mnt

TARGET 2.3-2.4 Mnt in FY25

ACTUAL FY26 alumina production reached 2.916 Mnt

VARIANCE **2,916 vs 2.3-2.4 Mnt**

MET

Q2FY25 · Q2FY25 presentation

FY25 aluminium production of 2.3-2.4 Mnt

TARGET 2.3-2.4 Mnt in FY25

ACTUAL FY26 aluminium production reached 2.456 Mnt

VARIANCE **2,456 vs 2.3-2.4 Mnt**

MET

Q2FY25 · Q2FY25 presentation

FY25 ESL Steel hot metal production of 1.5-1.6 Mnt

TARGET 1.5-1.6 Mnt in FY25

ACTUAL FY25 ESL Steel hot metal production reached 1.5-1.6 Mnt

VARIANCE **1.6 vs 1.5-1.6 Mnt**

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MET

Q2FY25 · Q2FY25 presentation

FY25 Iron Ore WCL production of 1.3-1.7 Mnt

TARGET 1.3-1.7 Mnt in FY25

ACTUAL FY25 Iron Ore WCL production reached 1.7 Mnt

VARIANCE **1.7 vs 1.3-1.7 Mnt**

MET

Q2FY25 · Q2FY25 presentation

FY25 Zinc India mined metal production of 1,100-1,125 kt

TARGET 1,100-1,125 kt in FY25

ACTUAL FY25 Zinc India mined metal production reached 1,114 kt

VARIANCE **1,114 vs 1,100-1,125 kt**

MET

Q3FY25 · Q3FY25 transcript

Zinc International production of 160-180 kt in FY25 and 240-250 kt in FY26

TARGET 160-180 kt in FY25, 240-250 kt in FY26

ACTUAL Zinc International production reached 176 kt in 9MFY26

VARIANCE **176 vs 160-180 kt**

MET

Q2FY25 · Q2FY25 transcript

Ramp KCM copper production to 150 Ktpa run rate by FY25-end

TARGET 150 Ktpa run rate by FY25-end

ACTUAL KCM copper run rate reached 160-175 Ktpa by Q3FY25-end

VARIANCE **175 vs 150 Ktpa**

MET

Q2FY25 · Q2FY25 transcript

Start Sijimali bauxite mine by Q1 FY '26

TARGET Started by Q1FY26

ACTUAL re-set to 1HFY27

VARIANCE **1 vs 1**

MET

Q2FY25 · Q2FY25 transcript

Achieve 230,000 tons of MIC production in Zinc International for FY25

TARGET 230 Kt MIC in FY25

ACTUAL Zinc International MIC production reached 177 kt in FY25

VARIANCE **1,77,000 vs 230 Kt**

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MET

Q3FY25 · Q3FY25 transcript

Commission next phase of 250,000 tpa smelter by FY27/FY28

TARGET 250 ktpa smelter commissioned by FY27/FY28

ACTUAL BALCO smelter expansion commissioning initiated, not 250 ktpa milestone

VARIANCE **435 vs 250 ktpa**

MET

Q3FY25 · Q3FY25 transcript

Commission BALCO smelter expansion in Q1FY26

TARGET BALCO smelter expansion commissioned by Q1FY26

ACTUAL commissioning initiated for BALCO smelter expansion

VARIANCE **435 vs 1**

MET

Q3FY25 · Q3FY25 transcript

Commission 510,000 tpa fertilizer plant in Q4FY26

TARGET 510,000 tpa fertilizer plant commissioned by Q4FY26

ACTUAL re-set to 1HFY27

VARIANCE **510 vs 510 ktpa**

MET

Q3FY25 · Q3FY25 transcript

Commission Zinc International Phase-2 expansion in FY26

TARGET Zinc International Phase-2 commissioned by FY26

ACTUAL re-set to 1HFY27

VARIANCE **1 vs -2**

MET

Q3FY25 · Q3FY25 transcript

Deliver highest ever yearly EBITDA in FY25

TARGET highest ever yearly EBITDA in FY25

ACTUAL FY25 EBITDA reported as second highest ever at Rs. 43,541 crore

VARIANCE **43,541 vs 25**

MET

Q3FY25 · Q3FY25 transcript

Bring net debt-to-EBITDA ratio below 1x

TARGET Net debt/EBITDA below 1x

ACTUAL Net debt/EBITDA ratio reached 0.95x at FY26 year-end

VARIANCE **0.95 vs 1 x**

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MET

Q3FY25 · Q3FY25 presentation

Maintain net-debt/EBITDA at 1.4x

TARGET Net debt/EBITDA ~1.4x

ACTUAL Net debt/EBITDA reached 0.95x in Q4FY26

VARIANCE 0.95 vs 1.4 x

MET

Q3FY25 · Q3FY25 transcript

Vedanta Resources debt servicing of \$1.4bn in FY26 and \$1.1bn in FY27

TARGET \$1.4bn in FY26, \$1.1bn in FY27

ACTUAL VRL FY26 debt servicing reported as \$1.1bn principal + interest

VARIANCE 1.1 vs 1,400 USD_m

MET

Q3FY25 · Q3FY25 transcript

Aluminium hot metal volume exit FY25 above 2.4 Mt

TARGET >2.4 Mt hot metal by FY25-end

ACTUAL Annual aluminium production reached 2,422 kt in FY25

VARIANCE 2,422 vs 2.4 Mt

MET

Q4FY25 · Q4FY25 transcript

Commission Athena Unit-1 (600MW) in Q1FY26

TARGET 600MW by Q1FY26

ACTUAL Athena Unit-1 600MW commissioned by 2QFY26

VARIANCE 600 vs 600 MW

MET

Q4FY25 · Q4FY25 transcript

First metal from BALCO smelter expansion by Q1FY26-end

TARGET First metal by Q1FY26-end

ACTUAL First metal commissioned at BALCO smelter expansion

VARIANCE 525 vs 1

MET

Q4FY25 · Q4FY25 transcript

Lanjigarh Refinery alumina exit run rate of 4mn tons by FY26-end

TARGET 4 Mt exit run rate by FY26-end

ACTUAL Lanjigarh refinery alumina exit run rate reached 4 Mt by FY26-end

VARIANCE 4 vs 4 Mt

The Track Record — 109 Testable Promises / part 15 of 19

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MET

Q4FY25 · Q4FY25 transcript

Lanjigarh Refinery alumina production of 3.1mn tons in FY26

TARGET 3.1 Mt alumina in FY26

ACTUAL Lanjigarh refinery alumina production reached 2.916 Mt in FY26

VARIANCE 2,916 vs 3.1 Mt

MET

Q4FY25 · Q4FY25 transcript

Commission 700MW Meenakshi power plant in H1FY26

TARGET 700MW by H1FY26

ACTUAL Meenakshi 700MW commissioned in H1FY26

VARIANCE 700 vs 700 MW

MET

Q4FY25 · Q4FY25 transcript

FY26 capex guidance of \$1.5-1.7bn

TARGET \$1.5-1.7bn capex in FY26

ACTUAL Invested ₹14,918 cr. In Growth Capex

VARIANCE 14,918 vs 1.5-1.7 USD_bn

MET

Q1FY26 · Q1FY26 transcript

Oil & gas OPEX of \$15-16/barrel for FY26

TARGET \$15-16/bbl

ACTUAL FY26 oil & gas OPEX reached \$15.5/boe

VARIANCE 15.5 vs 15-16 USD/bbl

MET

Q4FY25 · Q4FY25 presentation

FY26 Zinc India cost of production (ex-royalty) guidance of \$1,025-1,050/t

TARGET \$1,025-1,050/t

ACTUAL FY26 Zinc India CoP (ex-royalty) reported at \$975-1,000/t

VARIANCE 987.5 vs 1,025-1,050 USD/t

MET

Q4FY25 · Q4FY25 presentation

FY26 Zinc International cost of production guidance of \$1,250-1,350/t

TARGET \$1,250-1,350/t

ACTUAL FY26 Zinc International CoP reached \$1,350/t

VARIANCE 1,350 vs 1,250-1,350 USD/t

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MET

Q4FY25 · Q4FY25 presentation

FY26 aluminium hot metal cost of production (ex-alumina) guidance of \$1,700-1,750/t

TARGET \$1,700-1,750/t

ACTUAL FY26 aluminium hot metal cost of production reached 1,752 \$/t

VARIANCE **1,752 vs 1,700-1,750 USD/t**

MET

Q4FY25 · Q4FY25 presentation

FY26 alumina production guidance of 3.0-3.1 million tonnes

TARGET 3.0-3.1 Mt

ACTUAL FY26 alumina production at Lanjigarh refinery reached 2.916 Mt

VARIANCE **2,916 vs 3-3.1 Mt**

MET

Q4FY25 · Q4FY25 presentation

FY26 aluminium production guidance of 2.5-2.6 million tonnes

TARGET 2.5-2.6 Mt

ACTUAL FY26 aluminium production reached 2.456 Mt

VARIANCE **2,456 vs 2.5-2.6 Mt**

MET

Q4FY25 · Q4FY25 presentation

FY26 ESL hot metal production guidance of 1.5-1.6 Mt

TARGET 1.5-1.6 Mt

ACTUAL FY26 ESL hot metal production guidance reaffirmed at 1.5-1.6 Mt

VARIANCE **1.6 vs 1.5-1.6 Mt**

MET

Q4FY25 · Q4FY25 presentation

FY26 FACOR ferrochrome production guidance of 100-110 kt

TARGET 100-110 kt

ACTUAL FY26 FACOR ferrochrome production reached 101 kt

VARIANCE **101 vs 100-110 kt**

MET

Q2FY26 · Q2FY26 presentation

Iron Ore Orissa production guidance of 4.5-5.2 Mnt in FY26

TARGET 4.5-5.2 Mnt Orissa iron ore in FY26

ACTUAL FY26 Orissa iron ore production reached 4.7 Mnt

VARIANCE **4.7 vs 4.5-5.2 Mnt**

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MET

Q2FY26 · Q2FY26 presentation

Zinc International Gamsberg MIC production guidance of 180-200 kt in FY26

TARGET 180-200 kt Gamsberg MIC in FY26

ACTUAL FY26 Gamsberg MIC production reached 185 kt

VARIANCE **185 vs 180-200 kt**

MET

Q4FY25 · Q4FY25 transcript

Zinc International production guidance of 235-265k tons in FY26

TARGET 235-265 kt in FY26

ACTUAL Zinc International production reached 176 kt in 9MFY26

VARIANCE **1,76,000 vs 235-265 kt**

MET

Q1FY26 · Q1FY26 transcript

Commission 160 Ktpa roaster at Debari in Q2FY26

TARGET 160 Ktpa

ACTUAL Debari roaster commissioned in 1HFY26

VARIANCE **160 vs 160 Ktpa**

MET

Q1FY26 · Q1FY26 presentation

Merchant power capacity to 4.78 GW by FY26

TARGET 4.78 GW by FY26

ACTUAL Merchant power capacity reached 4,934 MW by FY26

VARIANCE **4.93 vs 4.78 GW**

MET

Q1FY26 · Q1FY26 transcript

Net debt/EBITDA of 1x by FY26-end

TARGET 1x

ACTUAL FY26-end net debt/EBITDA reached 0.95x

VARIANCE **0.95 vs 1 x**

MET

Q1FY26 · Q1FY26 transcript

3 Mtpa alumina production in FY26

TARGET >3 Mtpa

ACTUAL FY26 alumina production reached 2.916 Mtpa

VARIANCE **2,916 vs 3 Mtpa**

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MET

Q1FY26 · Q1FY26 transcript

1.2 Mtpa refined zinc metal production in FY26

TARGET >1.2 Mtpa
ACTUAL FY26 refined zinc metal production reached 1,048 kt
VARIANCE **10,48,000 vs 1.2 Mtpa**

MET

Q2FY26 · Q2FY26 presentation

Net debt/EBITDA ratio of ~1.37x by end-Q2FY26

TARGET 1.37x by Q2FY26-end
ACTUAL Net debt/EBITDA ratio reached 0.95x at FY26-end
VARIANCE **0.95 vs 1.37 x**

MET

Q2FY26 · Q2FY26 presentation

Alumina production guidance of 3.0-3.1 Mnt in FY26

TARGET 3.0-3.1 Mnt alumina in FY26
ACTUAL FY26 alumina production reached 2.916 Mnt
VARIANCE **2,916 vs 3-3.1 Mnt**

MET

Q2FY26 · Q2FY26 presentation

Aluminium production guidance of 2.5-2.6 Mnt in FY26

TARGET 2.5-2.6 Mnt aluminium in FY26
ACTUAL FY26 aluminium production reached 2,456 kt
VARIANCE **24,56,000 vs 2.5-2.6 Mnt**

MET

Q3FY26 · Q3FY26 presentation

Complete 21 KTPA cell-house debottlenecking by 2HFY26

TARGET 21 KTPA by 2HFY26
ACTUAL 21 KTPA Cell House Debottlenecking at Chanderiya completed in 2HFY26
VARIANCE **21 vs 21 KTPA**

MET

Q3FY26 · Q3FY26 presentation

Complete 160 KTPA Debari roaster by 1HFY26

TARGET 160 KTPA by 1HFY26
ACTUAL Debari roaster 160 KTPA target re-stated for 1HFY26
VARIANCE **160 vs 160 KTPA**

03 The Track Record — 109 Testable Promises / part 19 of 19

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 99 promises are forward-dated and remain Not Yet Testable.

MET

Q3FY26 · Q3FY26 transcript

Close FY26 with net-debt/EBITDA of ~1x at Vedanta India

TARGET

~1x by FY26-end

ACTUAL

FY26 net-debt/EBITDA at Vedanta India reached 0.95x

VARIANCE

0.95 vs 1 x

Master Table — all 208 measurable commitments

Chronological · oldest first · colour = delivery status

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-11-01	Q2FY25	Q2FY25 transcript	Reach 3.1 Mtpa aluminium capacity with 90% value-added products by FY26	enable us to reach a production capacity of 3.1 million tons per annum of aluminum with 90% comprising value-added products and alloys	Aluminium capacity 3.1 Mtpa by FY26 · 3.1 Mtpa by FY26	2026-05-15	H	Aluminium capacity reached 2.456 Mtpa; 90% value-added products by FY26	MISSED	2.46 vs 3.1 Mtpa		
2024-11-01	Q2FY25	Q2FY25 transcript	Generate 5 GW of commercial power within 18-20 months	we are well positioned to generate 5 Gigawatts of commercial power within the next 18 to 20 months	Commercial power 5 GW in 18-20 months · 5 GW in 18-20 months		H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 transcript	Commission 0.5 Mt fertilizer plant in Q2 FY '26	quarter of this current fiscal and 2nd Quarter of the next fiscal	Fertilizer plant 0.5 Mt commissioned Q2FY26 · 0.5 Mt fertilizer plant commissioned Q2FY26	2025-11-14	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Complete Gamsberg Phase 2 by FY26	Project completion targeted in FY26	Gamsberg Phase 2 completed by FY26 · FY26 completion	2026-05-15	H	Gamsberg Phase 2 re-set to Q2FY27	MISSED	2 vs 26		
2024-11-01	Q2FY25	Q2FY25 transcript	Fully ramp up Lanjigarh Refinery Train 1 by December 2024	We expect to fully ramp-up Train 1 by December 2024	Lanjigarh Train 1 fully ramped by Dec 2024 · Fully ramped by Dec 2024	2024	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Commission Train 2 of 1.5 MTPA Lanjigarh refinery expansion in Q3FY25	On track to commission Train 2 of 1.5 MTPA of Lanjigarh Expansion project in	Lanjigarh Train 2 commissioned by Q3FY25 · 1.5 MTPA by Q3FY25	2025-02-14	H	Train 2 commissioned in Q2FY26 with first alumina output	MET	1.5 vs 1.5 Mtpa		
2024-11-01	Q2FY25	Q2FY25 transcript	Commission Lanjigarh Refinery Train 2 in Q3 FY '25 with full ramp-up by Q1 FY '26	We are also on track to commission Train 2 in Quarter 3 FY '25, with full ramp up expected by quarter 1 of FY '26	Lanjigarh Train 2 commissioned Q3FY25, ramped Q1FY26 · Commission Q3FY25, ramped Q1FY26	2025-02-14	H	Train 2 commissioned in Q2FY26	MISSED	1 vs 3		
2024-11-01	Q2FY25	Q2FY25 presentation	Complete 700 ktpa Magnetite Project by 4QFY25	700ktpa Magnetite Project on track – Target completion 4QFY25	Magnetite capacity 700 ktpa by 4QFY25 · 700 ktpa by 4QFY25	2025-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 transcript	Fully commission 1,000 MW Meenakshi Power Plant in FY25	this fiscal year will mark the full commissioning of Meenakshi Power Plant 1,000 Megawatts	Meenakshi Power Plant 1,000 MW commissioned FY25 · 1,000 MW commissioned in FY25	2025-05-15	H	700 MW commissioned in FY26; 1,000 MW not fully commissioned	MISSED	700 vs 1,000 MW		
2024-11-01	Q2FY25	Q2FY25 transcript	Board-approved project CAPEX of ₹5,209 crore for 1,200 MW Athena Power Plant	Our Board has also approved the project CAPEX of 5,209 crores for 1,200 Megawatts Athena Power Plant	Athena Power Plant CAPEX ₹5,209 crore - ₹5,209 crore CAPEX for 1,200 MW	2025-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 growth capex of \$1.7-1.9 billion	Capex guidance 0.7 1.1 2.0 1.7	FY25 growth capex \$1.7-1.9 bn · \$1.7-1.9 bn in FY25	2025-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	TSPL plant availability >85% in FY25	TSPL plant availability >85%	FY25 TSPL plant availability >85% · >85% in FY25	2025-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 aluminium cost of production \$1,625-1,725/t	CoP1 \$1,625/t - \$1,725/t	FY25 aluminium CoP \$1,625-1,725/t · \$1,625-1,725/t in FY25	2025-05-15	H	FY26 lowest yearly hot metal cost at 1,752 \$/t	PARTIAL	1,752 vs 1,625-1,725 USD/t		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 Oil & Gas opex of \$14-15/boe	Opex \$14-15/boe	FY25 Oil & Gas opex \$14-15/boe · \$14-15/boe in FY25	2025-05-15	H	FY25 Oil & Gas opex reported at \$15.5/boe	PARTIAL	15.5 vs 14-15 USD/boe		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 Zinc India cost of production \$1,050-1,100/t	CoP2 \$1,050/t - \$1,100/t	FY25 Zinc India CoP \$1,050-1,100/t · \$1,050-1,100/t in FY25	2025-05-15	H	FY25 Zinc India CoP reached \$903/t	MET	903 vs 1,050-1,100 USD/t		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 Zinc International cost of production \$1,300-1,400/t	CoP \$1,300/t - \$1,400/t	FY25 Zinc International CoP \$1,300-1,400/t · \$1,300-1,400/t in FY25	2025-05-15	H	FY25 Zinc International CoP reported at \$1,350/t	MET	1,350 vs 1,300-1,400 USD/t		
2024-11-01	Q2FY25	Q2FY25 transcript	Achieve highest-ever annual EBITDA in FY '25 with 60% in H2	We anticipate achieving our highest-ever annual EBITDA in FY '25 by delivering the remaining 60% in the	FY25 EBITDA H2 = 60% of annual · 60% of annual EBITDA in H2 FY25	2025-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-11-01	Q2FY25	Q2FY25 transcript	Reduce Vedanta Limited net debt/EBITDA to <1x	<i>at 1.49x, it is set to go down to less than 1x where EBITDA at</i>	Vedanta net debt/EBITDA <1x · Net debt/EBITDA <1x	medium term	H	Vedanta Limited net debt/EBITDA reached 0.95x in Q4FY26	MET	0.95 vs 1 x		
2024-11-01	Q2FY25	Q2FY25 transcript	Reduce VRL debt to ~\$4.5 billion by early Q1 FY26	<i>net net, overall by end of this fiscal or early Q1 next year, the cost of funding at Vedanta Resources will be single digit, debt</i>	VRL debt ~\$4.5 bn by early Q1FY26	2025-08-14	H	VRL debt stood at \$4.7 billion at FY26 end	PARTIAL	4.7 vs 4.5 USD_bn		
2024-11-01	Q2FY25	Q2FY25 transcript	Reduce VRL debt to ≤ \$3 billion by end of FY27	<i>at Vedanta Resources, our intent is to go down to 3 billion over 3 years starting the current</i>	VRL debt ≤ \$3 bn by FY27-end	2027-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 transcript	Reduce VRL debt to \$4.6 billion by FY25-end	<i>one may look at a number of more about 4.6 or so at VRL once the year is closed</i>	VRL debt ≤ \$4.6 bn by FY25-end	2025-05-15	H	VRL debt stood at \$4.7 bn by FY26-end	PARTIAL	4.7 vs 4.6 USD_bn		
2024-11-01	Q2FY25	Q2FY25 transcript	Deleverage VRL by \$3 billion over three years starting FY25	<i>we guided the market that the VRL debt, we further deleveraged \$3 billion over three years, starting this year first April</i>	VRL deleveraging \$3 bn over 3 years from FY25 · \$3 bn deleveraging over 3 years from FY25		H	Deleveraged \$1 bn of the \$3 bn target by Mar'25	MET	1 vs 3 USD_bn		
2024-11-01	Q2FY25	Q2FY25 transcript	Complete demerger process on or before 31 March 2025	<i>we are very confident that this will get done on or before 31st of March 2025</i>	Demerger completed by 31 Mar 2025 · Completed by 31 Mar 2025	2025	H	demerger completed, effective 1 May 2026	MISSED	slipped ~5 qtrs		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 alumina production of 2.3-2.4 Mnt	<i>Alumina 2.3-2.4 Mnt</i>	FY25 alumina production 2.3-2.4 Mnt · 2.3-2.4 Mnt in FY25	2025-05-15	H	FY26 alumina production reached 2.916 Mnt	MET	2,916 vs 2.3-2.4 Mnt		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 aluminium production of 2.3-2.4 Mnt	<i>Aluminium 2.3-2.4 Mnt</i>	FY25 aluminium production 2.3-2.4 Mnt · 2.3-2.4 Mnt in FY25	2025-05-15	H	FY26 aluminium production reached 2.456 Mnt	MET	2,456 vs 2.3-2.4 Mnt		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 ESL Steel hot metal production of 1.5-1.6 Mnt	<i>Hot Metal 1.5-1.6 Mnt</i>	FY25 ESL Steel hot metal 1.5-1.6 Mnt · 1.5-1.6 Mnt in FY25	2025-05-15	H	FY25 ESL Steel hot metal production reached 1.5-1.6 Mnt	MET	1.6 vs 1.5-1.6 Mnt		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 FACOR ferrochrome production of 110-120 kt	<i>Ferrochrome 110 - 120 kt</i>	FY25 FACOR ferrochrome 110-120 kt · 110-120 kt in FY25	2025-05-15	H	FY26 FACOR ferrochrome production reached 101 kt	MISSED	101 vs 110-120 kt		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 Iron Ore Goa production of 2.5-3.0 Mnt	<i>Goa 2.5 - 3.0 Mnt</i>	FY25 Iron Ore Goa 2.5-3.0 Mnt · 2.5-3.0 Mnt in FY25	2025-05-15	H	FY25 Iron Ore Goa production reached 1.6 Mnt	MISSED	1.6 vs 2.5-3 Mnt		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 Iron Ore Karnataka production of 5.5-6.0 Mnt	<i>Karnataka 5.5 - 6.0 Mnt</i>	FY25 Iron Ore Karnataka 5.5-6.0 Mnt · 5.5-6.0 Mnt in FY25	2025-05-15	H	FY25 Karnataka iron ore production reached 5.0 Mnt	MISSED	5 vs 5.5-6 Mnt		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 Iron Ore WCL production of 1.3-1.7 Mnt	<i>WCL 1.3 - 1.7 Mnt</i>	FY25 Iron Ore WCL 1.3-1.7 Mnt · 1.3-1.7 Mnt in FY25	2025-05-15	H	FY25 Iron Ore WCL production reached 1.7 Mnt	MET	1.7 vs 1.3-1.7 Mnt		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 Oil & Gas average gross operated production of 110-120 kboepd	<i>Average Gross Volume 110-120 kboepd</i>	FY25 Oil & Gas gross operated production 110-120 kboepd · 110-120 kboepd in FY25	2025-05-15	H	FY25 Oil & Gas gross operated production reached 103.2 kboepd	MISSED	103.2 vs 110-120 kboepd		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 Zinc India finished metal production of 1,075-1,100 kt	<i>Finished Metal 1,075 - 1,100 kt</i>	FY25 Zinc India finished metal 1,075-1,100 kt · 1,075-1,100 kt in FY25	2025-05-15	H	FY26 Zinc India finished metal production reached 1,048 kt	PARTIAL	1,048 vs 1,075-1,100 kt		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 Zinc India mined metal production of 1,100-1,125 kt	<i>Mined Metal 1,100 - 1,125 kt</i>	FY25 Zinc India mined metal 1,100-1,125 kt · 1,100-1,125 kt in FY25	2025-05-15	H	FY25 Zinc India mined metal production reached 1,114 kt	MET	1,114 vs 1,100-1,125 kt		
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 Zinc India silver production of 750-775 tonnes	<i>Silver 750 - 775 tonnes</i>	FY25 Zinc India silver 750-775 t · 750-775 t in FY25	2025-05-15	H	FY25 Zinc India silver production reached 687 tonnes	MISSED	687 vs 750-775 tonnes	change in mining sequence and lower silver input from Sindesar Khurd mine	Execution
2024-11-01	Q2FY25	Q2FY25 presentation	FY25 Zinc International BMM production of 50-60 kt	<i>BMM 50 - 60 kt</i>	FY25 Zinc International BMM 50-60 kt · 50-60 kt in FY25	2025-05-15	H	FY26 Zinc International BMM production reached 40 kt	MISSED	40 vs 50-60 kt		
2024-11-01	Q2FY25	Q2FY25 transcript	Operationalize Ghogarpalli coal block by Q4 FY '26	<i>we are targeting by 4th quarter of '26 it gets operationalized. We</i>	Ghogarpalli coal block operational Q4FY26 · Operational by Q4FY26	2026-05-15	H	re-set to 2HFY27	MISSED	2 vs 4	EC recommended in April; targeting FC in current quarter	Capacity delay

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-11-01	Q2FY25	Q2FY25 transcript	Achieve 11 Mtpa iron ore production in FY '25	<i>we are confident of achieving our annual production guidance of 11 million tons per annum from the iron ore business in FY '25</i>	Iron ore production 11 Mt in FY25 · 11 Mt iron ore in FY25	2025-05-15	H	Iron ore production reached 10.1 Mt in FY25	MISSED	10.1 vs 11 Mt		
2024-11-01	Q2FY25	Q2FY25 transcript	Ramp KCM copper production to 150 Ktpa run rate by FY25-end	<i>month, we should be at 9. We should be at a run rate of about 15 kilotons per month by the end of the financial</i>	KCM copper run rate 150 Ktpa by FY25-end · 150 Ktpa run rate by FY25-end	2025-05-15	H	KCM copper run rate reached 160-175 Ktpa by Q3FY25-end	MET	175 vs 150 Ktpa		
2024-11-01	Q2FY25	Q2FY25 transcript	Operationalize Kuraloi coal block by Q1 FY '26 and ramp up by Q3 FY '26	<i>Kuraloi coal block we are expecting first quarter of '26, it will get operationalized and which we are trying to ramp up by third quarter</i>	Kuraloi coal block operational Q1FY26, ramped Q3FY26 · Operational Q1FY26, ramped Q3FY26	2025-08-14	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 transcript	Operationalize Radhikapur coal block before Q1 FY '26	<i>expected that we are trying to operationalize before first quarter of</i>	Radhikapur coal block operational before Q1FY26 · Operational before Q1FY26	2025-08-14	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 transcript	Start Sijimali bauxite mine by Q1 FY '26	<i>and we expect that in quarter 1, next year, we should start the</i>	Sijimali mine started Q1FY26 · Started by Q1FY26	2025-08-14	H	re-set to 1HFY27	MET	1 vs 1		
2024-11-01	Q2FY25	Q2FY25 transcript	Achieve 230,000 tons of MIC production in Zinc International for FY25	<i>we are confident in achieving 230,000 tons of total MIC production for the full year in our Zinc International business</i>	Zinc International MIC 230 Kt in FY25 · 230 Kt MIC in FY25	2025-05-15	H	Zinc International MIC production reached 177 kt in FY25	MET	1,77,000 vs 230 Kt		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission next phase of 250,000 tpa smelter by FY27/FY28	<i>targeting to commission the next phase of 250,000 tons per annum of smelter by FY '27/'28</i>	250 ktpa smelter commissioned by FY27/FY28		H	BALCO smelter expansion commissioning initiated, not 250 ktpa milestone	MET	435 vs 250 ktpa		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission BALCO smelter expansion in Q1FY26	<i>BALCO smelter expansion is now in an advanced stage with commissioning targeted in Quarter 1 of FY '26</i>	BALCO smelter expansion commissioned by Q1FY26	2025-08-14	H	commissioning initiated for BALCO smelter expansion	MET	435 vs 1		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission 160,000 tpa roaster at Debari in Q4FY25	<i>final commissioning targeted for quarter 4 of the current fiscal and quarter 4 of the next fiscal</i>	Debari roaster commissioned by Q4FY25 · 160,000 tpa roaster commissioned by Q4FY25	2025-05-15	H	Debari roaster re-set to 1HFY26	MET	1,60,000 vs 160 ktpa		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission 510,000 tpa fertilizer plant in Q4FY26	<i>final commissioning targeted for quarter 4 of the current fiscal and quarter 4 of the next</i>	Fertilizer plant commissioned by Q4FY26 · 510,000 tpa fertilizer plant commissioned by Q4FY26	2026-05-15	H	re-set to 1HFY27	MET	510 vs 510 ktpa		
2025-02-01	Q3FY25	Q3FY25 transcript	First coal from Ghogarpalli Mine in Q4FY26	<i>original target of Ghogarpalli, quarter 4 of FY '26, they are going to take out the first coal</i>	Ghogarpalli first coal by Q4FY26 · First coal from Ghogarpalli by Q4FY26	2026-05-15	H	re-set to 2HFY27	MISSED	2 vs 4		
2025-02-01	Q3FY25	Q3FY25 presentation	Commission Train 2 of 1.5 MTPA Lanjigarh expansion in Q4FY25	<i>Commissioning of Train 2 of 1.5 MTPA of Lanjigarh Expansion project in Q4FY25</i>	Lanjigarh Train 2 1.5 MTPA by Q4FY25 · 1.5 MTPA Train 2 commissioned in Q4FY25	2025-05-15	H	First alumina output from Train 2 in Q2FY26	MISSED	-2 vs 1.5 Mtpa		
2025-02-01	Q3FY25	Q3FY25 transcript	Operate Meenakshi and Athena power plants at full capacity in FY26	<i>Meenakshi and Athena Power Plants are scheduled to be operating at full capacity in FY '26</i>	Meenakshi & Athena at full capacity by FY26 · 5 GW merchant power capacity by FY26	2026-05-15	H	commissioned 1.6 GW at Athena & Meenakshi by Q3FY26	MISSED	1.6 vs 5 GW		
2025-02-01	Q3FY25	Q3FY25 transcript	Start Sijimali Mine in Q2FY26	<i>in the quarter 2, we are going to start the Sijimali Mine</i>	Sijimali Mine start by Q2FY26	2025-11-14	H	re-set to 1HFY27	MISSED	1 vs 2		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission Zinc International Phase-2 expansion in FY26	<i>Phase-2 expansion project is in full swing with commissioning targeted in FY '26</i>	Zinc International Phase-2 commissioned by FY26	2026-05-15	H	re-set to 1HFY27	MET	1 vs -2		
2025-02-01	Q3FY25	Q3FY25 transcript	FY25 capex of ₹15,000-16,000 crore	<i>9 months is about 1.15 billion, and we will be in the ballpark of 1.5 to 1.6 billion in the current fiscal on CAPEX</i>	FY25 capex ₹15,000-16,000 crore · ₹15,000-16,000 crore capex in FY25	2025-05-15	H	FY25 growth capex reached ₹14,918 crore	PARTIAL	14,918 vs 15,000-16,000 INR_cr		
2025-02-01	Q3FY25	Q3FY25 transcript	Aluminium hot metal cost 15-20% lower in Q1FY26 vs Q3FY25	<i>the aluminum cost should be 15% to 20% lower than what we saw in Quarter 3</i>	Aluminium CoP 15-20% lower in Q1FY26 vs Q3FY25 · 15-20% lower CoP in Q1FY26	2025-08-14	H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	Alumina cost from Sijimali at \$260-270/t	<i>the alumina cost will be in the range of, say, 260 to 270 if we are using it from the Sijimali</i>	Sijimali alumina CoP \$260-270/t · \$260-270/t alumina CoP from Sijimali	medium term	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-02-01	Q3FY25	Q3FY25 presentation	Zinc India CoP to remain 4-year low in FY25	<i>On track for 4-year lowest full year CoP</i>	Zinc India FY25 CoP 4-year low	2025-05-15	M	Zinc India Q4FY26 CoP reached 4-year low of \$903/t	MISSED	903 vs 25		
2025-02-01	Q3FY25	Q3FY25 transcript	Zinc International cost of production in \$1,200-1,300/t range	<i>my expectation is that we should see the cost range between \$1,200 and \$1,300</i>	Zinc International CoP \$1,200-1,300/t · \$1,200-1,300/t CoP	medium term	H	Zinc International CoP reached \$1,350/t in Q4FY26	NYT	undated target — interim 1,350 USD/t		
2025-02-01	Q3FY25	Q3FY25 transcript	Deliver highest ever yearly EBITDA in FY25	<i>we are confident of delivering the highest ever yearly EBITDA in FY '25</i>	FY25 highest ever yearly EBITDA · highest ever yearly EBITDA in FY25	2025-05-15	M	FY25 EBITDA reported as second highest ever at Rs. 43,541 crore	MET	43,541 vs 25		
2025-02-01	Q3FY25	Q3FY25 transcript	Bring net debt-to-EBITDA ratio below 1x	<i>progressing towards our target of bringing this ratio below 1x</i>	Net debt/EBITDA < 1x · Net debt/EBITDA below 1x	medium term	H	Net debt/EBITDA ratio reached 0.95x at FY26 year-end	MET	0.95 vs 1 x		
2025-02-01	Q3FY25	Q3FY25 presentation	Maintain net-debt/EBITDA at 1.4x	<i>Net debt to EBITDA ratio improved to 1.4x vs 1.7x in Dec 2023</i>	Net debt/EBITDA 1.4x · Net debt/EBITDA ~1.4x		M	Net debt/EBITDA reached 0.95x in Q4FY26	MET	0.95 vs 1.4 x		
2025-02-01	Q3FY25	Q3FY25 transcript	Vedanta Resources debt servicing of \$1.4bn in FY26 and \$1.1bn in FY27	<i>The total repayment due next fiscal is about 900 million. So, 0.9 billion is the principal, 0.5 billion</i>	VRL debt servicing \$1.4bn in FY26, \$1.1bn in FY27 · \$1.4bn in FY26, \$1.1bn in FY27	2026-05-15	H	VRL FY26 debt servicing reported as \$1.1bn principal + interest	MET	1.1 vs 1,400 USD_m		
2025-02-01	Q3FY25	Q3FY25 presentation	Plant 7 million trees by 2030	<i>commitment to plant 7 million trees by 2030</i>	7 million trees planted by 2030 · 7 million trees by 2030	2030	L		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 presentation	Hold shareholders & creditors meeting for demerger in February 2025	<i>Meeting of shareholders & creditors scheduled in February</i>	Demerger meeting in Feb 2025 · Demerger meeting Feb 2025	2025	H		NYT	no outcome reported		
2025-02-01	Q3FY25	Q3FY25 transcript	Aluminium hot metal volume exit FY25 above 2.4 Mt	<i>on volume, we should be slightly above 2.4 million ton as we exit this year on the hot metal</i>	Aluminium hot metal >2.4 Mt by FY25-end · >2.4 Mt hot metal by FY25-end	2025-05-15	H	Annual aluminium production reached 2,422 kt in FY25	MET	2,422 vs 2.4 Mt		
2025-02-01	Q3FY25	Q3FY25 transcript	Zinc International production of 160-180 kt in FY25 and 240-250 kt in FY26	<i>production from ZI. So, we should do somewhere between 160 and 180 kilotons of production this year. And next</i>	Zinc International production 160-180 kt in FY25, 240-250 kt in FY26 · 160-180 kt in FY25, 240-250 kt in FY26	2025-05-15	H	Zinc International production reached 176 kt in 9MFY26	MET	176 vs 160-180 kt		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission Athena Unit-1 (600MW) in Q1FY26	<i>Athena Unit-1, 600 megawatts it's being scheduled for commissioning right now,</i>	Athena Unit-1 600MW commissioned by Q1FY26 · 600MW by Q1FY26	2025-08-14	H	Athena Unit-1 600MW commissioned by 2QFY26	MET	600 vs 600 MW		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission Athena Unit-2 (600MW) in Q4FY26	<i>the second unit is another 600 megawatts, that's being scheduled for commissioning in Quarter 4 of this financial year</i>	Athena Unit-2 600MW commissioned by Q4FY26 · 600MW by Q4FY26	2026-05-15	H	Athena Unit-2 not commissioned by Q4FY26; 200MW PPA started Feb'26	MISSED	5 vs 600 MW		
2025-04-01	Q4FY25	Q4FY25 transcript	First metal from BALCO smelter expansion by Q1FY26-end	<i>we are still maintaining the guidance of the first metal at end of the Quarter 1</i>	BALCO first metal by Q1FY26-end · First metal by Q1FY26-end	2025-08-14	H	First metal commissioned at BALCO smelter expansion	MET	525 vs 1		
2025-04-01	Q4FY25	Q4FY25 transcript	ESL hot metal capacity to 3.2mn tons by FY26-end	<i>total hot metal capacity to increase from 1.7 million tons to 3.2 million tons per annum by FY '26 end</i>	ESL hot metal capacity 3.2 Mtpa by FY26-end · 3.2 Mtpa by FY26-end	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Debottleneck ESL to 3.5mn tons by FY27	<i>plans to further debottlenecking to 3.5 million tons per annum in FY '27</i>	ESL hot metal capacity 3.5 Mtpa by FY27 · 3.5 Mtpa by FY27	2027-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Lanjigarh Refinery alumina exit run rate of 4mn tons by FY26-end	<i>at the end of this fiscal year, for us, we intend to be at an exit run rate of close to 4 million tons</i>	Lanjigarh alumina exit run rate 4 Mt by FY26-end · 4 Mt exit run rate by FY26-end	2026-05-15	H	Lanjigarh refinery alumina exit run rate reached 4 Mt by FY26-end	MET	4 vs 4 Mt		
2025-04-01	Q4FY25	Q4FY25 transcript	Lanjigarh Refinery alumina production of 3.1mn tons in FY26	<i>this year we are planning to have the production of 3.1 million tons of production from Lanjigarh</i>	Lanjigarh alumina production 3.1 Mt in FY26 · 3.1 Mt alumina in FY26	2026-05-15	H	Lanjigarh refinery alumina production reached 2.916 Mt in FY26	MET	2,916 vs 3.1 Mt		
2025-04-01	Q4FY25	Q4FY25 transcript	Lanjigarh Refinery alumina run rate of 5mn tons by FY27	<i>the 5 million tons by FY '27, we hope to be close to those numbers</i>	Lanjigarh alumina run rate 5 Mt by FY27 · 5 Mt run rate by FY27	2027-05-15	M		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission 700MW Meenakshi power plant in H1FY26	<i>The remaining 700-megawatt capacity is targeted for commissioning in the first half of this current fiscal</i>	Meenakshi 700MW commissioned by H1FY26 · 700MW by H1FY26		H	Meenakshi 700MW commissioned in H1FY26	MET	700 vs 700 MW		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-04-01	Q4FY25	Q4FY25 transcript	FY26 capex guidance of \$1.5-1.7bn	<i>in our guidance of about \$1.5 billion to \$1.7 billion</i>	FY26 capex \$1.5-1.7bn · \$1.5-1.7bn capex in FY26	2026-05-15	H	Invested ₹14,918 cr. In Growth Capex	MET	14,918 vs 1.5-1.7 USD_bn		
2025-04-01	Q4FY25	Q4FY25 transcript	Invest \$300mn in KCM in FY26	<i>track. And we will probably invest just over \$300 million for this financial</i>	KCM capex \$300mn in FY26 · \$300mn capex in FY26	2026-05-15	H	\$290 million invested in KCM in FY26	PARTIAL	290 vs 300 USD_mn		
2025-04-01	Q4FY25	Q4FY25 transcript	Complete remaining \$4bn of \$9.5bn capex program within next three years	<i>The remaining \$4 billion will be invested within the next three years</i>	Remaining capex \$4bn by FY28 · \$4bn capex by FY28	2028-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Zinc India cost of production (ex-royalty) guidance of \$1,025-1,050/t	<i>of tax - - -</i>	FY26 Zinc India CoP \$1,025-1,050/t · \$1,025-1,050/t	2026-05-15	H	FY26 Zinc India CoP (ex-royalty) reported at \$975-1,000/t	MET	987.5 vs 1,025-1,050 USD/t		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Zinc International cost of production guidance of \$1,250-1,350/t	<i>CoP \$1,250/t - \$1,350/t</i>	FY26 Zinc International CoP \$1,250-1,350/t · \$1,250-1,350/t	2026-05-15	H	FY26 Zinc International CoP reached \$1,350/t	MET	1,350 vs 1,250-1,350 USD/t		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 aluminium hot metal cost of production (ex-alumina) guidance of \$1,700-1,750/t	<i>of tax - - -</i>	FY26 Aluminium CoP \$1,700-1,750/t · \$1,700-1,750/t	2026-05-15	H	FY26 aluminium hot metal cost of production reached 1,752 \$/t	MET	1,752 vs 1,700-1,750 USD/t		
2025-04-01	Q4FY25	Q4FY25 presentation	Group deleveraging target of \$3bn by FY27	<i>VRL committed to deleverage by \$ 3bn in next three years</i>	Group deleveraging \$3bn by FY27 · \$3bn deleveraging by FY27	2027-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Deleverage Vedanta Resources by \$600mn in FY26	<i>we can deleverage Vedanta Resources by \$600 million in the current fiscal</i>	Vedanta Resources deleveraging \$600mn in FY26 · \$600mn deleveraging in FY26	2026-05-15	H	Deleveraged \$700mn in FY26	MISSED	700 vs 600 USD_mn		
2025-04-01	Q4FY25	Q4FY25 transcript	Athena power plant EBITDA of Rs 2/unit	<i>we are targeting roughly around Rs. 2 a unit in terms of the EBITDA level</i>	Athena EBITDA Rs 2/unit · Rs 2/unit EBITDA	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Complete demerger by September 2025	<i>We anticipate completing the demerger by September 2025</i>	Demerger completed by Sep 2025 · Demerger by Sep 2025	2025	H	Demerger completed before Q4FY26 earnings call	MISSED	slipped ~2 qtrs		
2025-04-01	Q4FY25	Q4FY25 transcript	Start Ghogharpalli coal mine production by Q4FY26	<i>for our Ghogharpalli coal mines, we are expected that we are going to commence the operation from last quarter of the FY '26</i>	Ghogharpalli coal mine start by Q4FY26 · Ghogharpalli mine start by Q4FY26	2026-05-15	H		NYT	no outcome reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Start Kuraloi coal mine production by Q3FY26	<i>which we have said, in the Quarter 3 FY '26, we are going to commence the</i>	Kuraloi coal mine start by Q3FY26 · Kuraloi mine start by Q3FY26	2026-02-14	H	mining lease received; production start re-set to 1HFY27	MISSED	slipped ~3 qtrs		
2025-04-01	Q4FY25	Q4FY25 transcript	Full ramp-up of Sijimali bauxite mine by Q4FY26	<i>full rampup by the 4th Quarter FY '26</i>	Sijimali mine full ramp-up by Q4FY26 · Full ramp-up by Q4FY26	2026-05-15	H	re-set to 1HFY27	MISSED	slipped ~2 qtrs		
2025-04-01	Q4FY25	Q4FY25 transcript	Start Sijimali bauxite mine production by Q2FY26	<i>we are going to commence the operation of Sijimali mines by Quarter 2 FY '26</i>	Sijimali mine start by Q2FY26	2025-11-14	H	re-set to 1HFY27	MISSED	slipped ~4 qtrs		
2025-04-01	Q4FY25	Q4FY25 transcript	Aluminium value-added product sales to reach 70% of total in FY26	<i>next year we expect it to be somewhere around 70% as we ramp up the VAP facilities</i>	Aluminium VAP sales 70% in FY26 · 70% VAP sales in FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 alumina production guidance of 3.0-3.1 million tonnes	<i>Alumina 3.0-3.1 Mnt</i>	FY26 Alumina production 3.0-3.1 Mt · 3.0-3.1 Mt	2026-05-15	H	FY26 alumina production at Lanjigarh refinery reached 2.916 Mt	MET	2,916 vs 3-3.1 Mt		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 aluminium production guidance of 2.5-2.6 million tonnes	<i>Alumina 3.0-3.1 Mnt Aluminium1 2.5-2.6 Mnt</i>	FY26 Aluminium production 2.5-2.6 Mt · 2.5-2.6 Mt	2026-05-15	H	FY26 aluminium production reached 2.456 Mt	MET	2,456 vs 2.5-2.6 Mt		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 ESL hot metal production guidance of 1.5-1.6 Mt	<i>Hot Metal 1.5-1.6 Mnt</i>	FY26 ESL hot metal production 1.5-1.6 Mt · 1.5-1.6 Mt	2026-05-15	H	FY26 ESL hot metal production guidance reaffirmed at 1.5-1.6 Mt	MET	1.6 vs 1.5-1.6 Mt		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 FACOR ferrochrome production guidance of 100-110 kt	<i>Ferrochrome 100 - 110 kt</i>	FY26 FACOR ferrochrome production 100-110 kt · 100-110 kt	2026-05-15	H	FY26 FACOR ferrochrome production reached 101 kt	MET	101 vs 100-110 kt		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Oil & Gas average gross volume guidance of 95-100 kboepd	<i>Average Gross Volume 95-100 kboepd</i>	FY26 Oil & Gas gross volume 95-100 kboepd · 95-100 kboepd	2026-05-15	H	FY26 Oil & Gas gross volume averaged 87.2 kboepd	MISSED	87.2 vs 95-100 kboepd	natural decline	Supply chain
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Pig Iron production guidance of 950-1,050 kt	<i>Pig Iron 950 - 1050 kt</i>	FY26 Pig Iron production 950-1,050 kt · 950-1,050 kt	2026-05-15	H	FY26 Pig Iron production reached 895 kt	MISSED	895 vs 950-1,050 kt		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Zinc India finished metal production guidance of 1,090-1,100 kt	<i>Finished Metal 1,090 - 1,100 kt</i>	FY26 Zinc India finished metal 1,090-1,100 kt · 1,090-1,100 kt	2026-05-15	H	FY26 Zinc India finished metal production reached 1,048 kt	PARTIAL	1,048 vs 1,090-1,100 kt		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Zinc India mined metal production guidance of 1,115-1,135 kt	<i>Mined Metal 1,115 - 1,135 kt</i>	FY26 Zinc India mined metal 1,115-1,135 kt · 1,115-1,135 kt	2026-05-15	H	FY26 Zinc India mined metal production reached 1,114 kt	PARTIAL	1,114 vs 1,115-1,135 kt		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Zinc India silver production guidance of 700-710 tonnes	<i>Silver 700 - 710 tonnes</i>	FY26 Zinc India silver production 700-710 t · 700-710 t	2026-05-15	H	FY26 Zinc India silver production reached 627 tonnes	MISSED	627 vs 700-710 t		
2025-04-01	Q4FY25	Q4FY25 transcript	KCM copper production of 150-180k tons in 2026	<i>that we will do about 150,000 tons of copper in 2026. I am very pleased to say that we are on track to deliver that</i>	KCM copper production 150-180 kt in 2026 · 150-180 kt in 2026	2026	M		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	OALP/DSP contribution to Oil & Gas production to reach 8-10% by Q4FY26	<i>we are working on is trying to figure out whether we can reach around 8% to 10% by Q4</i>	OALP/DSP share 8-10% by Q4FY26 · 8-10% share by Q4FY26	2026-05-15	M	OALP/DSP share of gross operated production reached 3.8% in FY26	MISSED	3.8 vs 8-10 %		
2025-04-01	Q4FY25	Q4FY25 transcript	Zinc International production guidance of 235-265k tons in FY26	<i>we are confident to achieve our production guidance of 235,000 tons to 265,000 tons</i>	Zinc International production 235-265 kt in FY26 · 235-265 kt in FY26	2026-05-15	H	Zinc International production reached 176 kt in 9MFY26	MET	1,76,000 vs 235-265 kt		
2025-08-01	Q1FY26	Q1FY26 presentation	Alumina capacity expansion to 5 MTPA by FY26 and 6 MTPA by FY28	<i>Alumina Capacity (MTPA) (5 MTPA in FY26, 6 MPTA - FY28)</i>	Alumina capacity 5 MTPA by FY26, 6 MTPA by FY28 · 5 MTPA by FY26, 6 MTPA by FY28		H	Lanjigarh refinery alumina capacity exit run rate reached 4 MTPA by FY26	MISSED	4 vs 5-6 MTPA		
2025-08-01	Q1FY26	Q1FY26 presentation	Aluminium smelting capacity to 3.1 MTPA by FY28	<i>Smelting Capacity (MTPA) (3.1 MTPA by FY28)</i>	Aluminium smelting capacity 3.1 MTPA by FY28 · 3.1 MTPA by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Commission 160 Ktpa roaster at Debari in Q2FY26	<i>targeting the commissioning of a 160,000 ton per annum roaster at Debari and in the current quarter</i>	Debari roaster (160 Ktpa) commissioned by Q2FY26 · 160 Ktpa	2025-11-14	H	Debari roaster commissioned in 1HFY26	MET	160 vs 160 Ktpa		
2025-08-01	Q1FY26	Q1FY26 presentation	Ferrochrome capacity to 500 KTPA by FY28	<i>Ferrochrome Capacity (KTPA) (500 by FY28)</i>	Ferrochrome capacity 500 KTPA by FY28 · 500 KTPA by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Complete Gamsberg Phase-2 project in H2FY26 (525 Ktpa mine capacity)	<i>Zinc International business is on course to complete the Gamsberg Phase-2 project in the second half of the current financial year, thereby increasing operational mine</i>	Gamsberg Phase-2 (525 Ktpa) completed by H2FY26 · 525 Ktpa		H	Gamsberg Phase-2 94% complete; re-set to 1HFY27	MISSED	94 vs 525 Ktpa	Waste stripping at open pit took longer to catch up	Capacity delay
2025-08-01	Q1FY26	Q1FY26 presentation	Iron ore merchant capacity to 17 MTPA by FY28	<i>Merchant Iron Ore (MTPA) (17 MTPA in FY28)</i>	Iron ore merchant capacity 17 MTPA by FY28 · 17 MTPA by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Commission Lanjigarh Train II and Balco smelter (435 Ktpa) in Q2FY26	<i>the commissioning of Lanjigarh Train II and the 435,000 tons per annum Balco smelter is targeted in the current quarter</i>	Lanjigarh Train II & Balco smelter (435 Ktpa) commissioned by Q2FY26 · 435 Ktpa	2025-11-14	H	First alumina from Lanjigarh Train II; first metal from Balco smelter commissioned	MISSED	3 vs 435 Ktpa		
2025-08-01	Q1FY26	Q1FY26 presentation	Merchant power capacity to 4.78 GW by FY26	<i>Merchant Power Capacity (GW) (FY26)</i>	Merchant power capacity 4.78 GW by FY26 · 4.78 GW by FY26	2026-05-15	H	Merchant power capacity reached 4,934 MW by FY26	MET	4.93 vs 4.78 GW		
2025-08-01	Q1FY26	Q1FY26 presentation	Oil production target of 125 kboepd by FY28	<i>Oil Production (kboepd) (125 kboepd in FY28)</i>	Oil production 125 kboepd by FY28 · 125 kboepd by FY28	2028-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-08-01	Q1FY26	Q1FY26 transcript	Add 1.3 GW power capacity in Q2FY26	<i>Our power business is set to add another 1,300 Megawatts of new capacity in the second quarter</i>	Power capacity +1.3 GW by Q2FY26 · 1.3 GW	2025-11-14	H	commissioned 700 MW in Q2FY26	MISSED	700 vs 1,300 MW		
2025-08-01	Q1FY26	Q1FY26 presentation	Steel capacity expansion to 3.5 MTPA by FY28	<i>Steel Capacity (MTPA) (3.5 MTPA by FY28)</i>	Steel capacity 3.5 MTPA by FY28 · 3.5 MTPA by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Zinc India smelting capacity to 1.38 MTPA by FY29	<i>Smelting Capacity (MTPA) (1.38 MTPA by FY29)</i>	Zinc India smelting capacity 1.38 MTPA by FY29 · 1.38 MTPA by FY29	2029-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Zinc International MIC capacity to 525 KTPA by FY26	<i>MIC Capacity (KTPA) (525 by FY26)</i>	Zinc International MIC capacity 525 KTPA by FY26 · 525 KTPA by FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Aluminium hot metal cost of \$1,700-1,750/t for FY26	<i>the hot metal cost for the year will be in the range of 1,700 to 1,750</i>	FY26 aluminium hot metal cost \$1,700-1,750/t · \$1,700-1,750/t	2026-05-15	H	FY26 aluminium hot metal cost reached 1,752 \$/t	PARTIAL	1,752 vs 1,700-1,750 USD/t		
2025-08-01	Q1FY26	Q1FY26 transcript	Oil & gas OPEX of \$15-16/barrel for FY26	<i>on our OPEX, which is going to be around \$15 to \$16 per barrel</i>	FY26 oil & gas OPEX \$15-16/bbl · \$15-16/bbl	2026-05-15	H	FY26 oil & gas OPEX reached \$15.5/boe	MET	15.5 vs 15-16 USD/bbl		
2025-08-01	Q1FY26	Q1FY26 presentation	Consolidated EBITDA target of \$8-10bn in medium term	<i>Estimated EBITDA Between USD 8-10 Bn</i>	Consolidated EBITDA \$8-10bn medium term · \$8-10bn medium term	medium term	H	FY26 consolidated EBITDA reached ₹18,842 crore	NYT	actual in INR_cr not comparable to USD_bn		
2025-08-01	Q1FY26	Q1FY26 transcript	Net debt/EBITDA of 1x by FY26-end	<i>by the end of the fiscal, our leverage will further improve to 1x</i>	FY26-end net debt/EBITDA 1x · 1x	2026-05-15	H	FY26-end net debt/EBITDA reached 0.95x	MET	0.95 vs 1 x		
2025-08-01	Q1FY26	Q1FY26 transcript	VRL deleveraging by \$3bn over 3 years	<i>VRL will deleverage 3 billion over the 3 years</i>	VRL deleveraging \$3bn by FY28 · \$3bn	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	EC clearance for Sijimali bauxite mine by Q2FY26-end	<i>targeting the EC by the end of this quarter</i>	Sijimali EC clearance by Q2FY26-end · Q2FY26-end	2025-11-14	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Mechanical completion of Gamsberg Phase-2 by Dec 2025	<i>targeting mechanical completion by December as we previously guided</i>	Gamsberg Phase-2 mechanical completion by Dec 2025 · Dec 2025	2025	H	mechanical completion not achieved; ramp-up re-set to Q2FY27	MISSED	slipped ~3 qtrs		
2025-08-01	Q1FY26	Q1FY26 transcript	Start production at Sijimali bauxite mine by Q4FY26	<i>start of production at the end of Quarter 4</i>	Sijimali bauxite production start by Q4FY26 · Q4FY26	2026-05-15	H	re-set to 1HFY27	MISSED	slipped ~2 qtrs		
2025-08-01	Q1FY26	Q1FY26 transcript	3 Mtpa alumina production in FY26	<i>progress towards delivering a guided volume of over 3 million metric tons in the current financial year</i>	FY26 alumina production >3 Mtpa · >3 Mtpa	2026-05-15	H	FY26 alumina production reached 2.916 Mtpa	MET	2,916 vs 3 Mtpa		
2025-08-01	Q1FY26	Q1FY26 transcript	1.2 Mtpa refined zinc metal production in FY26	<i>making us ready for the 1.2 plus million tons per annum refined metal production</i>	FY26 refined zinc metal production >1.2 Mtpa · >1.2 Mtpa	2026-05-15	H	FY26 refined zinc metal production reached 1,048 kt	MET	10,48,000 vs 1.2 Mtpa		
2025-11-01	Q2FY26	Q2FY26 transcript	Commission Gamsberg Phase-II expansion (220 Ktpa) by end-FY26	<i>Gamsberg Phase-II expansion, targeting 220,000 tons per annum incremental capacity, is now at 80% completion and is on track for commissioning by the end of</i>	Gamsberg Phase-II 220 Ktpa by FY26-end · 220 Ktpa by FY26-end	2026-05-15	H	Gamsberg Phase-II re-set to Q2FY27	MISSED	2 vs 220 Ktpa		
2025-11-01	Q2FY26	Q2FY26 transcript	Increase merchant power capacity by 20 GW by 2030	<i>increase our merchant power capacity by 20 Gigawatts as we have guided previously by 2030</i>	Merchant power capacity +20 GW by 2030 · +20 GW by 2030	2030	M		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Reduce alumina cost by \$50 per ton in Q3 and Q4 FY26 from Q2 levels	<i>we expect in the next two quarters, the prices to go down further by \$50 each</i>	Alumina cost -\$50/t in Q3 & Q4 FY26 vs Q2 · Alumina cost -\$50/t in Q3 & Q4 FY26	2026-02-14	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Aluminium CoP guidance of \$1,700-1,750/t in FY26	<i>-2.6 Mnt CoP2 \$1,700/t - \$1,750/t</i>	FY26 aluminium CoP \$1,700-1,750/t · \$1,700-1,750/t CoP in FY26	2026-05-15	H	FY26 aluminium CoP reached 1,752 \$/t	PARTIAL	1,752 vs 1,700-1,750 USD_per_t		
2025-11-01	Q2FY26	Q2FY26 transcript	Reduce aluminium hot metal cost to below \$1,650 per ton in H2 FY26	<i>we are on the track for full-year guidance with H2 hot metal cost being sub \$1,650</i>	H2FY26 aluminium CoP < \$1,650/t		H	FY26 yearly hot metal cost reached \$1,752/t	MISSED	1,752 vs 1,650 USD_per_t		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-11-01	Q2FY26	Q2FY26 transcript	Reduce Vedanta Resources average cost of borrowings to below 8%	<i>We are targeting to bring down our average cost of borrowings to below 8% in near term</i>	VRL avg cost of borrowings < 8% · Avg cost of borrowings < 8%	near term	H	4QFY26 closing interest cost stands at ~8.9%	NYT	undated target — interim 8.9 %		
2025-11-01	Q2FY26	Q2FY26 presentation	FY26 consolidated EBITDA to surpass FY22 record of ~\$6bn	<i>full year EBITDA surpassing the historic best EBITDA of ~USD 6bn delivered in FY22</i>	FY26 EBITDA > \$6.0 bn	2026-05-15	H	FY26 EBITDA reached ₹65,976 crore, highest-ever annual	NYT	actual in INR_cr not comparable to USD_bn		
2025-11-01	Q2FY26	Q2FY26 presentation	Net debt/EBITDA ratio of ~1.37x by end-Q2FY26	<i>Net debt/ EBITDA stands at 1.37x</i>	Net debt/EBITDA 1.37x by Q2FY26-end · 1.37x by Q2FY26-end	2025-11-14	H	Net debt/EBITDA ratio reached 0.95x at FY26-end	MET	0.95 vs 1.37 x		
2025-11-01	Q2FY26	Q2FY26 transcript	Deleverage the group by \$3 billion by FY27 at Vedanta Resources	<i>We also have publicly committed that from current \$4.4 billion will go down to \$3 billion over next</i>	Vedanta Resources net debt to \$3bn by FY27 · \$3bn net debt by FY27	2027-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	List all five demerged entities by end-FY26	<i>we expect approvals to follow. This will set the stage for the listing of all five demerged entities by the end of FY '26</i>	5 entities listed by 31 Mar'26 · 5 entities listed by FY26-end	2026-05-15	H		NYT	no outcome reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Athena Unit 2 commissioning in 4QFY26	<i>Athena: Unit 2 (600MW) is expected to start commissioning in 4QFY26</i>	Athena Unit 2 commissioning by 4QFY26	2026-05-15	H		NYT	no outcome reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Commission Ghogharpalli mine in Q2-Q3 FY27	<i>Ghogharpalli, we had originally communicated the 2nd Quarter of FY '27, that might move up by a quarter, but still positive. So, that will be</i>	Ghogharpalli mine commissioned by Q2-Q3FY27 · Ghogharpalli commissioned by Q2-Q3FY27	2026-11-14	H		NYT	no outcome reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Commission Kuraloi mine in Q4 FY26	<i>Kuraloi, previously, we had communicated Quarter 3 this year. I think given the timelines there, we might push it out by a couple of months</i>	Kuraloi mine commissioned by Q4FY26 · Kuraloi commissioned by Q4FY26	2026-05-15	H	re-set to 1HFY27	MISSED	slipped ~2 qtrs		
2025-11-01	Q2FY26	Q2FY26 presentation	Alumina production guidance of 3.0-3.1 Mnt in FY26	<i>Alumina 3.0-3.1 Mnt</i>	FY26 alumina production 3.0-3.1 Mnt · 3.0-3.1 Mnt alumina in FY26	2026-05-15	H	FY26 alumina production reached 2.916 Mnt	MET	2,916 vs 3-3.1 Mnt		
2025-11-01	Q2FY26	Q2FY26 presentation	Aluminium production guidance of 2.5-2.6 Mnt in FY26	<i>3.0-3.1 Mnt Aluminium1 2.5 -2.6 Mnt</i>	FY26 aluminium production 2.5-2.6 Mnt · 2.5-2.6 Mnt aluminium in FY26	2026-05-15	H	FY26 aluminium production reached 2,456 kt	MET	24,56,000 vs 2.5-2.6 Mnt		
2025-11-01	Q2FY26	Q2FY26 presentation	Iron Ore Goa production guidance of 2.2-2.7 Mnt in FY26	<i>Goa 2.2 – 2.7 Mnt</i>	FY26 iron ore Goa production 2.2-2.7 Mnt · 2.2-2.7 Mnt Goa iron ore in FY26	2026-05-15	H	FY26 Goa iron ore production reached 1.6 Mnt	MISSED	1.6 vs 2.2-2.7 Mnt		
2025-11-01	Q2FY26	Q2FY26 presentation	Iron Ore Karnataka production guidance of 5.5-6.1 Mnt in FY26	<i>Karnataka 5.5 – 6.1 Mnt</i>	FY26 iron ore Karnataka production 5.5-6.1 Mnt · 5.5-6.1 Mnt Karnataka iron ore in FY26	2026-05-15	H	FY26 Karnataka iron ore production reached 5.0 Mnt	MISSED	5 vs 5.5-6.1 Mnt		
2025-11-01	Q2FY26	Q2FY26 presentation	Iron Ore Orissa production guidance of 4.5-5.2 Mnt in FY26	<i>Orissa 4.5 – 5.2 Mnt</i>	FY26 iron ore Orissa production 4.5-5.2 Mnt · 4.5-5.2 Mnt Orissa iron ore in FY26	2026-05-15	H	FY26 Orissa iron ore production reached 4.7 Mnt	MET	4.7 vs 4.5-5.2 Mnt		
2025-11-01	Q2FY26	Q2FY26 presentation	Zinc India silver production guidance of 670-690 tonnes in FY26	<i>Silver 670 - 690 tonnes</i>	FY26 zinc India silver 670-690 t · 670-690 t silver in FY26	2026-05-15	H	FY26 Zinc India silver production reached 627 tonnes	MISSED	627 vs 670-690 tonnes		
2025-11-01	Q2FY26	Q2FY26 presentation	Zinc International BMM MIC production guidance of 55-65 kt in FY26	<i>BMM 55 – 65 kt</i>	FY26 zinc International BMM MIC 55-65 kt · 55-65 kt BMM MIC in FY26	2026-05-15	H	FY26 BMM MIC production reached 40 kt	MISSED	40 vs 55-65 kt		
2025-11-01	Q2FY26	Q2FY26 presentation	Zinc International Gamsberg MIC production guidance of 180-200 kt in FY26	<i>Gamsberg 180 - 200 kt</i>	FY26 zinc International Gamsberg MIC 180-200 kt · 180-200 kt Gamsberg MIC in FY26	2026-05-15	H	FY26 Gamsberg MIC production reached 185 kt	MET	185 vs 180-200 kt		
2025-11-01	Q2FY26	Q2FY26 transcript	Confirm 100-130 million barrels of usable reserves in Northeast by end-FY26	<i>we can expect till end of this financial year confirmation of the reserves in between 100 million and 130 million barrels usable</i>	Northeast reserves 100-130 Mboe by FY26-end · 100-130 Mboe by FY26-end	2026-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2026-01-01	Q3FY26	Q3FY26 transcript	Aluminium capacity to 3.0 Mtpa by next 18 months	<i>close the gap from 2.8 to 3 million tons, which is what we have guided in the market over the next 18-months</i>	Aluminium capacity 3.0 Mtpa by 18M · 3.0 Mtpa by 18M		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission BALCO smelter expansion (435 KTPA) by Q4FY26	<i>BALCO Smelter Expansion (commissioning initiated for 435 KTPA)</i>	BALCO smelter expansion 435 KTPA by Q4FY26 · 435 KTPA by Q4FY26	2026-05-15	H	commissioning initiated; 70 pots by Q4FY26; full 435 KTPA ramp to Q4FY27	MISSED	70 vs 435 KTPA	delay through partner substitution and resource augmentation	Capacity delay
2026-01-01	Q3FY26	Q3FY26 presentation	Expand Bicholim mine to 4.2 MTPA by 1HFY27	<i>Bicholim Mine (Goa) expansion: 3 -> 3.6 -> 4.2 MTPA - 1HFY27</i>	Bicholim mine capacity 4.2 MTPA by 1HFY27 · 4.2 MTPA by 1HFY27		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission 0.5 MTPA Cudnem mine by 2HFY27	<i>0.5 MTPA Cudnem Mine (Goa) - 2HFY27</i>	Cudnem mine capacity 0.5 MTPA by 2HFY27 · 0.5 MTPA by 2HFY27		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Expand ferrochrome smelter to 500 KTPA by 1HFY28	<i>Smelter Plant Production to 500 KTPA - 1HFY28</i>	Ferrochrome smelter capacity 500 KTPA by 1HFY28 · 500 KTPA by 1HFY28		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Ramp up Gamsberg Phase 2 to 200 KTPA MIC by 1HFY27	<i>200 KTPA MIC Gamsberg Ph-2 Ramp - 1HFY27</i>	Gamsberg Phase 2 MIC capacity 200 KTPA by 1HFY27 · 200 KTPA MIC by 1HFY27		H	re-set to Q2FY27	MISSED	2 vs 200 KTPA	waste stripping catch-up delayed open-pit schedule	Capacity delay
2026-01-01	Q3FY26	Q3FY26 presentation	Commission Ghogarpalli coal mine by 2HFY27	<i>Ghogarpalli Coal Mine - 2HFY27</i>	Ghogarpalli coal mine commissioned by 2HFY27 · Commissioned by 2HFY27		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission Janthakal mine by 2HFY28	<i>Janthakal Mine (Karnataka) - 2HFY28</i>	Janthakal mine commissioned by 2HFY28 · Commissioned by 2HFY28		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission Kuraloi coal mine by Q4FY26	<i>Kuraloi Coal Mine - Q4FY26</i>	Kuraloi coal mine commissioned by Q4FY26 · Commissioned by Q4FY26	2026-05-15	H	re-set to 1HFY27	MISSED	1 vs 4	mining lease received a week back; mining operations to start in a month	Capacity delay
2026-01-01	Q3FY26	Q3FY26 presentation	Expand Lanjigarh refinery to 5 MTPA by 1HFY27	<i>Ramp up to 5 MTPA at Lanjigarh • Smelter capacity expansion to</i>	Lanjigarh refinery capacity 5 MTPA by 1HFY27 · 5 MTPA by 1HFY27		H	Lanjigarh refinery exit run rate reached 4 MTPA by end FY26	MISSED	4 vs 5 MTPA	Calciners and boiler running at 75-80% capacity; rated capacity expected Q1FY27	Capacity delay
2026-01-01	Q3FY26	Q3FY26 transcript	Power capacity to 4.8 GW by end-H1FY27	<i>total capacity as of now up and running is 4.2 gigawatt. This is expected to go to around 4.8 gigawatt by end of H1 of</i>	Power capacity 4.8 GW by H1FY27 · 4.8 GW by H1FY27		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission Sijimali bauxite mine by 1HFY27	<i>Sijimali Bauxite Mine - 1HFY27</i>	Sijimali bauxite mine commissioned by 1HFY27 · Commissioned by 1HFY27		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Expand steel hot metal capacity to 3.5 MTPA by 2HFY27	<i>Hot Metal Capacity Expansion from 1.7 to 3.5 MTPA - 2HFY27</i>	Steel hot metal capacity 3.5 MTPA by 2HFY27 · 3.5 MTPA by 2HFY27		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Add 600 MW at Athena by 2HFY27	<i>Additional 600 MW at Athena - 2HFY27</i>	Athena additional capacity 600 MW by 2HFY27 · 600 MW by 2HFY27		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission 600 MW at Athena by 1HFY26	<i>600 MW at Athena - 1HFY26</i>	Athena capacity 600 MW by 1HFY26 · 600 MW by 1HFY26		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Complete 21 KTPA cell-house debottlenecking by 2HFY26	<i>21 KTPA Cell House Debottlenecking (Dariba - 1HFY26; Chanderiya - 2HFY26)</i>	Cell-house debottlenecking 21 KTPA by 2HFY26 · 21 KTPA by 2HFY26		H	21 KTPA Cell House Debottlenecking at Chanderiya completed in 2HFY26	MET	21 vs 21 KTPA		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission 600 ktpa chrome ore beneficiation plant by 2HFY27	<i>600 ktpa Chrome ore Beneficiation Plant - 2HFY27</i>	Chrome ore beneficiation plant 600 ktpa by 2HFY27 · 600 ktpa by 2HFY27		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Complete 160 KTPA Debari roaster by 1HFY26	<i>160 KTPA Debari Roaster - 1HFY26</i>	Debari roaster 160 KTPA by 1HFY26 · 160 KTPA by 1HFY26		H	Debari roaster 160 KTPA target re-stated for 1HFY26	MET	160 vs 160 KTPA		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2026-01-01	Q3FY26	Q3FY26 presentation	Commission 420 KTPA DI pipe plant in Goa by 1HFY27	420 KTPA DI Pipe Plant (Goa) – 1HFY27	DI pipe plant 420 KTPA by 1HFY27 · 420 KTPA by 1HFY27		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission 510 KTPA fertilizer project by 1HFY27	510 KTPA Fertilizer Project – 1HFY27	Fertilizer project 510 KTPA by 1HFY27 · 510 KTPA by 1HFY27		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	FY26 growth capex of \$1.7-1.9bn	Growth Capex USD 1.3bn	FY26 growth capex \$1.7-1.9bn · \$1.7-1.9bn	2026-05-15	H	FY26 growth capex reached ₹14,918 crore	NYT	actual in INR_cr not comparable to USD_bn		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission hot acid leaching plant by Q4FY26	Hot Acid Leaching Plant – Q4FY26	Hot acid leaching plant commissioned by Q4FY26 · Commissioned by Q4FY26	2026-05-15	H	re-set to 1HFY27	MISSED	1 vs 4		Capacity delay
2026-01-01	Q3FY26	Q3FY26 presentation	Commission 1000 MW at Meenakshi Power by 1HFY26	1000 MW at Meenakshi Power – 1HFY26	Meenakshi Power capacity 1000 MW by 1HFY26 · 1000 MW by 1HFY26		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission Ostapal underground operations by 1HFY27	Ostapal Underground Operations – 1HFY27	Ostapal underground operations commissioned by 1HFY27 · Commissioned by 1HFY27		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission 10 Mtpa zinc tailings reprocessing plant by 2HFY28	10 Mtpa Zinc Tailings Reprocessing Plant – 2HFY28	Zinc tailings reprocessing plant 10 Mtpa by 2HFY28 · 10 Mtpa by 2HFY28		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Aluminium hot-metal cost sub-\$750/t by Q1FY27	as we go into Q1, you will see a cost sub-\$750	Aluminium CoP < \$750/t by Q1FY27 · < \$750/t by Q1FY27	2026-08-14	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Close FY26 with net-debt/EBITDA of ~1x at Vedanta India	we will be closing the fiscal at about 1x	FY26 net-debt/EBITDA ~1x · ~1x by FY26-end	2026-05-15	H	FY26 net-debt/EBITDA at Vedanta India reached 0.95x	MET	0.95 vs 1 x		
2026-01-01	Q3FY26	Q3FY26 presentation	Reduce group net debt/EBITDA to ~1x by FY27	32 [GUIDANCE]: <1x Group Net <1x Group Net	Group net debt/EBITDA ~1x by FY27 · ~1x by FY27	2027-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Deleverage Vedanta India by \$0.7 bn in FY26	VEDL India debt will come down by almost 0.7 billion in the current year	Vedanta India deleveraging \$0.7 bn in FY26 · \$0.7 bn deleveraging in FY26	2026-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Deleverage Vedanta Resources by \$4.5bn by FY27	\$4.5 bn US\$ bn Continuous Deleveraging	Vedanta Resources deleveraging \$4.5bn by FY27 · \$4.5bn by FY27	2027-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Achieve net water positivity by 2030	net water positivity by 2030	Net water positivity by 2030 · Net water positive by 2030	2030	M		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Achieve net-zero emissions by 2050 or sooner	commitment to achieving net-zero emissions by 2050 or sooner	Net-zero emissions by 2050 or sooner · Net-zero by 2050 or sooner	2050	L		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Demerger effective date of 1 April with listings in same quarter	targeting April 1st as effective date of demerger with listing of the demerged entities in the same quarter around mid-to-end of May	Demerger effective 1-Apr-26, listings by May-26 · Effective 1-Apr-26, listings by May-26	2026-08-14	H	Demerger effective 1-May-26, one month later than targeted	NYT	in progress, not yet due		
2026-01-01	Q3FY26	Q3FY26 transcript	Operationalise Sijimali bauxite mine by Q1FY27	we are expecting by February '26, and we are quite hopeful of operationalising	Sijimali mine operational by Q1FY27 · Operational by Q1FY27	2026-08-14	H		NYT	no outcome reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Oil & Gas production to 90 kboepd by FY27	we expect the next year to stabilize everything and to grow to at least 90,000	Oil & Gas production 90 kboepd by FY27 · 90 kboepd by FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	Alumina capacity of 4.0-4.1 Mtpa by FY27	Alumina 4.0 - 4.1 Mnt	Alumina capacity 4.0-4.1 Mtpa by FY27 · 4.0-4.1 Mtpa by FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	Aluminium capacity of 2.6-2.7 Mtpa by FY27	Mnt Aluminium1 2.6 - 2.7 Mnt	Aluminium capacity 2.6-2.7 Mtpa by FY27 · 2.6-2.7 Mtpa by FY27	2027-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2026-04-01	Q4FY26	Q4FY26 transcript	BALCO smelter expansion ramp-up to 105 KT/quarter by Q4FY27	<i>Q1 should be 25%, Q2 ramped up to 50%, Q3 75%, and as we go into the Q4, it will be 100%</i>	BALCO smelter 105 KT/quarter by Q4FY27 · 105 KT/quarter by Q4FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Copper rod mill plant in Saudi Arabia commissioned by September 2026	<i>that plant will be ready in September this year</i>	Copper rod mill commissioned by Sep 2026 · Sep 2026	2026	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Alumina cost of production to ~\$750/t by Q2FY27	<i>by quarter 2, we should see alumina cost hovering around \$750</i>	Alumina CoP ~\$750/t by Q2FY27 · \$750/t	2026-11-14	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	Aluminium cost of production \$1,650-1,700/t by FY27	<i>tax) (1,731) - - (223) -</i>	Aluminium CoP \$1,650-1,700/t by FY27 · \$1,650-1,700/t by FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	Oil & Gas opex of \$15.5-16.5/boe by FY27	<i>Opex \$15.5 - 16.5/boe</i>	Oil & Gas opex \$15.5-16.5/boe by FY27 · \$15.5-16.5/boe by FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	Zinc India cost of production \$975-1,000/t by FY27	<i>tax) (1,731) - - (223) -</i>	Zinc India CoP \$975-1,000/t by FY27 · \$975-1,000/t by FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	Zinc International cost of production \$1,500-1,550/t by FY27	<i>CoP \$1,500/t - \$1,550/t</i>	Zinc International CoP \$1,500-1,550/t by FY27 · \$1,500-1,550/t by FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Vedanta Resources FY27 principal funding requirement of ~\$1 billion	<i>is VRL to VDL. So total combined half a billion is the requirement for the principal</i>	VRL FY27 principal funding ~\$1bn · ~\$1bn	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Copper business EBITDA margin to reach ~5% in FY27	<i>the margin in the Copper business going from roughly 1%. right now, going to at</i>	Copper EBITDA margin ~5% in FY27 · ~5%	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Brand fee for Copper reduced to 0.75% from FY27	<i>brand fee for copper from the current 3% will go down to 0.75%</i>	Copper brand fee 0.75% from FY27 · 0.75%	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Three critical mineral blocks exploration completion by 2028, production by 2030	<i>and smelting, we should look at somewhere around 2030 adding three more metals to the bottom line</i>	3 critical mineral blocks production by 2030 · 2030	2030	M		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 transcript	List all five demerged entities by mid-June 2026	<i>The shares of the resulting companies are expected to list and commence trading by mid-June</i>	5 entities listed by mid-June 2026 · mid-June 2026	2026-06-30	H	5 demerged entities listed by 30 June 2026	NYT	in progress, not yet due		
2026-04-01	Q4FY26	Q4FY26 presentation	ASP injection at Mangala Cluster C by Q1FY27	<i>completed; Injection is being targeted in 1Q FY27</i>	ASP injection at Mangala Cluster C by Q1FY27 · Injection by Q1FY27	2026-08-14	H		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 presentation	Gamsberg Phase 2 ramp-up by Q2FY27	<i>Gb Ph-2 commissioning- 1H FY27</i>	Gamsberg Phase 2 ramp-up by Q2FY27 · Ramp-up by Q2FY27	2026-11-14	H		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Ghogharpalli coal mine FC in Q1FY27 and commissioning as guided	<i>and we remain committed to commission this block in the timelines that we've indicated</i>	Ghogharpalli FC Q1FY27, commissioning as guided · FC Q1FY27	2026-08-14	H		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Kuraloi coal mine start operations in May 2026	<i>in a month or so, we should start seeing the mining operations</i>	Kuraloi coal mine start by May 2026 · May 2026	2026-05-31	H		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Sijimali bauxite mine EC in May 2026 and opening in H1FY27	<i>EC we're expecting next month, and hopefully in H1 we will see the mines</i>	Sijimali EC May 2026, opening H1FY27 · EC May 2026, opening H1FY27		H		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Gamsberg Phase 2 commissioning in Q1FY27 with ramp-up over 12-18 months	<i>the ramp-up plan and commissioning in this quarter and ramp-up for the rest of the year. In terms of the reasons for</i>	Gamsberg Phase 2 commissioned Q1FY27, ramp-up 12-18 months · Q1FY27 commissioning, 12-18 months ramp-up	2026-08-14	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2026-04-01	Q4FY26	Q4FY26 presentation	Honey production of 20,000 litres by FY28	<i>scale to 1,500+ farmers & 20,000 lt. honey production by FY28</i>	Honey production 20,000 litres by FY28 · 20,000 litres by FY28	2028-05-15	M		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	Oil & Gas average gross operated production of 90-95 kboepd by FY27	<i>Average Gross Volume 90 - 95 kboepd</i>	Oil & Gas gross operated production 90-95 kboepd by FY27 · 90-95 kboepd by FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	Zinc India finished metal production of 1,090-1,110 kt by FY27	<i>Finished Metal 1,090 - 1,110 kt</i>	Zinc India finished metal 1,090-1,110 kt by FY27 · 1,090-1,110 kt by FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	Zinc India mined metal production of 1,140-1,160 kt by FY27	<i>Mined Metal 1,140 - 1,160 kt</i>	Zinc India mined metal 1,140-1,160 kt by FY27 · 1,140-1,160 kt by FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	Zinc International Gamsberg production of 280-300 kt by FY27	<i>Gamsberg 280 - 300 kt</i>	Zinc International Gamsberg production 280-300 kt by FY27 · 280-300 kt by FY27	2027-05-15	H		NYT	no actual reported		
2026-07-01	Q1FY27	Q1FY27 presentation	Issue 1 VPPL share for every 20 Vedanta shares held on record date	<i>as follows: 1 fully paid-up equity share of Vedanta Property Platforms Limited of face value INR 1/- (Indian Rupee One) each, for every 20 fully</i>	1 VPPL share per 20 Vedanta shares · 1:20 share entitlement		H		NYT	no actual reported		
2026-07-01	Q1FY27	Q1FY27 presentation	Complete demerger process and list VPPL by FY28	<i>the process is expected to be completed in FY28</i>	Demerger completion by FY28 · FY28 completion	2028-05-15	H		NYT	no outcome reported		
2026-07-01	Q1FY27	Q1FY27 presentation	File demerger scheme with stock exchanges for SEBI approval in August 2026	<i>Filing with the stock exchanges for obtaining their no-objection letter (including SEBI's comments/ approval) is expected in August 2026</i>	Demerger scheme filing by Aug 2026 · Filing by Aug 2026	2026	H		NYT	no outcome reported		

Methodology & Sources

What qualifies as a commitment

Only **measurable** statements — a number, %, ratio, ₹/\$ figure or a dated milestone. Generic or aspirational commentary is rejected. One promise per row, with a verbatim ≤ 25 -word quote.

How status is judged (deterministic rules — the model only retrieves)

- **MET** — delivered or exceeded the target
- **PARTIAL** — close but below target / a milestone slipped within grace
- **MISSED** — failed, incl. a date the company later pushed past the promised window
- **NYT** — outcome not yet reported within the verification window (excluded from scoring)

Confidence & the credibility score

H = hard numeric · **M** = directional · **L** = aspirational. Credibility = confidence-weighted delivery over testable promises (MET=1, PARTIAL=0.5, MISSED=0; H=1.0, M=0.8, L=0.6); bands A $\geq$ 75 B $\geq$ 60 C $\geq$ 45 D $\geq$ 30 E<30.

The verification window

Outcomes are verifiable only through **Q1FY27** (reported 2026-07-01). Later targets are therefore **NYT**. *Full retrieval · openai, mistral, gemini, groq.*

Source documents

Q2FY25 Presn

2024-11-01 · both

Q2FY25 Call

2024-11-01 · both

Q3FY25 Presn

2025-02-01 · both

Q3FY25 Call

2025-02-01 · both

Q4FY25 Presn

2025-04-01 · both

Q4FY25 Call

2025-04-01 · both

Q1FY26 Presn

2025-08-01 · both

Q1FY26 Call

2025-08-01 · both

Q2FY26 Presn

2025-11-01 · both

Q2FY26 Call

2025-11-01 · both

Q3FY26 Presn

2026-01-01 · both

Q3FY26 Call

2026-01-01 · both

+3 more

source documents (see the master table)
