

VEDANTA LIMITED

Lie Detector

Every **measurable** management commitment for this Metals & Mining company — extracted from the earnings calls and investor decks, then verified against reported actuals across **Q1FY26-Q3FY26**.



DELIVERY VS. DEADLINES

Delivery		42
Timelines		14

Curated

42

Measurable commitments tracked

12

Testable now · 4 delivered / partial

8

Missed — incl. slipped deadlines

30

Not yet testable (later periods)

Q1FY26 Presn · 2025-07-31

Q2FY26 Call · 2025-10-31

Q2FY26 Presn · 2025-10-31

Q3FY26 Call · 2026-01-29


Q3FY26 Presn · 2026-01-29

Verification window: through Q3FY26 (reported 2026-01-29)


01 Executive Dashboard

Most already-testable promises missed — chiefly slipped project deadlines; the beating full-year cost/profit guidance is still NYT.


STATUS OF ALL 42 COMMITMENTS

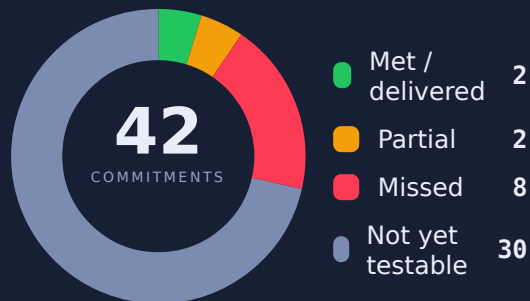

COMMITMENTS BY REPORTING QUARTER

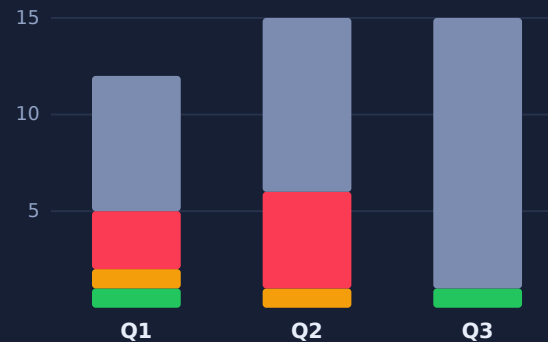


ROOT CAUSE OF MISSES & SHORTFALLS



Most already-testable promises missed — chiefly slipped project deadlines; the beating full-year cost/profit guidance is still NYT.

Of the 7 dated commitments that came due, 1 landed on time and 6 slipped right. The slippage timeline is overleaf.


CONFIDENCE MIX OF THE PROMISES




Deadline Slippage & Execution Momentum

Left: where each promised date **started** (amber) versus where management **re-set it** (red). Right: the reported financials.

TIMELINE COMMITMENTS — PROMISED → REVISED

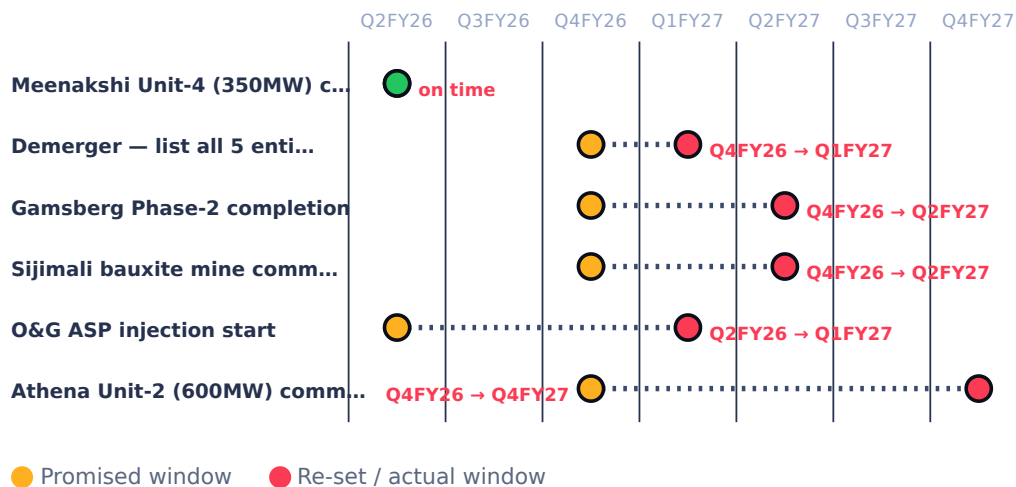

EBITDA (₹ CR) & MARGIN

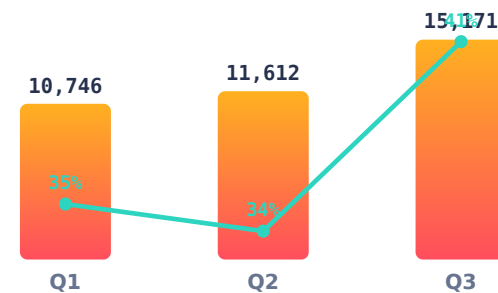

1.23×
Net debt /
EBITDA · Q3

27%
ROCE ·
Q3

₹45,899
cr
Revenue · Q3

The Track Record — 12 Testable Promises / part 1 of 2

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 30 promises are forward-dated and remain Not Yet Testable.

MISSED

Q1FY26 · Q1FY26 Presn (31 Jul'25)

Gamsberg Phase-2 completion

TARGET Gamsberg Ph-2 200 ktpa by 2HFY26

ACTUAL Q2 82%; Q3 ~90%, commissioning re-set to 1HFY27

VARIANCE **Slipped ~1-2 quarters**

Why: Ramp pushed to next year

Capacity delay

MISSED

Q1FY26 · Q1FY26 Presn (31 Jul'25)

O&G ASP injection start

TARGET ASP injection live by Q2FY26

ACTUAL Re-set to mid-3QFY26, then Q4FY26; first oil ~Apr'26

VARIANCE **Slipped ~2 quarters**

Why: Large/complex EOR; commissioning delayed

Capacity delay

MISSED

Q1FY26 · Q1FY26 Presn (31 Jul'25)

Athena Unit-2 (600MW) commissioning

TARGET Athena U2 600MW by Q4FY26

ACTUAL Q3 deck re-sets to 2HFY27

VARIANCE **Slipped ~3-4 quarters**

Why: Sequenced after first unit ramp/PPAs

Capacity delay

MISSED

Q2FY26 · Q2FY26 Call (31 Oct'25)

Alumina cost reduction (Q3 & Q4)

TARGET Alumina -\$50/t each Q3 & Q4

ACTUAL Q3 only -\$20/-22; exit re-set to sub-\$750 (Q1FY27)

VARIANCE **~-\$28-30/t short (~58%)**

Why: LME surge on priced bought-out alumina

Pricing / mix

MISSED

Q2FY26 · Q2FY26 Call (31 Oct'25)

O&G volume stabilisation

TARGET O&G volume stabilises from Q3

ACTUAL Q3 84.9 kboepd — fell from 89 (Q2)

VARIANCE **-4 kboepd QoQ (declined, not stable)**

Why: ASP commissioning/startup delayed

Capacity delay

MISSED

Q2FY26 · Q2FY26 Call (31 Oct'25)

Demerger — list all 5 entities

TARGET 5 entities listed by 31 Mar'26

ACTUAL NCLT order 16 Dec; effective 1 Apr'26; listing ~late May

VARIANCE **~2 months late (into Q1FY27)**

Why: NCLT/CP steps; power order only 9 Jan

Regulatory

The Track Record — 12 Testable Promises / part 2 of 2

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 30 promises are forward-dated and remain Not Yet Testable.

MISSED

Q2FY26 · Q2FY26 Call (31 Oct'25)

Sijimali bauxite mine commissioning

TARGET Sijimali live by Q4FY26
ACTUAL FC-I only on 31 Dec'25; EC awaited; re-set to 1HFY27
VARIANCE **Slipped ~1-2 quarters**

Why: Forest/EC clearances pending

Regulatory

MISSED

Q2FY26 · Q2FY26 Call (31 Oct'25)

O&G Northeast exploratory wells

TARGET Rudra spud Nov'25; Nagaland Feb'26
ACTUAL Q3: NE (SP-1) still delayed; spud pushed to ~end Mar'26
VARIANCE **~1 quarter+ slip**

Why: Env/local-govt approvals not complete

Regulatory

PARTIAL

Q1FY26 · Q1FY26 Presn (31 Jul'25)

FY26 Oil & Gas volume target

TARGET O&G 95-100 kboepd (rev 90-95)
ACTUAL Cut to 90-95 at Q2; Q3 84.9; 9M ~89 kboepd
VARIANCE **~-6 to -11 kboepd vs 95-100 (~6-11%)**

Why: ASP commissioning delay; base decline

Capacity delay

PARTIAL

Q2FY26 · Q2FY26 Call (31 Oct'25)

H2FY26 hot-metal cost

TARGET Hot-metal CoP < \$1,650/t (H2)
ACTUAL Q3 \$1,674/t (above); Q4 guided flat
VARIANCE **Q3 +\$24/t (+1.5%) vs cap**

Why: Carbon inflation; alumina benefit delayed

Cost inflation

MET

Q1FY26 · Q1FY26 Presn (31 Jul'25)

Meenakshi Unit-4 (350MW) commissioning

TARGET Meenakshi U4 350MW by Q2FY26
ACTUAL Commissioned in H1FY26 (1.3 GW added H1)
VARIANCE **On time**

MET

Q3FY26 · Q3FY26 Call (29 Jan'26)

Zinc India OFS / HZL stake

TARGET OFS ~1.1% HZL (~Rs 3,000 cr)
ACTUAL OFS launched 27 Jan, bids closed; ~1.1% / ~Rs 3,000 cr
VARIANCE **Delivered as stated**

Master Table — all 42 measurable commitments

Chronological · oldest first · colour = delivery status

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
31 Jul 2025	Q1FY26	Q1FY26 Presn (31 Jul'25)	FY26 alumina production target	Guidance: "Alumina 3.0-3.1 Mnt"	Alumina 3.0-3.1 Mnt (FY26)	FY26 results (Apr'26)	H	9M FY26: 2,034 kt (+32% YoY); Q3 0.8 Mnt — on track	NYT	9M 2.03 Mnt of 3.0-3.1 (~67%)		
31 Jul 2025	Q1FY26	Q1FY26 Presn (31 Jul'25)	FY26 aluminium production target	Guidance: "Aluminium 2.5-2.6 Mnt"	Aluminium 2.5-2.6 Mnt (FY26)	FY26 results (Apr'26)	H	9M FY26: 1,842 kt (+1%); run-rate ~2.45 Mnt — slightly soft	NYT	9M 1.84 Mnt; FY ~2.45 vs 2.5-2.6	BALCO ramp gradual	Capacity delay
31 Jul 2025	Q1FY26	Q1FY26 Presn (31 Jul'25)	FY26 aluminium hot-metal cost	Guidance: "CoP \$1,700/t - \$1,750/t"	Hot-metal CoP \$1,700-1,750/t	FY26 results (Apr'26)	H	Q3 \$1,674/t (below guide); 9M avg ~\$1,755/t	NYT	Q3 -\$26 to -\$76 vs band; tracking in-range	Power/alumina cost down in H2	
31 Jul 2025	Q1FY26	Q1FY26 Presn (31 Jul'25)	FY26 Zinc India cost of production	Guidance: "Zinc India CoP \$1,025/t-\$1,050/t"	Zinc CoP \$1,025-1,050/t (rev ~\$1,000)	FY26 results (Apr'26)	H	Q3 \$940/t — 6% better than guide	NYT	Q3 ~-\$60 to -\$110/t (beating)	Record mined metal, lower input cost	
31 Jul 2025	Q1FY26	Q1FY26 Presn (31 Jul'25)	FY26 Oil & Gas volume target	Guidance: "Avg Gross Volume 95-100 kboepd"	O&G 95-100 kboepd (rev 90-95)	FY26 results (Apr'26)	H	Cut to 90-95 at Q2; Q3 84.9; 9M ~89 kboepd	PARTIAL	~-6 to -11 kboepd vs 95-100 (~6-11%)	ASP commissioning delay; base decline	Capacity delay
31 Jul 2025	Q1FY26	Q1FY26 Presn (31 Jul'25)	Gamsberg Phase-2 completion	Slide: "Project completion targeted in 2HFY26"	Gamsberg Ph-2 200 ktpa by 2HFY26	FY26-end (Mar'26)	M	Q2 82%; Q3 ~90%, commissioning re-set to 1HFY27	MISSED	Slipped ~1-2 quarters	Ramp pushed to next year	Capacity delay
31 Jul 2025	Q1FY26	Q1FY26 Presn (31 Jul'25)	O&G ASP injection start	Slide: "ASP: Injection targeted in 2QFY26"	ASP injection live by Q2FY26	Q2FY26 results	M	Re-set to mid-3QFY26, then Q4FY26; first oil ~Apr'26	MISSED	Slipped ~2 quarters	Large/complex EOR; commissioning delayed	Capacity delay
31 Jul 2025	Q1FY26	Q1FY26 Presn (31 Jul'25)	Meenakshi Unit-4 (350MW) commissioning	Slide: "Unit 4 (350 MW) set to begin operation in 2QFY26"	Meenakshi U4 350MW by Q2FY26	Q2FY26 results	M	Commissioned in H1FY26 (1.3 GW added H1)	MET	On time		
31 Jul 2025	Q1FY26	Q1FY26 Presn (31 Jul'25)	Athena Unit-2 (600MW) commissioning	Slide: "Unit 2 (600MW) expected to start operations in 4QFY26"	Athena U2 600MW by Q4FY26	Q4FY26 results	M	Q3 deck re-sets to 2HFY27	MISSED	Slipped ~3-4 quarters	Sequenced after first unit ramp/PPAs	Capacity delay
31 Jul 2025	Q1FY26	Q1FY26 Presn (31 Jul'25)	FY26 Athena PLF target	Guidance: "Athena PLF 61%"	Athena PLF 61% (FY26)	FY26 results (Apr'26)	M	Q3 PLF 72% — mgmt: 11% over guidance	NYT	Q3 +11 ppt (ahead)	Strong availability	
31 Jul 2025	Q1FY26	Q1FY26 Presn (31 Jul'25)	VRL FY26 debt repayment	Slide: "remaining FY26, repayment of loan \$320 Mn"	VRL repay \$320M in FY26	FY26 results (Apr'26)	H	\$227M repaid in 1Q; ICL/maturities on track	NYT	~\$227M of \$320M done by Q1		
31 Jul 2025	Q1FY26	Q1FY26 Presn (31 Jul'25)	Group leverage (deleveraging path)	Slide: "Group Net Debt/EBITDA <1x (Med Term); VEDL <1x near term"	Group/VEDL ND-EBITDA <1x	FY26-FY27	M	Q3 1.23x; mgmt guides ~1x by Mar'26	NYT	1.23x vs <1x target		
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	FY26 consolidated EBITDA	"confident in achieving an annual EBITDA of more than \$6 billion in FY 26 at Vedanta India consol level"	FY26 EBITDA > \$6.0 bn	FY26 results (Apr'26)	H	9M EBITDA Rs 37,529 cr (~\$4.3bn); reaffirmed in Q3	NYT	Needs ~\$1.7bn in Q4 (on track)		
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	FY26 growth capex	"well on track to achieve our enhanced full-year capital guidance of between USD \$1.7 to \$1.9 billion"	FY26 capex \$1.7-1.9 bn	FY26 results (Apr'26)	H	9M \$1.3bn; Q3 narrowed to ~\$1.7bn (low end)	NYT	Tracking low end of range		
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	Alumina cost reduction (Q3 & Q4)	"\$50 per ton in Quarter 3 and \$50 per ton in Quarter 4... exit... closer to \$700 to \$710"	Alumina -\$50/t each Q3 & Q4	Q3FY26 results (29 Jan'26)	H	Q3 only -\$20/- \$22; exit re-set to sub-\$750 (Q1FY27)	MISSED	~-\$28-30/t short (~58%)	LME surge on priced bought-out alumina	Pricing / mix
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	H2FY26 hot-metal cost	"H2 hot metal cost being sub \$1,650"	Hot-metal CoP < \$1,650/t (H2)	Q4FY26 results (Apr'26)	H	Q3 \$1,674/t (above); Q4 guided flat	PARTIAL	Q3 +\$24/t (+1.5%) vs cap	Carbon inflation; alumina benefit delayed	Cost inflation
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	H2FY26 power cost	"timely power plant shutdown will enable us to achieve sub 500 per ton power cost in H2 FY 26"	Power cost < \$500/t (H2)	Q4FY26 results (Apr'26)	H	Q3 power cost -\$110/t QoQ (sharp fall)	NYT	H2 not fully reported		
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	O&G volume stabilisation	"We expect ASP injection to stabilize production volumes from Quarter 3 onwards"	O&G volume stabilises from Q3	Q3FY26 results (29 Jan'26)	M	Q3 84.9 kboepd — fell from 89 (Q2)	MISSED	-4 kboepd QoQ (declined, not stable)	ASP commissioning/startup delayed	Capacity delay
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	Demerger — list all 5 entities	"listing of all five demerged entities by the end of FY 26"	5 entities listed by 31 Mar'26	FY26-end (Mar'26)	H	NCLT order 16 Dec; effective 1 Apr'26; listing ~late May	MISSED	~2 months late (into Q1FY27)	NCLT/CP steps; power order only 9 Jan	Regulatory
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	VRL deleveraging (2-year)	"from current \$4.4 billion will go down to \$3 billion over next two years"	VRL net debt \$4.4bn -> \$3.0bn by ~FY27	FY27 (by Mar'27)	H	Dec'25 ~\$4.8bn incl ICL; ~\$0.3bn cut guided FY26	NYT	2-year target; early innings		
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	VEDL India leverage to 1x	"our debt to EBITDA will further improve to 1x... That goal remains unchanged"	VEDL ND/EBITDA -> 1.0x	FY26 results (Apr'26)	H	Q3 1.23x; mgmt guides closing FY26 ~1x	NYT	0.23x to go		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	Cost of borrowings	"targeting to bring down our average cost of borrowings to below 8% in near term"	Avg borrowing cost < 8%	Near term (FY26-27)	M	Q3 ~9% (below 9%, not yet <8%)	NYT	~100 bps above 8% target		
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	Sijimali bauxite mine commissioning	"on Sijimali, we have previously communicated Quarter 4 FY 26, so we are keeping the commissioning"	Sijimali live by Q4FY26	Q4FY26 results (Apr'26)	M	FC-I only on 31 Dec'25; EC awaited; re-set to 1HFY27	MISSED	Slipped ~1-2 quarters	Forest/EC clearances pending	Regulatory
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	Kuraloi coal mine commissioning	"on Kuraloi... we might push it out by a couple of months to Quarter 4 this year"	Kuraloi live by Q4FY26	Q4FY26 results (Apr'26)	M	FC Stage-II on 12 Jan'26; MDO on ground; on track Q4	NYT	Tracking to Q4FY26		
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	VRL ICL repayment (no rollover)	"\$200 million is due in January... balance \$217 million... in May... repay as scheduled... no further rollover"	Repay ICL \$417M (\$200M Jan/\$217M May)	Q1FY27 (May'26)	H	\$50M prepaid Dec'25; \$150M Jan, \$200M May — on time	NYT	\$50M prepaid; rest pending		
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	O&G Northeast exploratory wells	"first valve... in the Rudra region will be end of November spudded. Second well in Nagaland... in February"	Rudra spud Nov'25; Nagaland Feb'26	Q3/Q4 FY26	M	Q3: NE (SP-1) still delayed; spud pushed to ~end Mar'26	MISSED	~1 quarter+ slip	Env/local-govt approvals not complete	Regulatory
31 Oct 2025	Q2FY26	Q2FY26 Call (31 Oct'25)	Merchant power capacity (long-term)	"increase our merchant power capacity by 20 Gigawatts as we have guided previously by 2030"	+20 GW merchant power by 2030	2030	L	4.2 GW now; +10-12 GW plan being framed (Q3)	NYT	Long-dated aspiration		
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	Demerger effective date & listing	"targeting 1st of April as the effective date with listings in the same quarter... mid-to-end of May"	Effective 1 Apr'26; list by ~end May'26	Q1FY27 (Apr-May'26)	H	Pending (post-Q3 event)	NYT	Test Apr-May'26		
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	Q4FY26 EBITDA / FY26 record	"With our Quarter 4 performance likely to surpass Q3 levels... lifetime high annual EBITDA of over \$6 billion"	Q4 EBITDA > Rs 15,171 cr; FY26 > \$6bn	FY26 results (Apr'26)	H	Pending	NYT	Test Apr'26		
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	FY26 group deleveraging	"roughly about 0.8 to 1 billion will be deleveraging across the group in the current fiscal... closing the fiscal at about 1x"	FY26 deleverage \$0.8-1.0bn; VEDL ~1.0x	FY26 results (Apr'26)	H	Pending (OFS ~Rs 3,000 cr earmarked)	NYT	Test Apr'26		
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	Zinc India OFS / HZL stake	"launched Zinc India offer-for-sale... shareholding in HZL will be around 60.7% from 61.8%"	OFS ~1.1% HZL (~Rs 3,000 cr)	Immediate (Jan'26)	H	OFS launched 27 Jan, bids closed; ~1.1% / ~Rs 3,000 cr	MET	Delivered as stated		
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	Captive alumina mix ramp	"60% in Q3 captive, 70% in Q4, and going forward, Q1, Q2, it should be 80%"	Captive alumina 70% Q4FY26; 80% Q1FY27	Q4FY26 / Q1FY27	M	Pending	NYT	Test Apr-Jul'26		
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	Q4FY26 aluminium production	"we did about 800 KT in Q3, and we are expecting 900 KT plus in Q4"	Aluminium 900 kt+ in Q4FY26	Q4FY26 results (Apr'26)	M	Pending	NYT	Test Apr'26		
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	BALCO smelter pot ramp	"increase to about 1 lakh ton by this March end, and then next three to six months... rest of the pots"	BALCO 100 kt by Mar'26; full ramp +3-6 mo	Q4FY26 / 1HFY27	M	Pending (20 pots live at Q3)	NYT	Test Apr'26 onward		
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	Aluminium capacity expansion	"get to 2.8 million tons... post BALCO ramp... close the gap from 2.8 to 3 million tons... over the next 18-months"	Al capacity 2.8 Mnt then 3.0 Mnt (~18 mo)	~FY27/FY28	M	Pending	NYT	Test ~FY27-28		
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	Hot-metal cost trajectory	"next quarter... costs will remain flat... Coming to Quarter 1... a \$50-\$60 cost reduction"	Q4 cost flat; Q1FY27 -\$50-60/t	Q4FY26 / Q1FY27	M	Pending	NYT	Test Apr-Jul'26		
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	Q1FY27 alumina cost	"as we go into Q1, you will see a cost sub-\$750"	Alumina CoP < \$750/t by Q1FY27	Q1FY27 results (Jul'26)	M	Pending	NYT	Test Jul'26		
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	Power capacity expansion	"4.2 gigawatt. This is expected to go to around 4.8 gigawatt by end of H1 of the next year"	Power capacity 4.2 -> 4.8 GW by H1FY27	H1FY27 (Sep'26)	M	Pending	NYT	Test ~Oct'26		
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	O&G ASP first volumes	"to pick up the first volumes... in the period of next three months... additional reserves of 50 million barrels"	ASP first oil in ~3 mo; +50 mn bbl	Q1FY27 (~Apr'26)	M	Pending	NYT	Test ~Apr'26		
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	O&G production recovery	"we expect the next year to stabilize everything and to grow to at least 90,000, and then... ultimate target of 150,000"	O&G ~90 kboepd in FY27; ult. 150 kboepd	FY27+	M	Pending (Q3 84.9 kboepd)	NYT	Test through FY27		
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	O&G Ambe (West offshore) field	"that project will be commissioned and startup this financial year 27 in Quarter 4... around 15,000 in March next year"	Ambe live Q4FY27; ~15 kboepd by Mar'27	Q4FY27 (Mar'27)	M	Pending	NYT	Test Mar'27		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
29 Jan 2026	Q3FY26	Q3FY26 Call (29 Jan'26)	VRL FY27 debt servicing	"interest... almost 450 million... principal, the actual debt is 450 and ICL 200, 650... self-funded to a 5% dividend and routine brand fee"	VRL FY27: \$650M principal + \$450M interest	FY27	M	Pending	NYT	Test through FY27		

What qualifies as a commitment

Only **measurable** statements — a number, %, ratio, ₹/\$ figure or a dated milestone. Generic or aspirational commentary is rejected. One promise per row, with a verbatim ≤ 25 -word quote.

How status is judged (deterministic rules — the model only retrieves)

- **MET** — delivered or exceeded the target
- **PARTIAL** — close but below target / a milestone slipped within grace
- **MISSED** — failed, incl. a date the company later pushed past the promised window
- **NYT** — outcome not yet reported within the verification window (excluded from scoring)

Confidence & the credibility score

H = hard numeric · **M** = directional · **L** = aspirational. Credibility = confidence-weighted delivery over testable promises (MET=1, PARTIAL=0.5, MISSED=0; H=1.0, M=0.8, L=0.6); bands A ≥ 75 B ≥ 60 C ≥ 45 D ≥ 30 E<30.

The verification window

Outcomes are verifiable only through **Q3FY26** (reported 2026-01-29). Later targets are therefore **NYT**. *Hand-verified reference ledger.*

Source documents

Q1FY26 Presn

2025-07-31 · both

Q2FY26 Call

2025-10-31 · guidance

Q2FY26 Presn

2025-10-31 · both

Q3FY26 Call

2026-01-29 · both

Q3FY26 Presn

2026-01-29 · both
