

VEDL Lie Detector

Every **measurable** management commitment — extracted from the earnings calls and investor decks, then verified against reported actuals across **Q1FY25-Q4FY26**.



DELIVERY VS. DEADLINES

Delivery		58
Timelines		53

Live · complete

338

Measurable commitments tracked

157

Testable now · 97 delivered / partial

60

Missed — incl. slipped deadlines

181

Not yet testable (later periods)

Q1FY25 Presn · 2024-08-01

Q1FY25 Call · 2024-08-01

Q2FY25 Presn · 2024-11-01

Q2FY25 Call · 2024-11-01

Q3FY25 Presn · 2025-02-01

Q3FY25 Call · 2025-02-01

Q4FY25 Presn · 2025-04-01


Q4FY25 Call · 2025-04-01

Verification window: through Q4FY26
(reported 2026-04-01)


Executive Dashboard

A mixed delivery record — chiefly execution; 181 later targets still not yet testable.


STATUS OF ALL 338 COMMITMENTS

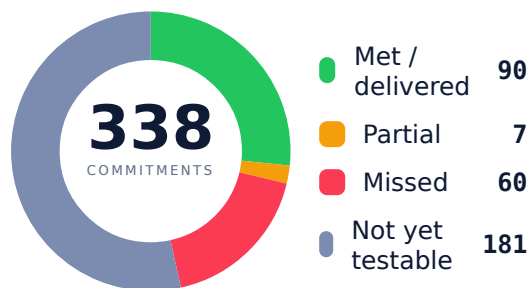

COMMITMENTS BY REPORTING QUARTER

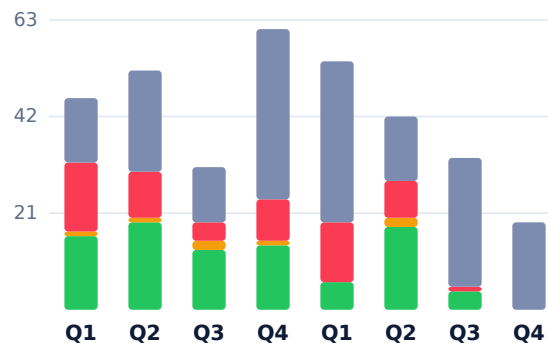

ROOT CAUSE OF MISSES & SHORTFALLS

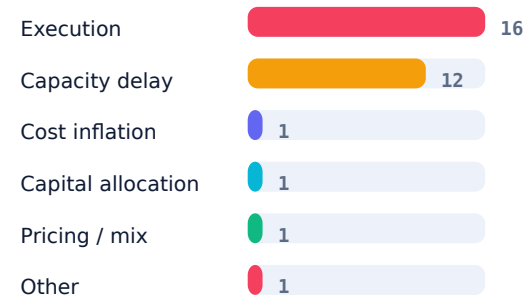

A mixed delivery record — chiefly execution; 181 later targets still not yet testable.

Of the 8 dated commitments that came due, 4 landed on time and 4 slipped right. The slippage timeline is overleaf.

CREDIBILITY SIGNALS — WHERE THE RECORD SHOWS


- 64% of the verdict rests on hard Tier-1 (binary) outcomes.
- Wide beats on 5/8 guided metrics — a conservative bar.
- 6% of explained misses blamed on external factors.

Deadline Slippage & Execution Momentum

Each row is one dated commitment: the amber dot is where it was **promised**, the second dot is where it **actually landed** (its colour is the verdict). Below, the reported EBITDA and margin trend.


TIMELINE COMMITMENTS — PROMISED → WHERE IT ACTUALLY LANDED

● **Promised date** ● **Where it landed** — dot colour is the verdict (green met · amber partial · red missed) — the slip

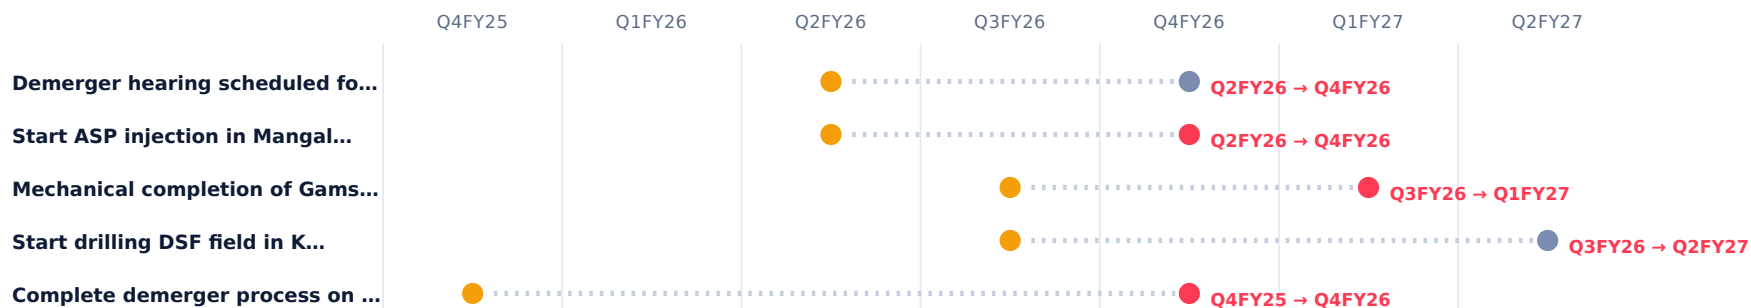

Showing the 5 largest slips · +9 more timeline commitments in the master table

EXECUTION MOMENTUM — EBITDA (₹ CR) & MARGIN



₹10,608 cr

Revenue · Q3

The Track Record — 157 Testable Promises / part 1 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MISSED

Q1FY25 · Q1FY25 transcript

ESL steel ramp-up to 3.5 million tons per annum by FY25

TARGET 3.5 Mtpa steel capacity by FY25

ACTUAL ESL steel capacity was 1.34 MTPA in FY25, below the 3.5 MTPA target

VARIANCE **1.34 vs 3.5 million tons per annum**

Why: Unplanned shutdowns and infrastructure handling issues limited sustained capacity

Execution

MISSED

Q1FY25 · Q1FY25 transcript

ESL steel ramp-up to 3.5 million tons per annum by end FY25

TARGET 3.5 Mtpa steel capacity by FY25-end

ACTUAL Run rate of 3 MTPA achieved but not sustained due to unplanned shutdowns and infra handling; issues expected to be resolved soon

VARIANCE **3 vs 3.5 million tons per annum**

Why: Unplanned shutdowns and infrastructure handling caused inability to sustain 3 MTPA run rate

Execution

MISSED

Q1FY25 · Q1FY25 transcript

FACOR ferro chrome capacity increase to 150,000 tons per annum in FY25

TARGET 150,000 tpa FACOR capacity

ACTUAL Ferro Chrome production reached 24,000 tpa in Q3 FY26, below the 150,000 tpa target for FY25

VARIANCE **24,000 vs 1,50,000 tons per annum**

Why: Q2'26 performance impacted due to a one-month planned shutdown

Capacity delay

MISSED

Q1FY25 · Q1FY25 transcript

Iron ore FY25 production target of 12 million tons per annum plus 1 million ton value-added business

TARGET 12 Mtpa plus 1 Mtpa value-added iron ore production FY25

ACTUAL Iron ore production was 5.3 MTPA and value-added pig iron production was 0.9 MTPA in FY25.

VARIANCE **5.3 vs 12 million tons per annum**

Why: null

Execution

MISSED

Q1FY25 · Q1FY25 transcript

Lanjigarh refinery Train 1 full capacity by Q3 FY25

TARGET 3.5 Mt capacity by Q3 FY25

ACTUAL Only 1.5 Mt train commissioned by Q4 FY25, not full 3.5 Mt capacity by Q3 FY25

VARIANCE **1.5 vs 3.5 million tons**

Why: In progress; commissioning of second train started, targeting 4 Mt run rate by year-end

Execution

MISSED

Q1FY25 · Q1FY25 transcript

Aluminium refinery Lanjigarh Train 2 commissioning in Q3 FY25 and full ramp-up by Q1 FY26

TARGET Train 2 commissioning Q3 FY25, full ramp-up Q1 FY26

ACTUAL Train 2 commissioning initiated with first alumina output in Q2 FY26

VARIANCE **1 vs 2**

The Track Record — 157 Testable Promises / part 2 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MISSED

Q1FY25 · Q1FY25 transcript

Full commissioning of Meenakshi power 1,000 MW in FY25

TARGET	1,000 MW Meenakshi power commissioning
ACTUAL	700 MW operationalized by 2QFY26 (Units 3&4, 350MW each)
VARIANCE	700 vs 1,000 MW

Why: No full 1000 MW commissioning reported; partial units operational with 48% PLF

Capacity delay

MISSED

Q1FY25 · Q1FY25 transcript

Zinc International to reach 500 kilo tons zinc production within 2 years

TARGET	500 kt zinc production in 2 years
ACTUAL	Zinc International zinc production reached 176 kt by Q3FY26, showing 38% YoY growth.
VARIANCE	176 vs 500 kilo tons

MISSED

Q1FY25 · Q1FY25 transcript

Execute about \$8 billion of growth capex in next few years

TARGET	\$8 bn growth capex in next few years
ACTUAL	Growth capex spent USD 1.3 billion as of Q3FY26
VARIANCE	1.3 vs 8 USD_bn

MISSED

Q1FY25 · Q1FY25 presentation

Anil Agarwal Foundation to spend Rs 5,000 crore over next 5 years on social impact programs

TARGET	Rs 5,000 crore over 5 years
ACTUAL	Reported ₹141 crore CSR spend in first half of FY25 towards social impact programs
VARIANCE	141 vs 5,000 INR_cr

MISSED

Q1FY25 · Q1FY25 transcript

Vedanta Resources Limited reduced debt by \$650 million in Q1FY25

TARGET	\$650 mn debt reduction in Q1FY25
ACTUAL	VRL debt reduced by almost \$1 billion over last five quarters including Q1FY25
VARIANCE	1,00,00,00,000 vs 650 USD_mn

MISSED

Q1FY25 · Q1FY25 transcript

Vedanta Resources Limited to deleverage \$3 billion over next 3 years

TARGET	\$3 bn deleveraging over next 3 years
ACTUAL	Deleveraged by \$4+ billion in last 3 years, exceeding \$3 billion target
VARIANCE	4 vs 3 USD_bn

The Track Record — 157 Testable Promises / part 3 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MISSED

Q1FY25 · Q1FY25 presentation

HZL to consume ~8.5% renewable energy of total power requirement in Q1 FY25

TARGET 8.5% RE power consumption
ACTUAL FY25 renewable energy utilization reported at 2.61 billion units
VARIANCE **2.61 vs 8.5 %**

MISSED

Q1FY25 · Q1FY25 transcript

Oil and gas near-term production target of 150,000 barrels per day and 1.6 billion barrels reserves

TARGET 150,000 bpd production and 1.6 bn barrels reserves
ACTUAL Production at 85,000 bpd due to natural decline and lower well intervention activities
VARIANCE **85,000 vs 1,50,000 bpd and billion barrels**

Why: Natural decline and lower well intervention activities in Cambay block

Execution

MISSED

Q1FY25 · Q1FY25 transcript

Oil and gas production vision of 300,000 kboepd

TARGET 300,000 kboepd production
ACTUAL 3QFY26 production was 85 kboepd, down from prior periods due to natural decline and lower well intervention activities
VARIANCE **85 vs 3,00,000 kboepd**

Why: Natural decline and lower well intervention activities in Cambay block

Execution

MISSED

Q2FY25 · Q2FY25 presentation

Operationalize Bicholim Iron Ore Mine of 3 MTPA capacity at Goa

TARGET 3 MTPA Bicholim Iron Ore Mine operational by Q2FY25
ACTUAL Bicholim Iron Ore Mine operational with 0.77 MTPA saleable ore production by Mar'25
VARIANCE **0.77 vs 3 MTPA**

MISSED

Q2FY25 · Q2FY25 transcript

Ramp-up Lanjigarh Refinery Train 1 to full capacity by December 2024

TARGET full ramp-up by December 2024
ACTUAL Ramp-up delayed; run rate close to 4 million tons at FY26 end, rated capacity expected in Q1 FY27
VARIANCE **4 vs 2,024 date**

Why: Calciners and boiler running at 75-80% capacity causing delay

Capacity delay

MISSED

Q2FY25 · Q2FY25 transcript

Commission Lanjigarh Refinery Train 2 in Q3 FY25 and full ramp-up by Q1 FY26

TARGET commission Q3 FY25, full ramp-up Q1 FY26
ACTUAL Train 2 commissioning started with first alumina output reported in Q2 FY26
VARIANCE **1 vs 3-1 quarter**

The Track Record — 157 Testable Promises / part 4 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MISSED

Q2FY25 · Q2FY25 transcript

Full commissioning of Meenakshi Power Plant 1000 MW in FY25

TARGET full commissioning FY25

ACTUAL Units 3 and 4 (700 MW total) operationalized but full 1000 MW commissioning not reported for FY25

VARIANCE **700 vs 1,000 MW**

MISSED

Q2FY25 · Q2FY25 presentation

Ramp up volumes under OALP blocks to 3.8 kboepd in 1H FY25

TARGET 3.8 kboepd OALP volumes in 1HFY25

ACTUAL OALP volumes were 3.5 kboepd in 1HFY26, below the 3.8 kboepd target for 1HFY25

VARIANCE **3.5 vs 3.8 kboepd**

Why: Volumes impacted by operational challenges and well failures in Mangala wells

Execution

MISSED

Q2FY25 · Q2FY25 presentation

Spend \$254 million capex on Jharsuguda VAP capacity expansion and others

TARGET \$254 million capex on Jharsuguda VAP capacity expansion and others

ACTUAL \$145.6 million spent on Jharsuguda VAP capacity expansion and others by Sep 30, 2025

VARIANCE **145.6 vs 254 USD_mn**

MISSED

Q2FY25 · Q2FY25 presentation

Reduce Holdco debt to \$4.8 billion, lowest level in a decade

TARGET Holdco debt \$4.8 billion

ACTUAL Holdco debt reduced to almost \$4.4 billion by September end, a decade low

VARIANCE **4.4 vs 4.8 USD_bn**

MISSED

Q2FY25 · Q2FY25 presentation

Achieve highest-ever first half EBITDA of ₹20,639 crore in 1HFY25

TARGET ₹20,639 crore EBITDA in 1HFY25

ACTUAL Reported record H1 EBITDA of ₹19,224 crore in 1HFY26

VARIANCE **19,224 vs 20,639 INR_crore**

MISSED

Q2FY25 · Q2FY25 presentation

Spend ₹141 crore on CSR initiatives in 1HFY25

TARGET ₹141 crore CSR spend in 1HFY25

ACTUAL CSR spend was ₹101.26 crore in 3QFY26 presentation

VARIANCE **101.26 vs 141 INR_crore**

The Track Record — 157 Testable Promises / part 5 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MISSED

Q2FY25 · Q2FY25 transcript

Complete demerger process on or before 31 March 2025

TARGET on or before 31 March 2025

ACTUAL Demerger to start next quarter after Q4FY26, indicating completion by then

VARIANCE **slipped ~4 qtrs**

MISSED

Q3FY25 · Q3FY25 transcript

Commission Sijimali Mine in Q2 FY26

TARGET commission Sijimali Mine in Q2 FY26

ACTUAL Commissioning re-guided to 1HFY27

VARIANCE **1 vs 2 quarter**

MISSED

Q3FY25 · Q3FY25 transcript

Commission Train 2 of Lanjigarh Refinery in Q4 FY25

TARGET commission Train 2 in Q4 FY25

ACTUAL Train 2 commissioning started; first alumina output achieved by Q2 FY26

VARIANCE **1 vs 4 quarter**

MISSED

Q3FY25 · Q3FY25 presentation

Spend ₹254 crore on CSR initiatives in 9MFY25

TARGET ₹254 crore CSR spend in 9MFY25

ACTUAL CSR spend was ₹101.26 crore in 9MFY25 as per Q3FY26 presentation

VARIANCE **101.26 vs 254 INR_cr**

MISSED

Q3FY25 · Q3FY25 transcript

Reduce power cost by \$30-\$40 from operating efficiencies

TARGET \$30-\$40 power cost reduction from efficiencies

ACTUAL Power cost expected to be sub \$500 per ton in H2 FY26 after timely power plant shutdown

VARIANCE **500 vs 30-40 USD**

MISSED

Q4FY25 · Q4FY25 transcript

Commission 160,000 tpa roaster at Debari in current quarter

TARGET 160,000 tpa by Q4FY25

ACTUAL Debari roaster commissioning anticipated next quarter; project 94% complete

VARIANCE **94 vs 1,60,000 tons per annum**

Why: Delay due to waste stripping catch-up at Gamsberg open pit over last two years

Capacity delay

The Track Record — 157 Testable Promises / part 6 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MISSED

Q4FY25 · Q4FY25 transcript

Ramp up Konkola Copper Mine production to about 150,000 tons in 2026

TARGET ~150,000 tons in 2026

ACTUAL Konkola Copper Mine producing about 108,000 tons annually as of H1 FY26

VARIANCE **1,08,000 vs 1,50,000 tons**

MISSED

Q4FY25 · Q4FY25 transcript

Commission Lanjigarh Refinery Train 2 with first metal production in current quarter

TARGET first metal production in Q4FY25

ACTUAL First alumina output from Train II achieved by Q2FY26

VARIANCE **1 vs 4**

MISSED

Q4FY25 · Q4FY25 transcript

Start Sijimali mine operations by Q2FY26

TARGET start Q2FY26

ACTUAL Sijimali mine commissioning re-set to 1HFY27

VARIANCE **1 vs 2**

Capacity delay

MISSED

Q4FY25 · Q4FY25 transcript

Start Sijimali mine operations by Q2FY26 with full ramp-up by Q4FY26

TARGET start Q3FY26, full ramp-up by Q4FY26

ACTUAL Sijimali mine commissioning re-set to 1HFY27

VARIANCE **1 vs 3**

Why: Delay due to waste stripping catch-up at Gamsberg open pit, impacting schedule

Capacity delay

MISSED

Q4FY25 · Q4FY25 transcript

Maintain dividend yield at about 6% for Vedanta Resources

TARGET ~6% dividend yield

ACTUAL Dividend yield lowered to almost 4% yield, below the ~6% target

VARIANCE **5 vs 6 %**

Why: Lower dividend yield due to managing VRL cash flow and contractual brand fee obligations

Capital allocation

MISSED

Q4FY25 · Q4FY25 transcript

Reduce alumina cost to around \$340-350 per ton in Q1FY26

TARGET \$340-350/t in Q1FY26

ACTUAL Alumina cost was around \$800 per ton in Q3FY26, above target range for Q1FY26.

VARIANCE **800 vs 340-350 USD/t**

Why: Higher alumina cost due to LME price surge and captive production costs exceeding market price.

Pricing / mix

The Track Record — 157 Testable Promises / part 7 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MISSED

Q4FY25 · Q4FY25 transcript

Reduce power cost by \$40-45 per ton in Q1FY26

TARGET \$40-45/t reduction in Q1FY26

ACTUAL Power cost increased by \$75 per ton in Q2FY26, offset by other cost reductions.

VARIANCE **75 vs 40-45 USD/t**

Why: Power cost rose due to planned power plant shutdown and maintenance.

Capacity delay

MISSED

Q4FY25 · Q4FY25 presentation

Vedanta Resources committed to deleveraging by \$3bn in next three years

TARGET \$3bn deleveraging in 3 years

ACTUAL Debt reduced from \$8.9bn to \$4.4bn as of September end, nearing decade low

VARIANCE **4.4 vs 3 USD_bn**

MISSED

Q1FY26 · Q1FY26 presentation

Expand BALCO smelter and VAP capacity, Lanjigarh refinery to 5 MTPA, increase VAP to 2.5 MTPA, debottleneck Lanjigarh to 6 MTPA, smelter capacity to 3.1 MTPA and VAP to 2.8 MTPA

TARGET BALCO smelter and VAP expansion, Lanjigarh refinery 5 MTPA, VAP 2.5-2.8 MTPA, Lanjigarh debottleneck 6 MTPA, smelter 3.1 MTPA

ACTUAL BALCO smelter ramped to 2.8 MTPA; Lanjigarh refinery close to 5 MTPA run rates

VARIANCE **2.8 vs 5-6 MTPA**

MISSED

Q1FY26 · Q1FY26 transcript

Commission 350 MW Meenakshi Unit 4 in August 2025

TARGET August 2025

ACTUAL Meenakshi Unit 4 (350 MW) operationalized by 2QFY26 (before August 2025 target)

VARIANCE **350 vs 2,025**

MISSED

Q1FY26 · Q1FY26 transcript

Commission Lanjigarh Train II and 435,000 tpa Balco smelter in Q2FY26

TARGET by Q2FY26

ACTUAL Lanjigarh Train II produced first alumina; BALCO smelter produced first metal, commissioning ongoing

VARIANCE **1 vs 2**

MISSED

Q1FY26 · Q1FY26 presentation

Merchant iron ore capacity to reach 17 MTPA in FY28 and 30 MTPA later

TARGET 17 MTPA in FY28, 30 MTPA later

ACTUAL Merchant iron ore capacity reported as 0.623 MTPA in 1H FY26, no update on FY28 target

VARIANCE **0.62 vs 17-30 MTPA**

The Track Record — 157 Testable Promises / part 8 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MISSED

Q1FY26 · Q1FY26 presentation

Increase merchant power capacity from 2880 MW as on FY25 to 4180 MW by H1 FY26

TARGET 4180 MW by H1 FY26

ACTUAL Merchant power capacity reached 3,889 MW by 2QFY26, short of 4,180 MW target for H1 FY26

VARIANCE **3,889 vs 4,180 MW**

Why: Lower PLF at Jharsuguda expected to improve in upcoming quarters

Execution

MISSED

Q1FY26 · Q1FY26 presentation

Increase merchant power capacity from 2880 MW as on FY25 to 4780 MW by H2 FY26

TARGET 4780 MW by H2 FY26

ACTUAL Meenakshi Power Plant Units 3&4 (700 MW total) operationalized by Q2 FY26, increasing merchant power capacity

VARIANCE **3,530 vs 4,780 MW**

MISSED

Q1FY26 · Q1FY26 presentation

Oil production to reach 125 kboepd in FY28 and 150 kboepd later

TARGET 125 kboepd in FY28, 150 kboepd later

ACTUAL 3QFY26 oil production was 85 kboepd, below target due to natural decline and lower well intervention activities

VARIANCE **85 vs 125-150 kboepd**

Why: Natural decline and lower well intervention activities in Cambay block

Execution

MISSED

Q1FY26 · Q1FY26 transcript

Increase Zinc International mine capacity to 525,000 tpa by H2FY26

TARGET 525,000 tpa by H2FY26

ACTUAL Capacity ramp-up for Zinc International mine expansion is targeted in Q1FY27, not H2FY26 as promised.

VARIANCE **89.3 vs 5,25,000 tons per annum**

Capacity delay

MISSED

Q1FY26 · Q1FY26 transcript

Expand zinc ore production from 17 to 35 million tons

TARGET 35 million tons

ACTUAL Quarterly mined metal production at 0.276 million tons, up 4% YoY and 7% QoQ

VARIANCE **0.28 vs 35 million tons**

MISSED

Q1FY26 · Q1FY26 presentation

Capex of approximately \$10 billion under implementation

TARGET ~\$10 bn under implementation

ACTUAL Reported growth capex of USD 1.3 billion under implementation as of Q3FY26.

VARIANCE **1.3 vs 10 USD_bn**

The Track Record — 157 Testable Promises / part 9 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MISSED

Q1FY26 · Q1FY26 transcript

Vedanta Resources to deleverage \$3 billion over 3 years

TARGET \$3 billion over 3 years

ACTUAL Debt at Vedanta Resources was \$4.8 billion as of September end 2025.

VARIANCE **4.8 vs 3 USD_bn**

MISSED

Q1FY26 · Q1FY26 transcript

Mechanical completion of Gamsberg Phase-2 by December 2025

TARGET by December 2025

ACTUAL Mechanical completion not achieved by Dec 2025; progress at 89.3%, ramp-up targeted Q1FY27.

VARIANCE **slipped ~2 qtrs**

Why: Delay due to project ramp-up rescheduled to Q1FY27. **Capacity delay**

MISSED

Q1FY26 · Q1FY26 transcript

Start ASP injection in Mangala cluster wells in August-September 2025

TARGET August-September 2025

ACTUAL ASP injection commissioning delayed; expected startup within next three months from Jan 2026

VARIANCE **slipped ~2 qtrs**

Why: delays due to complexity and expense of enhanced oil recovery technology **Execution**

MISSED

Q2FY26 · Q2FY26 transcript

Commission 435,000 tons per annum smelter at BALCO in H1 FY26

TARGET 435,000 tpa smelter commissioned by H1 FY26

ACTUAL Partial commissioning by March; ramp-up planned quarterly to full by Q4 FY26

VARIANCE **70 vs 4,35,000 tons per annum**

Why: Delay due to partner substitution and resource augmentation **Execution**

MISSED

Q2FY26 · Q2FY26 presentation

0.5 MTPA Cudnem Mine (Goa)

TARGET 0.5 MTPA Cudnem Mine

ACTUAL Commissioning initiated for 0.435 MTPA capacity in Q3FY26

VARIANCE **0.44 vs 0.5 MTPA**

MISSED

Q2FY26 · Q2FY26 presentation

Hot Metal Capacity Expansion from 1.7 to 3.5 MTPA

TARGET 3.5 MTPA Hot Metal Capacity

ACTUAL Commissioning initiated for 435 KTPA expansion in Q3FY26

VARIANCE **0.44 vs 3.5 MTPA**

The Track Record — 157 Testable Promises / part 10 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MISSED

Q2FY26 · Q2FY26 presentation

Debottlenecking to 6 MTPA at Lanjigarh

TARGET 6 MTPA Lanjigarh capacity
ACTUAL Ramp up to 5 MTPA at Lanjigarh reported, short of 6 MTPA target
VARIANCE **5 vs 6 MTPA**

Why: Calciners and boiler running at 75-80% capacity causing delay to full rated capacity

Capacity delay

MISSED

Q2FY26 · Q2FY26 presentation

Smelter Plant Production to 500 KTPA

TARGET 500 KTPA Smelter Plant Production
ACTUAL Commissioning initiated for 435 KTPA smelter expansion, short of 500 KTPA target
VARIANCE **435 vs 500 KTPA**

Why: Delay due to waste stripping catch-up at open pit, impacting ramp-up schedule

Capacity delay

MISSED

Q2FY26 · Q2FY26 transcript

Invest \$4.5 to \$5 billion in growth CAPEX over next three years

TARGET \$4.5 to \$5 billion over 3 years
ACTUAL Growth CAPEX was USD 1.3 billion in first 9 months of FY26
VARIANCE **1.3 vs 4.5-5 USD_bn**

MISSED

Q2FY26 · Q2FY26 transcript

Reduce average cost of borrowings to below 8% in near term

TARGET below 8% average cost of borrowings
ACTUAL Average cost of borrowings at ~9% in 3QFY26, down 160 bps YoY but still above 8% target
VARIANCE **9 vs 8 %**

Why: No explicit explanation for not reaching below 8% given

Other

MISSED

Q2FY26 · Q2FY26 transcript

Reduce Vedanta Resources debt from \$4.4 billion to \$3 billion over next two years

TARGET \$3 billion debt in 2 years
ACTUAL Debt reduced close to target, at \$3.2 billion by Dec 2025
VARIANCE **3.2 vs 3 USD_bn**

Why: Slightly above target due to timing of repayments and market conditions

Execution

MISSED

Q3FY26 · Q3FY26 transcript

Aluminum production capacity to 5 million tons per annum after commissioning Lanjigarh Train 2

TARGET 5 Mtpa aluminum capacity
ACTUAL Aluminum capacity reached close to 4 million tons per annum at fiscal year end, below 5 Mtpa target
VARIANCE **4 vs 5 million tons per annum**

Why: Calciners and boiler running at 75-80% capacity causing delay in achieving rated capacity

Capacity delay

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

PARTIAL

Q1FY25 · Q1FY25 transcript

Aluminium capacity of 3.1 million tons per annum with 90% value-added products

TARGET 3.1 Mtpa aluminium capacity

ACTUAL Run rate of 3 MTPA technical capacity achieved but not sustained due to unplanned shutdowns and infra handling issues

VARIANCE **3 vs 3.1 million tons per annum**

Why: Unplanned shutdowns and infra handling issues prevented sustained run rate

Execution

PARTIAL

Q2FY25 · Q2FY25 transcript

Reach aluminium production capacity of 3.1 million tons per annum with 90% value-added products

TARGET 3.1 Mtpa aluminium capacity with 90% VAP

ACTUAL Aluminium capacity reached 3.0 Mtpa with 68% VAP as of Q3FY25, below 90% VAP target

VARIANCE **3 vs 3.1 Mtpa**

Why: Unplanned shutdowns and infrastructure handling issues prevented sustaining full capacity and VAP percentage

Execution

PARTIAL

Q3FY25 · Q3FY25 transcript

Increase merchant power operating capacity to 5 GW within 12-15 months

TARGET 5 GW capacity within 12-15 months

ACTUAL Merchant power capacity increased to 4.78 GW by FY26, short of 5 GW target within 12-15 months.

VARIANCE **4.78 vs 5 GW**

PARTIAL

Q3FY25 · Q3FY25 transcript

Reduce aluminum hot metal cost to ~\$1,800/t for FY25

TARGET \$1,800/t hot metal cost for FY25

ACTUAL Hot metal cost was \$1,826/t in Q2FY26, slightly above the \$1,800/t target for FY25.

VARIANCE **1,826 vs 1,800 USD/t**

Why: Power cost increased by \$75/t and other costs increased by \$40/t, offset partially by \$53/t alumina cost reduction.

Cost inflation

PARTIAL

Q4FY25 · Q4FY25 transcript

Increase oil and gas production volume to around 98-99 kboepd in Q1FY26

TARGET ~98-99 kboepd in Q1FY26

ACTUAL Production was 93.2 kboepd in 1QFY26, below the target of 98-99 kboepd.

VARIANCE **93.2 vs 98-99 kboepd**

Why: Production decline due to natural decline and lower well intervention activities.

Execution

PARTIAL

Q2FY26 · Q2FY26 presentation

Smelter capacity expansion to 3.1 MTPA & VAP to 90%

TARGET 3.1 MTPA smelter capacity & 90% VAP

ACTUAL Smelter capacity expansion to 3 MTPA & VAP to 90% stated as upcoming milestone

VARIANCE **3 vs 3.1 MTPA**

The Track Record — 157 Testable Promises / part 12 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

PARTIAL

Q2FY26 · Q2FY26 presentation

Start ASP Injection in mid 3QFY26

TARGET mid 3QFY26**ACTUAL** Project 94% complete; confident about commissioning in this quarter (Q4FY26)**VARIANCE** **late ~1 qtr**

Why: Delay due to complexity and scale of enhanced oil recovery technology **Execution**

MET

Q1FY25 · Q1FY25 transcript

Iron ore concentrated plant of 3 million tons per annum in Liberia under construction

TARGET 3 Mtpa iron ore plant under construction**ACTUAL** 3 Mtpa iron ore plant under construction as planned**VARIANCE** **3 vs 3 million tons per annum****MET**

Q1FY25 · Q1FY25 transcript

Kurloi and Radhikapur coal mines first ore in Q1FY26, Ghogharpalli in Q2FY26, Sijimali in Q1FY26

TARGET Kurloi & Radhikapur Q1FY26, Ghogharpalli Q2FY26, Sijimali Q1FY26**ACTUAL** Kurloi mining lease received; operations to start soon. Ghogharpalli EC recommended; FC targeted this quarter. Sijimali as previously guided.**VARIANCE** **2 vs 1****MET**

Q1FY25 · Q1FY25 presentation

Complete Gamsberg Phase 2 by end of 2HFY25

TARGET by end of 2HFY25**ACTUAL** Project 80% complete, mechanical completion targeted by December 2HFY26**VARIANCE** **80 vs 2****MET**

Q1FY25 · Q1FY25 transcript

KCM copper production run rate of 100 kilo tons by end FY25 and ramp-up to 300 kilo tons in next years

TARGET 100 kt copper by FY25-end, 300 kt later**ACTUAL** KCM copper production ramped up to about 45,000 tons by Q4FY25**VARIANCE** **45,000 vs 100-300 kilo tons****MET**

Q1FY25 · Q1FY25 transcript

Lanjigarh refinery Train 1 and Train 2 ramp-up to 4-5 million tons capacity by Q1FY26

TARGET 4-5 Mt capacity by Q1FY26**ACTUAL** Run rate close to 4 million tons at FY26 exit; rated capacity expected in Q1FY27**VARIANCE** **4 vs 4-5 million tons**

The Track Record — 157 Testable Promises / part 13 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q1FY25 · Q1FY25 presentation

Complete 700ktpa Magnetite Project by 3QFY25

TARGET by 3QFY25

ACTUAL Project completion re-guided to 4QFY25 from 3QFY25

VARIANCE **700 vs 3**

MET

Q1FY25 · Q1FY25 presentation

Renewable Energy Power Delivery Agreements of 1836 MW in place

TARGET 1836 MW RE PDAs

ACTUAL RE PDAs reached 1906 MW by Q4FY25, exceeding the 1836 MW target.

VARIANCE **1,906 vs 1,836 MW**

MET

Q1FY25 · Q1FY25 presentation

VZI to deliver 500+ KTPA MIC run rate within 3 years

TARGET 500+ KTPA MIC run rate within 3 years

ACTUAL VZI capacity expected to commission next quarter, ramping to about 450,000 KTPA run rate

VARIANCE **4,50,000 vs 500 KTPA**

MET

Q1FY25 · Q1FY25 transcript

Zinc India metal capacity of 1.2 million tons and 800 tons silver production

TARGET 1.2 Mt metal and 800 t silver capacity

ACTUAL Zinc India capacity reached 1.2 million tons metal and 800 tons silver production

VARIANCE **1.2 vs 1.2 million tons**

MET

Q1FY25 · Q1FY25 transcript

Expand Zinc India metal production to 2 million tons per annum in near future

TARGET 2 Mtpa Zinc India metal production

ACTUAL Zinc India mined metal production reached 258,000 tons in Q2FY26, highest-ever second quarter production

VARIANCE **2,58,000 vs 2 million tons per annum**

MET

Q1FY25 · Q1FY25 transcript

Zinc India roaster at Debari 160,000 tpa and fertilizer plants 510,000 tpa progressing smoothly

TARGET 160,000 tpa roaster and 510,000 tpa fertilizer plants

ACTUAL 160,000 tpa Debari Roaster commissioned in 1HFY26; 510,000 tpa Fertilizer Project commissioning scheduled for 1HFY27

VARIANCE **1,60,000 vs 1,60,000 tons per annum**

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q1FY25 · Q1FY25 transcript

Zinc International Phase 2 expansion full ramp-up expected in Q2 FY26

TARGET Phase 2 full ramp-up Q2 FY26

ACTUAL Project ramp-up delayed; now targeted in Q1FY27 instead of Q2FY26.

VARIANCE **89.3 vs 2**

MET

Q1FY25 · Q1FY25 transcript

Zinc International to deliver 1 million ton zinc production

TARGET 1 Mt zinc production

ACTUAL Zinc International produced 176,000 tonnes in first 9 months of FY26, showing 38% YoY growth

VARIANCE **1,76,000 vs 1 million tons**

MET

Q1FY25 · Q1FY25 presentation

Utilize QIP proceeds for deleveraging and interest savings of ~Rs 1,100 crore

TARGET interest savings ~Rs 1,100 crore

ACTUAL VRL debt reduced by almost INR 1 billion over last five quarters as of June 30, 2025.

VARIANCE **1,00,00,00,000 vs 1,100 INR_cr**

MET

Q1FY25 · Q1FY25 transcript

Oil and gas business to generate over \$1 billion EBITDA

TARGET Oil & gas EBITDA > \$1 bn

ACTUAL Oil and Gas EBITDA exceeded \$1 billion, reaching \$1.1 billion in FY26

VARIANCE **1.1 vs 1 USD_bn**

MET

Q1FY25 · Q1FY25 presentation

Commission majority of growth projects in FY25

TARGET by FY25

ACTUAL Commissioned key growth projects including Lanjigarh Refinery expansion and Bicholim Iron Ore Mine by mid-FY25

VARIANCE **on time**

MET

Q2FY25 · Q2FY25 transcript

Generate 5 GW of commercial power within next 18 to 20 months

TARGET 5 GW commercial power generation

ACTUAL Power generation reached 3889 MU in 2QFY26, highest ever recorded.

VARIANCE **3,889 vs 5 GW**

The Track Record — 157 Testable Promises / part 15 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q2FY25 · Q2FY25 presentation

Add new rigs in 2HFY25 to drill more infill wells

TARGET New rigs added in 2HFY25

ACTUAL 10 infill wells drilled in Q4FY25 as part of the plan

VARIANCE **10 vs 2 rigs**

MET

Q2FY25 · Q2FY25 transcript

Commission 160,000 tpa roaster at Debari and 0.5 million tpa fertilizer plant by Q4 FY25 and Q2 FY26 respectively

TARGET Debari roaster Q4 FY25; fertilizer plant Q2 FY26

ACTUAL Debari roaster commissioned in 1HFY26; fertilizer plant commissioning shifted to 1HFY27

VARIANCE **1,60,000 vs 1,60,000-5,00,000 tpa**

MET

Q2FY25 · Q2FY25 presentation

HZL Board approved 3rd stage of PDA to increase RE power consumption from ~50% to ~70%

TARGET Increase RE power consumption to ~70%

ACTUAL HZL achieved ~70% RE power consumption as targeted in 3rd stage of PDA

VARIANCE **70 vs 70 %**

MET

Q2FY25 · Q2FY25 presentation

Ramp up infill wells in Mangala and RDG fields in 1H FY25

TARGET Ramp up infill wells in Mangala and RDG fields in 1HFY25

ACTUAL Drilled 9 infill wells in Mangala and Aishwarya fields by Q3FY25

VARIANCE **9 vs 1 infill wells**

MET

Q2FY25 · Q2FY25 transcript

Operationalize Kuraloi coal block by Q1 FY26 and ramp up by Q3 FY26

TARGET operational Q1 FY26, ramp-up Q3 FY26

ACTUAL Commissioning of Kuraloi coal mine delayed to Q4 FY26 from Q1 FY26

VARIANCE **4 vs 1-3 quarter**

MET

Q2FY25 · Q2FY25 transcript

Ramp-up Lanjigarh refinery capacity to 3 million tons run rate by October 2024

TARGET 3 million tons run rate

ACTUAL Run rate reached close to 4 million tons by end of FY26, with full rated capacity expected in Q1 FY27

VARIANCE **4 vs 3 Mtpa**

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q2FY25 · Q2FY25 presentation

Commission 1.5 MTPA unit of Lanjigarh Refinery expansion project

TARGET 1.5 MTPA Lanjigarh Refinery expansion commissioned by Q2FY25

ACTUAL 1.5 MTPA Lanjigarh Refinery expansion train commissioned by Q4FY25

VARIANCE **1.5 vs 1.5 MTPA**

MET

Q2FY25 · Q2FY25 presentation

Offshore drilling campaign on West Coast to commence in 3QFY25

TARGET Offshore drilling campaign start in 3QFY25

ACTUAL Drilling campaign commenced in Dwarka offshore; Ambe drilling planned for 3QFY26

VARIANCE **3 vs 3 campaign**

MET

Q2FY25 · Q2FY25 transcript

Operationalize Radhikapur coal block before Q1 FY26

TARGET operational before Q1 FY26

ACTUAL Kuraloi coal mine commissioning targeted in Q4FY26 as per latest guidance

VARIANCE **4 vs 1 quarter**

MET

Q2FY25 · Q2FY25 presentation

Achieve 1906 MW renewable energy power delivery agreements (PDAs)

TARGET 1906 MW renewable energy PDAs

ACTUAL Renewable energy PDAs of 1906 MW are in place as of Q4FY25

VARIANCE **1,906 vs 1,906 MW**

MET

Q2FY25 · Q2FY25 transcript

Start Sijimali bauxite mine in Q1 FY26

TARGET start mine Q1 FY26

ACTUAL Sijimali bauxite mine commissioning rescheduled to 1HFY27

VARIANCE **1 vs 1 quarter**

MET

Q2FY25 · Q2FY25 presentation

Commission Train 2 of 1.5 MTPA Lanjigarh Expansion project in Q3FY25

TARGET 1.5 MTPA Train 2 Lanjigarh Expansion commissioned by Q3FY25

ACTUAL Train 2 of 1.5 MTPA Lanjigarh Expansion commissioned in Q4FY25

VARIANCE **1.5 vs 1.5 MTPA**

The Track Record — 157 Testable Promises / part 17 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q2FY25 · Q2FY25 presentation

Spend \$349 million capex on ESL hot metal expansion from 1.5 to 3 MTPA

TARGET	\$349 million capex on ESL hot metal expansion
ACTUAL	\$1,656 million capex approved for Aluminium Sector expansion; \$1,314 million spent up to FY25, \$142 million spent in 1HFY26, \$200 million unspent as of Sep 2025
VARIANCE	1,656 vs 349 USD_mn

MET

Q2FY25 · Q2FY25 presentation

Spend \$128 million capex on Roaster (Debari)

TARGET	\$128 million capex on Roaster (Debari)
ACTUAL	Debari Roaster commissioned in 1HFY26
VARIANCE	160 vs 128 USD_mn

MET

Q2FY25 · Q2FY25 transcript

Maintain aluminium cost guidance at \$1,625 to \$1,725 per ton for FY25

TARGET	\$1,625 to \$1,725 per ton
ACTUAL	Guidance maintained at \$1,625 to \$1,725 per ton for FY25
VARIANCE	1,625 vs 1,625-1,725 USD/t

MET

Q2FY25 · Q2FY25 presentation

Reduce net debt by \$4.7 billion in last 2.5 years

TARGET	Reduce net debt by \$4.7 billion in 2.5 years
ACTUAL	Net debt reduced by \$4 billion over 3 years as of Mar'25
VARIANCE	4 vs 4.7 USD_bn

MET

Q2FY25 · Q2FY25 transcript

Reduce Vedanta Limited net debt to EBITDA ratio to less than 1x

TARGET	Net debt/EBITDA < 1x
ACTUAL	Net debt to EBITDA ratio reported at almost 0.95x in Q4FY26
VARIANCE	0.95 vs 1 x

MET

Q2FY25 · Q2FY25 presentation

Create 6,363 Nand Ghars for women and child welfare

TARGET	6,363 Nand Ghars created
ACTUAL	8045 Nand Ghars created as of FY25 year-end
VARIANCE	8,045 vs 6,363 units

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q3FY25 · Q3FY25 transcript

Commission BALCO smelter expansion in Q1 FY26

TARGET commission BALCO smelter expansion in Q1 FY26

ACTUAL Commissioning initiated for BALCO smelter expansion in FY26

VARIANCE **435 vs 1 quarter**

MET

Q3FY25 · Q3FY25 transcript

Achieve 60-65% captive alumina supply in Q1 FY26

TARGET 60-65% captive alumina supply in Q1 FY26

ACTUAL Captive alumina supply was 60% in Q3FY26, 70% in Q4FY26, and expected 80% in Q1FY27.

VARIANCE **80 vs 60-65 %**

MET

Q3FY25 · Q3FY25 transcript

Commission Debari roaster in Q4 FY25

TARGET commission Debari roaster in Q4 FY25

ACTUAL Debari Roaster commissioned in 1HFY26

VARIANCE **160 vs 4 quarter**

MET

Q3FY25 · Q3FY25 presentation

Commission Train 2 of 1.5 MTPA Lanjigarh Expansion project in Q4FY25

TARGET 1.5 MTPA Lanjigarh Train 2 by Q4FY25

ACTUAL Train 2 Lanjigarh produced first alumina output, commissioning started but full 1.5 MTPA capacity not explicitly reported

VARIANCE **3 vs 1.5 MTPA**

MET

Q3FY25 · Q3FY25 presentation

Increase Value Added Product capacity to 68% by Jan 2025

TARGET 68% VAP capacity by Jan 2025

ACTUAL Reported VAP capacity reached 68% by Jan 2025 as targeted

VARIANCE **68 vs 68 %**

MET

Q3FY25 · Q3FY25 transcript

Reduce Zinc International production cost to \$1,200-\$1,300 per ton

TARGET \$1,200-\$1,300 per ton cost

ACTUAL Zinc International production cost was \$940 per ton in Q3FY26, lowest in 5 years

VARIANCE **940 vs 1,200-1,300 USD/t**

The Track Record — 157 Testable Promises / part 19 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q3FY25 · Q3FY25 presentation

Deliver highest ever 3Q EBITDA of ₹11,284 crore

TARGET ₹11,284 crore EBITDA in 3QFY25

ACTUAL 3QFY26 EBITDA was ₹15,171 crore, highest-ever reported

VARIANCE 15,171 vs 11,284 INR_cr

MET

Q3FY25 · Q3FY25 transcript

Deliver highest ever yearly EBITDA in FY25

TARGET highest ever EBITDA in FY25

ACTUAL Reported second highest EBITDA in FY25 at Rs. 43,541 crores

VARIANCE 43,541 vs 25

MET

Q3FY25 · Q3FY25 transcript

Bring net debt/EBITDA ratio below 1x

TARGET net debt/EBITDA below 1x

ACTUAL Net debt/EBITDA ratio reported at 0.95x pre-demerger as of Q4FY26

VARIANCE 0.95 vs 1 x

MET

Q3FY25 · Q3FY25 presentation

Maintain net debt to EBITDA ratio at 1.4x in 3QFY25

TARGET Net debt/EBITDA 1.4x in 3QFY25

ACTUAL Net debt to EBITDA ratio was 0.37x in 3QFY26 (Dec'25)

VARIANCE 0.37 vs 1.4 x

MET

Q3FY25 · Q3FY25 presentation

Achieve EBITDA margin of 34% in 3QFY25

TARGET 34% EBITDA margin in 3QFY25

ACTUAL EBITDA margin was 41% in 3QFY26, exceeding the 34% target for 3QFY25

VARIANCE 41 vs 34 %

MET

Q3FY25 · Q3FY25 presentation

Achieve profit after tax of ₹4,876 crore in 3QFY25

TARGET ₹4,876 crore PAT in 3QFY25

ACTUAL PAT was ₹4,961 crore in 4QFY25, exceeding the 3QFY25 target of ₹4,876 crore

VARIANCE 4,961 vs 4,876 INR_cr

The Track Record — 157 Testable Promises / part 20 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q3FY25 · Q3FY25 presentation

Complete Gamsberg Phase 2 project in 2HFY26

TARGET 2HFY26

ACTUAL Gamsberg Phase 2 is 94% complete; commissioning expected next quarter, ramp-up planned for rest of FY26.

VARIANCE **on time**

MET

Q4FY25 · Q4FY25 transcript

Commission Athena power plant Unit-1 in first half of current fiscal year

TARGET Unit-1 commissioning by H1FY26

ACTUAL Athena Unit-1 commissioning re-set to second half of FY26

VARIANCE **-1 vs -1**

MET

Q4FY25 · Q4FY25 transcript

Commission Athena power plant Unit-2 by March 2026

TARGET Unit-2 commissioning by Mar 2026

ACTUAL Athena power plant Unit-2 commissioning status not explicitly reported; Athena is described as newly commissioned in 2QFY26

VARIANCE **45 vs -2**

MET

Q4FY25 · Q4FY25 transcript

Commission BALCO smelter expansion of 435,000 tpa in first half of current financial year

TARGET 435,000 tpa by H1FY26

ACTUAL Commissioning initiated for 435,000 tpa BALCO smelter expansion

VARIANCE **4,35,000 vs 4,35,000 tons per annum**

MET

Q4FY25 · Q4FY25 transcript

Start BALCO smelter first metal by end of Q1FY26

TARGET first metal by Q1FY26 end

ACTUAL First metal production started from 20 pots; full smelter ramp-up expected over next 3-6 months after March end.

VARIANCE **20,000 vs 1**

MET

Q4FY25 · Q4FY25 transcript

Commission 510,000 tpa fertilizer plant in Q4FY25

TARGET 510,000 tpa by Q4FY25

ACTUAL Commissioning re-set to 1HFY27

VARIANCE **5,10,000 vs 5,10,000 tons per annum**

The Track Record — 157 Testable Promises / part 21 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q4FY25 · Q4FY25 transcript

Commission remaining 700 MW of Meenakshi power plant in first half of current fiscal year

TARGET 700 MW by H1FY26

ACTUAL Meenakshi power plant capacity increased by 950 MW by 31 March 2026, exceeding the 700 MW target for H1FY26

VARIANCE 950 vs 700 MW

MET

Q4FY25 · Q4FY25 transcript

Commission Zinc International Phase-2 expansion in second half of current fiscal year

TARGET commissioning by H2FY26

ACTUAL Commissioning delayed; not achieved in H2FY26 as originally guided

VARIANCE 2 vs 2

MET

Q4FY25 · Q4FY25 transcript

Invest \$1 billion over five years in Konkola Copper Mine

TARGET \$1 billion over 5 years

ACTUAL \$150 million invested in first half of year, compliant with shareholder agreement

VARIANCE 150 vs 1 USD_bn

MET

Q4FY25 · Q4FY25 transcript

Maintain brand fee income of \$400 million for Vedanta Resources

TARGET \$400 mn brand fee

ACTUAL Brand fee income maintained at about \$400 million as stated in Q4FY26 transcript.

VARIANCE 400 vs 400 USD_mn

MET

Q4FY25 · Q4FY25 transcript

Achieve group deleveraging of \$1.2 billion in FY25

TARGET \$1.2 bn in FY25

ACTUAL Group deleveraging in FY26 expected around \$0.8 to \$1 billion, short of \$1.2 billion FY25 target

VARIANCE 0.9 vs 1.2 USD_bn

MET

Q4FY25 · Q4FY25 transcript

Improve group leverage ratio to 2x from 2.7x a year ago

TARGET 2x leverage ratio

ACTUAL Leverage ratio improved to 1.88x as of Q2FY26, down from 2.7x a year ago

VARIANCE 1.88 vs 2 x

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q4FY25 · Q4FY25 transcript

Maintain net debt-to-EBITDA ratio at 1.2x

TARGET 1.2x net debt/EBITDA

ACTUAL Net debt-to-EBITDA ratio reported at 0.95x at fiscal year end FY26

VARIANCE 0.95 vs 1.2 x

MET

Q4FY25 · Q4FY25 transcript

Reduce parent company VRL debt to \$5 billion

TARGET \$5 bn

ACTUAL VRL debt at \$4.7 billion as of Q4FY26

VARIANCE 4.7 vs 5 USD_bn

MET

Q4FY25 · Q4FY25 transcript

Increase oil and gas production volume from Q2FY26 onwards with higher volumes in Q3 and Q4

TARGET growth from Q2FY26 onwards

ACTUAL 3QFY26 production was 85 kboepd, lower than expected due to natural decline and delayed project commissioning.

VARIANCE 85 vs 2

MET

Q1FY26 · Q1FY26 presentation

Alumina capacity to reach 5 MTPA in FY26 and 6 MTPA in FY28

TARGET 5 MTPA in FY26, 6 MTPA in FY28

ACTUAL Lanjigarh alumina capacity expanded to 5 MTPA in FY26 with Train-2 commissioned

VARIANCE 5 vs 5-6 MTPA

MET

Q1FY26 · Q1FY26 transcript

Commission 160,000 tpa roaster at Debari in Q2FY26

TARGET by Q2FY26

ACTUAL 160,000 tpa Debari Roaster commissioning scheduled for 1HFY26

VARIANCE 1,60,000 vs 1,60,000 tons per annum

MET

Q1FY26 · Q1FY26 transcript

Complete Gamsberg Phase-2 project in H2FY26

TARGET by H2FY26

ACTUAL Project 94% complete; commissioning expected in Q1FY27, ramp-up thereafter.

VARIANCE 94 vs 2

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q1FY26 · Q1FY26 transcript

Meenakshi power capacity to reach 1,000 MW by end Q2FY26

TARGET 1,000 MW by end Q2FY26

ACTUAL 1.6 GW commissioned at Meenakshi by Q3FY26, total capacity 4.2 GW, expected 4.8 GW by H1FY27

VARIANCE **1,600 vs 1,000 MW**

MET

Q1FY26 · Q1FY26 transcript

Expand zinc metal production capacity to 2 million tons with 0.25 million ton phase 1 expansion

TARGET 2 million tons with 0.25 million ton phase 1

ACTUAL Phase 1 expansion progress at 89.3%, ramp up targeted in Q1FY27.

VARIANCE **89.3 vs 2 million tons**

MET

Q1FY26 · Q1FY26 transcript

Gain 15,000 bpd from full-scale ASP injection in 3-4 quarters

TARGET 15,000 bpd gain in 3-4 quarters

ACTUAL ASP commissioning delayed; first volumes expected in next three months

VARIANCE **85,000 vs 15,000 bpd**

MET

Q2FY26 · Q2FY26 transcript

Add 1.3 GW combined capacity at Meenakshi and Athena power plants in H1 FY26

TARGET 1.3 GW added in H1 FY26

ACTUAL 1.6 GW capacity commissioned at Athena and Meenakshi as of Q3 FY26

VARIANCE **1.6 vs 1.3 GW**

MET

Q2FY26 · Q2FY26 transcript

Reach total merchant power capacity of 4.2 GW by H1 FY26

TARGET 4.2 GW merchant power capacity by H1 FY26

ACTUAL Reached 4.2 GW merchant power capacity by Q3 FY26, on track for H1 FY26 target

VARIANCE **4.2 vs 4.2 GW**

MET

Q2FY26 · Q2FY26 presentation

Commission 600 MW at Athena

TARGET 600 MW Athena

ACTUAL Athena capacity reported as 1200 MW in Q3FY26 presentation, exceeding 600 MW target

VARIANCE **1,200 vs 600 MW**

The Track Record — 157 Testable Promises / part 24 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q2FY26 · Q2FY26 presentation

Commission additional 600 MW at Athena taking total capacity to 1200 MW

TARGET Additional 600 MW Athena
ACTUAL Commissioned around 1.6 GW additional capacity at Athena as of Q3FY26
VARIANCE **1,600 vs 600 MW**

MET

Q2FY26 · Q2FY26 transcript

Commission 160,000 ton per annum Debari roaster at Hindustan Zinc

TARGET 160,000 tpa Debari roaster commissioned
ACTUAL 160,000 tpa Debari roaster commissioned in 1HFY26 as scheduled
VARIANCE **1,60,000 vs 1,60,000 tons per annum**

MET

Q2FY26 · Q2FY26 presentation

Commission Gamsberg Phase 2 project by 2HFY26

TARGET Gamsberg Phase 2 completion
ACTUAL Gamsberg Phase 2 is 94% complete; commissioning expected in Q1FY27 with ramp-up thereafter.
VARIANCE **94 vs 2**

MET

Q2FY26 · Q2FY26 transcript

Commission 1.5 million tons per annum alumina Train II at Lanjigarh in H1 FY26

TARGET 1.5 Mtpa alumina Train II commissioned by H1 FY26
ACTUAL Train II commissioned during Q3FY26 as per presentation
VARIANCE **1.5 vs 1.5 million tons per annum**

MET

Q2FY26 · Q2FY26 presentation

Commission 1000 MW at Meenakshi Power

TARGET 1000 MW Meenakshi Power
ACTUAL Commissioned 1600 MW capacity at Meenakshi and Athena combined as of Q3FY26
VARIANCE **1,600 vs 1,000 MW**

MET

Q2FY26 · Q2FY26 presentation

Merchant Thermal Power capacity enhanced to 4.2 GW with commissioning of Athena 600MW and Meenakshi 1000 MW

TARGET 4.2 GW Merchant Thermal Power capacity
ACTUAL Merchant Thermal Power capacity reached 4.2 GW as of Q3FY26, currently up and running
VARIANCE **4.2 vs 4.2 GW**

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q2FY26 · Q2FY26 presentation

Doubling of VAP capacity from 1.4 to 2.8 MTPA

TARGET 2.8 MTPA VAP capacity
ACTUAL Reached 2.8 MTPA aluminum capacity after BALCO ramp up
VARIANCE **2.8 vs 2.8 MTPA**

MET

Q2FY26 · Q2FY26 presentation

4 MTPA Wet Beneficiation Plant at IOK

TARGET 4 MTPA Wet Beneficiation Plant
ACTUAL Commissioning initiated in FY26 as per Q3FY26 presentation
VARIANCE **4 vs 4 MTPA**

MET

Q2FY26 · Q2FY26 transcript

Commission India's first Zinc tailings reprocessing plant at Rampura Agucha with 10 million ton per annum capacity

TARGET 10 Mtpa Zinc tailings plant capacity
ACTUAL 10 Mtpa Zinc Tailings Reprocessing listed in commissioning schedule for FY26
VARIANCE **10 vs 10 million tons per annum**

MET

Q2FY26 · Q2FY26 presentation

Growth capex of USD 0.9 billion in 1H FY26

TARGET \$0.9 bn capex in 1H FY26
ACTUAL Growth capex was USD 1.3 billion in 9M FY26, exceeding the 1H FY26 target of USD 0.9 billion.
VARIANCE **1.3 vs 0.9 USD_bn**

MET

Q2FY26 · Q2FY26 presentation

Declared dividend of Rs. 16 per share during the quarter

TARGET Dividend Rs.16 per share
ACTUAL Dividend of Rs.16 per share was paid last quarter as stated in Q4FY26 transcript
VARIANCE **16 vs 16 INR/share**

MET

Q2FY26 · Q2FY26 presentation

Net Debt to EBITDA ratio to improve to 1.37x

TARGET Net Debt/EBITDA 1.37x
ACTUAL Net Debt/EBITDA ratio reported at 1.23x in Q3FY26 presentation.
VARIANCE **1.23 vs 1.37 x**

The Track Record — 157 Testable Promises / part 26 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q2FY26 · Q2FY26 transcript

Reduce Vedanta India net debt to EBITDA ratio from 1.37x to 1x

TARGET 1x net debt/EBITDA

ACTUAL Vedanta India net debt to EBITDA ratio reported at 0.95x at fiscal year end FY26

VARIANCE **0.95 vs 1 x**

MET

Q2FY26 · Q2FY26 transcript

Achieve hot metal cost of production below \$1,650 per ton in H2 FY26

TARGET sub \$1,650 hot metal COP in H2 FY26

ACTUAL Hot metal cost was \$1,674/t in Q3FY26, slightly above the \$1,650/t target for H2 FY26.

VARIANCE **1,674 vs 1,650 USD/ton**

MET

Q2FY26 · Q2FY26 transcript

Complete demerger and list all five entities by end of FY26

TARGET 5 entities listed by FY26-end

ACTUAL Demerger completed; five entities listed and operating separately from next quarter.

VARIANCE **on time**

MET

Q3FY26 · Q3FY26 transcript

Increase aluminum production to 2.8 million tons post BALCO ramp-up and close gap to 3 million tons in 18 months

TARGET 2.8 million tons now, 3 million tons in 18 months

ACTUAL Aluminum production at run rate close to 4 million tons exiting FY26

VARIANCE **40,00,000 vs 2.8-3 million tons**

MET

Q3FY26 · Q3FY26 transcript

Ramp up BALCO smelter to 100,000 tons by March end and full ramp-up in next 3-6 months

TARGET 100,000 tons by Mar 2026, full ramp-up in 3-6 months

ACTUAL BALCO smelter ramp-up progressing quarterly to full 100,000 tons run rate by Q4 FY26

VARIANCE **1,00,000 vs 1,00,000 tons**

MET

Q3FY26 · Q3FY26 transcript

Commission 160,000 tons per annum Debari roaster and add 21,000 tons per annum refined zinc capacity

TARGET 160,000 tpa Debari roaster + 21,000 tpa capacity addition

ACTUAL Refined zinc capacity at run rate close to 4 million tons per annum exiting FY26

VARIANCE **40,00,000 vs 1,81,000 tons per annum**

03

The Track Record — 157 Testable Promises / part 27 of 27

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 181 promises are forward-dated and remain Not Yet Testable.

MET

Q3FY26 · Q3FY26 presentation

Ramp up Gamsberg Phase 2 project in Q1FY27

TARGET

Ramp up by Q1FY27

ACTUAL

Anticipated commissioning in next quarter and ramp-up for rest of the year

VARIANCE

on time

Master Table — all 338 measurable commitments

Chronological · oldest first · colour = delivery status

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-08-01	Q1FY25	Q1FY25 transcript	Iron ore concentrated plant of 3 million tons per annum in Liberia under construction	we are initiating construction of our first 3 million ton per annum concentrated plant in that region	3 Mtpa iron ore plant under construction	near term	H	3 Mtpa iron ore plant under construction as planned	MET	3 vs 3 million tons per annum		
2024-08-01	Q1FY25	Q1FY25 transcript	Aluminium capacity of 3.1 million tons per annum with 90% value-added products	we will be a fully integrated 3.1 million tons per year producer, while maintaining global lowest cost positioning	Aluminium capacity 3.1 Mtpa · 3.1 Mtpa aluminium capacity	near term	H	Run rate of 3 MTPA technical capacity achieved but not sustained due to unplanned shutdowns and infra handling issues	PARTIAL	3 vs 3.1 million tons per annum	Unplanned shutdowns and infra handling issues prevented sustained run rate	Execution
2024-08-01	Q1FY25	Q1FY25 transcript	BALCO smelter expansion progressing steadily	BALCO smelter expansion is advancing steadily with all equipment orders fulfilled and installations underway	BALCO smelter expansion progressing	near term	L	Commissioning initiated for 435 KTPA BALCO smelter expansion	NYT	no numeric target		
2024-08-01	Q1FY25	Q1FY25 transcript	Kurloi and Radhikapur coal mines first ore in Q1FY26, Ghogharpalli in Q2FY26, Sijimali in Q1FY26	for Kurloi, Radhikapur, we're looking at first quarter of FY '26. For Ghogharpalli, second quarter of	Coal mines first ore Q1FY26 and Q2FY26 · Kurloi & Radhikapur Q1FY26, Ghogharpalli Q2FY26, Sijimali Q1FY26	2025-08-14	H	Kuraloi mining lease received; operations to start soon. Ghogharpalli EC recommended; FC targeted this quarter. Sijimali as previously guided.	MET	2 vs 1		
2024-08-01	Q1FY25	Q1FY25 transcript	Increase cobalt production from 1 kilo ton to over 6 kilo tons per annum, potential to 10 kilo tons	we can extract over 6 kilo tons of Cobalt per annum, with the plan further once we've done that and we ramp up to 300	Cobalt production >6 ktpa, potential 10 ktpa · >6 ktpa cobalt production, potential 10 ktpa		L		NYT	no actual reported		
2024-08-01	Q1FY25	Q1FY25 transcript	ESL steel ramp-up to 3.5 million tons per annum by FY25	ESL, the expansion to 3.5 million tons per annum is estimated to be completed by FY'25	ESL steel capacity 3.5 Mtpa by FY25 · 3.5 Mtpa steel capacity by FY25	2025-05-15	H	ESL steel capacity was 1.34 MTPA in FY25, below the 3.5 MTPA target	MISSED	1.34 vs 3.5 million tons per annum	Unplanned shutdowns and infrastructure handling issues limited sustained capacity	Execution
2024-08-01	Q1FY25	Q1FY25 transcript	ESL steel ramp-up to 3.5 million tons per annum by end FY25	we are completing the expansion to 3.5 million tons to be commissioned by end of this year	ESL steel capacity 3.5 Mtpa by FY25-end · 3.5 Mtpa steel capacity by FY25-end	2025-05-15	H	Run rate of 3 MTPA achieved but not sustained due to unplanned shutdowns and infra handling; issues expected to be resolved soon	MISSED	3 vs 3.5 million tons per annum	Unplanned shutdowns and infrastructure handling caused inability to sustain 3 MTPA run rate	Execution
2024-08-01	Q1FY25	Q1FY25 transcript	FACOR ferro chrome capacity increase to 150,000 tons per annum in FY25	we are gearing up to increase our capacity to 150,000 tons per annum in FY'25	FACOR capacity 150,000 tpa · 150,000 tpa FACOR capacity	2025-05-15	H	Ferro Chrome production reached 24,000 tpa in Q3 FY26, below the 150,000 tpa target for FY25	MISSED	24,000 vs 1,50,000 tons per annum	Q2'26 performance impacted due to a one-month planned shutdown	Capacity delay
2024-08-01	Q1FY25	Q1FY25 presentation	Commission FeSi Plant in May 2024 with 70% Si consistently achieved	In May'24, FeSi Plant was commissioned and 70% Si is being achieved on consistent basis	FeSi Plant commissioned May 2024 with 70% Si · commissioned May 2024 with 70% Si	2024-05-31	H		NYT	no actual reported		
2024-08-01	Q1FY25	Q1FY25 presentation	Complete Gamsberg Phase 2 by end of 2HFY25	Target completion by end of 2HFY25	Gamsberg Phase 2 completion by 2HFY25 · by end of 2HFY25		H	Project 80% complete, mechanical completion targeted by December 2HFY26	MET	80 vs 2		
2024-08-01	Q1FY25	Q1FY25 transcript	Iron ore FY25 production target of 12 million tons per annum plus 1 million ton value-added business	we remain on track in our FY'25 production target of 12 million ton per annum with an additional 1 million ton from our value-added business	Iron ore production 12 Mtpa + 1 Mtpa value-added · 12 Mtpa plus 1 Mtpa value-added iron ore production FY25	2025-05-15	H	Iron ore production was 5.3 MTPA and value-added pig iron production was 0.9 MTPA in FY25.	MISSED	5.3 vs 12 million tons per annum	null	Execution
2024-08-01	Q1FY25	Q1FY25 transcript	Iron ore annual production of approximately 30 million tons at Liberia	Our near-term projections at Liberia indicate an annual production of approximately 30 million tons of iron ore	Iron ore production 30 Mtpa · 30 Mtpa iron ore production	near term	L		NYT	no actual reported		
2024-08-01	Q1FY25	Q1FY25 transcript	KCM copper production run rate of 100 kilo tons by end FY25 and ramp-up to 300 kilo tons in next years	we will be at a run rate of about 100 kilo tons of copper, and then a very fast ramp-up over the next number of	KCM copper production 100 kt by FY25-end, 300 kt later · 100 kt copper by FY25-end, 300 kt later		H	KCM copper production ramped up to about 45,000 tons by Q4FY25	MET	45,000 vs 100-300 kilo tons		
2024-08-01	Q1FY25	Q1FY25 transcript	Lanjigarh refinery Train 1 and Train 2 ramp-up to 4-5 million tons capacity by Q1FY26	we will be able to ramp up capacity to the 4 million to 5 million tons of capacity	Lanjigarh refinery capacity 4-5 Mt by Q1FY26 · 4-5 Mt capacity by Q1FY26	2025-08-14	H	Run rate close to 4 million tons at FY26 exit; rated capacity expected in Q1FY27	MET	4 vs 4-5 million tons		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-08-01	Q1FY25	Q1FY25 transcript	Lanjigarh refinery Train 1 full capacity by Q3 FY25	<i>we expect to be running at an effectively a full 3.5 million ton capacity by third quarter of this financial year</i>	Lanjigarh Train 1 full capacity 3.5 Mt by Q3 FY25 · 3.5 Mt capacity by Q3 FY25	2025-02-14	H	Only 1.5 Mt train commissioned by Q4 FY25, not full 3.5 Mt capacity by Q3 FY25	MISSED	1.5 vs 3.5 million tons	In progress; commissioning of second train started, targeting 4 Mt run rate by year-end	Execution
2024-08-01	Q1FY25	Q1FY25 transcript	Aluminium refinery Lanjigarh Train 2 commissioning in Q3 FY25 and full ramp-up by Q1 FY26	<i>we are on track to commission Train 2 in quarter 3 of current FY'25 with a full ramp up expected by quarter 1 of FY'26</i>	Lanjigarh Train 2 commissioned Q3 FY25, full ramp-up by Q1 FY26 · Train 2 commissioning Q3 FY25, full ramp-up Q1 FY26	2025-02-14	H	Train 2 commissioning initiated with first alumina output in Q2 FY26	MISSED	1 vs 2		
2024-08-01	Q1FY25	Q1FY25 presentation	Complete 700ktpa Magnetite Project by 3QFY25	<i>700ktpa Magnetite Project – Target completion 3QFY25</i>	Magnetite Project completion by 3QFY25 · by 3QFY25	2025-02-14	H	Project completion re-guided to 4QFY25 from 3QFY25	MET	700 vs 3		
2024-08-01	Q1FY25	Q1FY25 transcript	Full commissioning of Meenakshi power 1,000 MW in FY25	<i>The fiscal year will see the full commissioning of Meenakshi power of 1,000 megawatt</i>	Meenakshi power 1,000 MW commissioned · 1,000 MW Meenakshi power commissioning	2025-05-15	H	700 MW operationalized by 2QFY26 (Units 3&4, 350MW each)	MISSED	700 vs 1,000 MW	No full 1000 MW commissioning reported; partial units operational with 48% PLF	Capacity delay
2024-08-01	Q1FY25	Q1FY25 transcript	Power generation of 5 gigawatts of commercial power over next two years	<i>we are well placed to generate 5 gigawatts of commercial power over the next two years</i>	Power generation 5 GW · 5 GW power generation		L		NYT	no actual reported		
2024-08-01	Q1FY25	Q1FY25 presentation	Renewable Energy Power Delivery Agreements of 1836 MW in place	<i>RE Power Delivery agreements (PDAs) of 1836 MW in place</i>	RE PDAs 1836 MW · 1836 MW RE PDAs	2024-08-14	H	RE PDAs reached 1906 MW by Q4FY25, exceeding the 1836 MW target.	MET	1,906 vs 1,836 MW		
2024-08-01	Q1FY25	Q1FY25 presentation	VZl to deliver 500+ KTPA MIC run rate within 3 years	<i>VZl to deliver 500+ KTPA MIC run rate within 3 years</i>	VZl MIC run rate 500+ KTPA · 500+ KTPA MIC run rate within 3 years		H	VZl capacity expected to commission next quarter, ramping to about 450,000 KTPA run rate	MET	4,50,000 vs 500 KTPA		
2024-08-01	Q1FY25	Q1FY25 transcript	Zinc India metal capacity of 1.2 million tons and 800 tons silver production	<i>Zinc India, with defined metal capacity of 1.2 million tons and 800 tons of silver production</i>	Zinc India capacity 1.2 Mt metal, 800 t silver · 1.2 Mt metal and 800 t silver capacity	near term	H	Zinc India capacity reached 1.2 million tons metal and 800 tons silver production	MET	1.2 vs 1.2 million tons		
2024-08-01	Q1FY25	Q1FY25 transcript	Expand Zinc India metal production to 2 million tons per annum in near future	<i>we are exploring avenues to expand our metal production to 2 million ton per annum in near future</i>	Zinc India metal production 2 Mtpa · 2 Mtpa Zinc India metal production		L	Zinc India mined metal production reached 258,000 tons in Q2FY26, highest-ever second quarter production	MET	2,58,000 vs 2 million tons per annum		
2024-08-01	Q1FY25	Q1FY25 transcript	Zinc India roaster at Debari 160,000 tpa and fertilizer plants 510,000 tpa progressing smoothly	<i>Zinc India, 160,000 tons per annum roaster at Debari and 510,000 tons of fertilizer plants are progressing smoothly</i>	Zinc India roaster 160,000 tpa, fertilizer plants 510,000 tpa · 160,000 tpa roaster and 510,000 tpa fertilizer plants	near term	L	160,000 tpa Debari Roaster commissioned in 1HFY26; 510,000 tpa Fertilizer Project commissioning scheduled for 1HFY27	MET	1,60,000 vs 1,60,000 tons per annum		
2024-08-01	Q1FY25	Q1FY25 transcript	Zinc International Phase 2 expansion full ramp-up expected in Q2 FY26	<i>globally. Our Phase 2 expansion project is in full swing with full ramp up expected in quarter 2 of</i>	Zinc International Phase 2 full ramp-up Q2 FY26 · Phase 2 full ramp-up Q2 FY26	2025-11-14	H	Project ramp-up delayed; now targeted in Q1FY27 instead of Q2FY26.	MET	89.3 vs 2		
2024-08-01	Q1FY25	Q1FY25 transcript	Zinc International to deliver 1 million ton zinc production	<i>we are committed to deliver 1 million ton of zinc production from Zinc International</i>	Zinc International zinc production 1 Mt · 1 Mt zinc production	near term	L	Zinc International produced 176,000 tonnes in first 9 months of FY26, showing 38% YoY growth	MET	1,76,000 vs 1 million tons		
2024-08-01	Q1FY25	Q1FY25 transcript	Zinc International to reach 500 kilo tons zinc production within 2 years	<i>Within 2 years, we will be at 500 kilo ton</i>	Zinc International zinc production 500 kt in 2 years · 500 kt zinc production in 2 years		H	Zinc International zinc production reached 176 kt by Q3FY26, showing 38% YoY growth.	MISSED	176 vs 500 kilo tons		
2024-08-01	Q1FY25	Q1FY25 transcript	Execute about \$8 billion of growth capex in next few years	<i>commitment to execute about \$ 8 billion of growth capex in the next few years</i>	Growth capex \$8 bn · \$8 bn growth capex in next few years		L	Growth capex spent USD 1.3 billion as of Q3FY26	MISSED	1.3 vs 8 USD_bn		
2024-08-01	Q1FY25	Q1FY25 transcript	Spend about \$1 billion over next 5 years to achieve KCM copper ramp-up	<i>we have committed to spend about \$1 billion over the next 5 years to achieve that ramp-up</i>	KCM capex \$1 bn over 5 years · \$1 bn capex over 5 years		H	fundraising for \$1 billion over 5 years is still a work in progress	NYT	fundraising for \$1 billion over 5 years is still a work in p		
2024-08-01	Q1FY25	Q1FY25 presentation	Utilize QIP proceeds for deleveraging and interest savings of ~Rs 1,100 crore	<i>Proceeds will be utilized for deleveraging Interest Savings : ~Rs 1,100 crore</i>	Interest savings ~Rs 1,100 crore from QIP proceeds · interest savings ~Rs 1,100 crore	2025-05-15	H	VRL debt reduced by almost INR 1 billion over last five quarters as of June 30, 2025.	MET	1,00,00,00,000 vs 1,100 INR_cr		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-08-01	Q1FY25	Q1FY25 presentation	Raise Rs. 8,500 crore through QIP	<i>Successfully raised Rs. 8,500 crore through the largest QIP</i>	QIP raise Rs 8,500 crore · Rs 8,500 crore QIP raise	2024-08-14	H		NYT	no actual reported		
2024-08-01	Q1FY25	Q1FY25 presentation	Anil Agarwal Foundation to spend Rs 5,000 crore over next 5 years on social impact programs	<i>social initiatives, has pledged Rs 5000 crore over the next five years</i>	Rs 5,000 crore CSR spend over 5 years · Rs 5,000 crore over 5 years		H	Reported ₹141 crore CSR spend in first half of FY25 towards social impact programs	MISSED	141 vs 5,000 INR_cr		
2024-08-01	Q1FY25	Q1FY25 transcript	Aluminium business EBITDA about \$4 billion at LME \$2,600	<i>we are well positioned to deliver EBITDA in the region of about \$4 billion from our aluminium business at LME of about \$2,600</i>	Aluminium EBITDA \$4 bn at LME \$2,600 · \$4 bn aluminium EBITDA at LME \$2,600	near term	L	Aluminium segment EBITDA reported at ₹7,023 crore in Q3FY26	NYT	actual in INR crore not comparable to USD_bn		
2024-08-01	Q1FY25	Q1FY25 transcript	Near-term annual EBITDA of \$10 billion	<i>In the near term, we are poised to deliver \$ 30 billion in</i>	Annual EBITDA \$10 bn · Near-term annual EBITDA \$10 bn	near term	L	Reported highest-ever EBITDA of ₹15,171 crore in Q3FY26	NYT	actual in INR_crore not comparable to USD_bn		
2024-08-01	Q1FY25	Q1FY25 transcript	Oil and gas business to generate over \$1 billion EBITDA	<i>With this, our oil and gas business will generate over a \$1 billion of EBITDA</i>	Oil & gas EBITDA > \$1 bn	near term	L	Oil and Gas EBITDA exceeded \$1 billion, reaching \$1.1 billion in FY26	MET	1.1 vs 1 USD_bn		
2024-08-01	Q1FY25	Q1FY25 transcript	Zinc India annual EBITDA of \$2.7 billion	<i>HZL is poised to generate annual EBITDA of \$2.7 billion</i>	Zinc India EBITDA \$2.7 bn · \$2.7 bn Zinc India EBITDA	near term	L	Zinc India reported ₹15,171 crore EBITDA in Q3FY26, highest-ever quarter 3 EBITDA	NYT	actual in INR crore not comparable to USD_bn		
2024-08-01	Q1FY25	Q1FY25 transcript	Vedanta Resources Limited reduced debt by \$650 million in Q1FY25	<i>we have achieved a reduction of 650 million in the first quarter itself</i>	VRL debt reduction \$650 mn in Q1FY25 · \$650 mn debt reduction in Q1FY25	2024-08-14	H	VRL debt reduced by almost \$1 billion over last five quarters including Q1FY25	MISSED	1,00,00,00,000 vs 650 USD_mn		
2024-08-01	Q1FY25	Q1FY25 transcript	Vedanta Resources Limited to deleverage \$3 billion over next 3 years	<i>we have further announced deleveraging of 3 billion over the next 3 years</i>	VRL deleveraging \$3 bn · \$3 bn deleveraging over next 3 years		H	Deleveraged by \$4+ billion in last 3 years, exceeding \$3 billion target	MISSED	4 vs 3 USD_bn		
2024-08-01	Q1FY25	Q1FY25 presentation	HZL to consume ~8.5% renewable energy of total power requirement in Q1 FY25	<i>HZL already consumed c.8.5% RE power of total requirement in Q1 FY25</i>	HZL RE power consumption 8.5% · 8.5% RE power consumption	2024-08-14	H	FY25 renewable energy utilization reported at 2.61 billion units	MISSED	2.61 vs 8.5 %		
2024-08-01	Q1FY25	Q1FY25 presentation	Achieve workplace gender diversity target 7 years in advance at 22%	<i>Achieved our workplace gender diversity target for full-time employees 7 years in advance. Gender diversity for</i>	Workplace gender diversity 22% · 22% gender diversity	2024-08-14	H		NYT	no actual reported		
2024-08-01	Q1FY25	Q1FY25 presentation	FY25 near-term target to deliver \$10bn annual EBITDA	<i>On track to deliver US\$ 10bn annual EBITDA in near term</i>	Annual EBITDA \$10bn near term · \$10bn annual EBITDA	near term	L	Reported second highest EBITDA of Rs. 43,541 crores for FY25	NYT	actual in INR_crores not comparable to USD_bn		
2024-08-01	Q1FY25	Q1FY25 transcript	Near-term annual revenue of \$30 billion	<i>In the near term, we are poised to deliver \$ 30 billion in annual revenue</i>	Annual revenue \$30 bn · Near-term annual revenue \$30 bn	near term	L	Reported record-best revenue of ₹1,22,551 crore for 9 months ended Dec 2025	NYT	actual in INR_crore not comparable to USD_bn		
2024-08-01	Q1FY25	Q1FY25 presentation	Plant 7 million trees by 2030	<i>commitment to plant 7 million trees by 2030</i>	7 million trees planted by 2030 · 7 million trees by 2030	2030	H	3.8 million trees planted by Q3FY26	NYT	in progress, not yet due		
2024-08-01	Q1FY25	Q1FY25 presentation	Commission majority of growth projects in FY25	<i>remain committed to commission the majority of these projects in FY25</i>	Majority of growth projects commissioned by FY25 · by FY25	2025-05-15	H	Commissioned key growth projects including Lanjigarh Refinery expansion and Bicholim Iron Ore Mine by mid-FY25	MET	on time		
2024-08-01	Q1FY25	Q1FY25 transcript	Oil and gas near-term production target of 150,000 barrels per day and 1.6 billion barrels reserves	<i>Our near-term target is to deliver 150,000 barrels production a day and 1.6 billion barrels in reserve and resources</i>	Oil & gas production 150,000 bpd, reserves 1.6 bn barrels · 150,000 bpd production and 1.6 bn barrels reserves	near term	L	Production at 85,000 bpd due to natural decline and lower well intervention activities	MISSED	85,000 vs 1,50,000 bpd and billion barrels	Natural decline and lower well intervention activities in Cambay block	Execution
2024-08-01	Q1FY25	Q1FY25 transcript	Oil and gas production vision of 300,000 kboepd	<i>Our vision, however, is to reach production of 300,000 kboepd barrels a day</i>	Oil & gas production 300,000 kboepd · 300,000 kboepd production	long term	L	3QFY26 production was 85 kboepd, down from prior periods due to natural decline and lower well intervention activities	MISSED	85 vs 3,00,000 kboepd	Natural decline and lower well intervention activities in Cambay block	Execution

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-11-01	Q2FY25	Q2FY25 transcript	Generate 5 GW of commercial power within next 18 to 20 months	<i>we are well positioned to generate 5 Gigawatts of commercial power within the next 18 to 20 months</i>	5 GW commercial power generation		H	Power generation reached 3889 MU in 2QFY26, highest ever recorded.	MET	3,889 vs 5 GW		
2024-11-01	Q2FY25	Q2FY25 presentation	Complete 700ktpa Magnetite Project by 4QFY25	<i>700ktpa Magnetite Project on track – Target completion 4QFY25</i>	700 ktpa Magnetite Project completion by 4QFY25	2025-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Add new rigs in 2HFY25 to drill more infill wells	<i>New rigs being added in 2HFY25 to add more infill wells</i>	Add rigs for infill wells drilling in 2HFY25 · New rigs added in 2HFY25		M	10 infill wells drilled in Q4FY25 as part of the plan	MET	10 vs 2 rigs		
2024-11-01	Q2FY25	Q2FY25 transcript	Reach aluminium production capacity of 3.1 million tons per annum with 90% value-added products	<i>enable us to reach a production capacity of 3.1 million tons per annum of aluminum with 90% comprising value-added products and alloys</i>	Aluminium capacity 3.1 Mtpa with 90% VAP · 3.1 Mtpa aluminium capacity with 90% VAP	medium term	H	Aluminium capacity reached 3.0 Mtpa with 68% VAP as of Q3FY25, below 90% VAP target	PARTIAL	3 vs 3.1 Mtpa	Unplanned shutdowns and infrastructure handling issues prevented sustaining full capacity and VAP percentage	Execution
2024-11-01	Q2FY25	Q2FY25 presentation	Operationalize Bicholim Iron Ore Mine of 3 MTPA capacity at Goa	<i>Operationalized Bicholim Iron Ore Mine of 3MTPA capacity at Goa</i>	Bicholim Iron Ore Mine 3 MTPA operational · 3 MTPA Bicholim Iron Ore Mine operational by Q2FY25	2024-11-14	H	Bicholim Iron Ore Mine operational with 0.77 MTPA saleable ore production by Mar'25	MISSED	0.77 vs 3 MTPA		
2024-11-01	Q2FY25	Q2FY25 transcript	Commission 160,000 tpa roaster at Debari and 0.5 million tpa fertilizer plant by Q4 FY25 and Q2 FY26 respectively	<i>160,000 tons per annum roaster at Debari and 0.5-million-ton fertilizer plant are processing as planned with final commissioning targeted in the last quarter of this</i>	Debari roaster 160 ktpa by Q4 FY25; fertilizer plant 0.5 Mtpa by Q2 FY26 · Debari roaster Q4 FY25; fertilizer plant Q2 FY26	2025-05-15	H	Debari roaster commissioned in 1HFY26; fertilizer plant commissioning shifted to 1HFY27	MET	1,60,000 vs 1,60,000-5,00,000 tpa		
2024-11-01	Q2FY25	Q2FY25 transcript	Commission 300 ktpa Ferrochrome capacity with underground mine expansion at FACOR	<i>we are on track to become the India's largest Ferrochrome producer</i>	FACOR 300 ktpa Ferrochrome capacity · 300 ktpa Ferrochrome capacity	medium term	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Complete Gamsberg Phase II Project in FY26	<i>Project completion targeted in FY26</i>	Gamsberg Phase II Project completion by FY26	2026-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 transcript	Operationalize Ghogarpalli coal block by Q4 FY26	<i>we are targeting by 4th quarter of '26 it gets operationalized</i>	Ghogarpalli coal block operational Q4 FY26 · operational Q4 FY26	2026-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	HZL Board approved 3rd stage of PDA to increase RE power consumption from ~50% to ~70%	<i>HZL Board approved 3rd stage of PDA for increasing RE power (RTC) consumption from c.50% to c.70%</i>	HZL RE power consumption ~70% · Increase RE power consumption to ~70%	2025-05-15	H	HZL achieved ~70% RE power consumption as targeted in 3rd stage of PDA	MET	70 vs 70 %		
2024-11-01	Q2FY25	Q2FY25 presentation	Ramp up infill wells in Mangala and RDG fields in 1H FY25	<i>partially offset by infill wells brought online in Mangala and RDG fields</i>	Infill wells ramp up in Mangala and RDG fields in 1HFY25 · Ramp up infill wells in Mangala and RDG fields in 1HFY25		M	Drilled 9 infill wells in Mangala and Aishwarya fields by Q3FY25	MET	9 vs 1 infill wells		
2024-11-01	Q2FY25	Q2FY25 presentation	Ramp up Jaya oilfield production in 1H FY25	<i>supported by ramp up of Jaya oilfield</i>	Jaya oilfield ramp up in 1HFY25 · Ramp up Jaya oilfield production in 1HFY25		M	Commissioning delayed; startup expected and first volumes targeted within next three months from Jan 2026	NYT	Commissioning delayed; startup expected and first volumes ta		
2024-11-01	Q2FY25	Q2FY25 transcript	Operationalize Kuraloi coal block by Q1 FY26 and ramp up by Q3 FY26	<i>Kuraloi coal block we are expecting first quarter of '26, it will get operationalized and which we are trying to ramp up by third quarter</i>	Kuraloi coal block operational Q1 FY26, ramp-up Q3 FY26 · operational Q1 FY26, ramp-up Q3 FY26	2025-08-14	H	Commissioning of Kuraloi coal mine delayed to Q4 FY26 from Q1 FY26	MET	4 vs 1-3 quarter		
2024-11-01	Q2FY25	Q2FY25 transcript	Ramp-up Lanjigarh refinery capacity to 3 million tons run rate by October 2024	<i>capacity has gone up to 3 million tons</i>	Lanjigarh refinery 3 million tons run rate · 3 million tons run rate	2024	H	Run rate reached close to 4 million tons by end of FY26, with full rated capacity expected in Q1 FY27	MET	4 vs 3 Mtpa		
2024-11-01	Q2FY25	Q2FY25 presentation	Commission 1.5 MTPA unit of Lanjigarh Refinery expansion project	<i>Commissioned 1.5 MTPA unit of Lanjigarh Refinery expansion project</i>	Lanjigarh Refinery expansion 1.5 MTPA commissioned · 1.5 MTPA Lanjigarh Refinery expansion commissioned by Q2FY25	2024-11-14	H	1.5 MTPA Lanjigarh Refinery expansion train commissioned by Q4FY25	MET	1.5 vs 1.5 MTPA		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-11-01	Q2FY25	Q2FY25 transcript	Ramp-up Lanjigarh Refinery Train 1 to full capacity by December 2024	<i>We expect to fully ramp-up Train 1 by December 2024</i>	Lanjigarh Refinery Train 1 full ramp-up by Dec 2024 · full ramp-up by December 2024	2024	H	Ramp-up delayed; run rate close to 4 million tons at FY26 end, rated capacity expected in Q1 FY27	MISSED	4 vs 2,024 date	Calciners and boiler running at 75-80% capacity causing delay	Capacity delay
2024-11-01	Q2FY25	Q2FY25 transcript	Commission Lanjigarh Refinery Train 2 in Q3 FY25 and full ramp-up by Q1 FY26	<i>We are also on track to commission Train 2 in Quarter 3 FY '25, with full ramp up expected by quarter 1 of FY '26</i>	Lanjigarh Refinery Train 2 commission Q3 FY25, full ramp-up Q1 FY26 · commission Q3 FY25, full ramp-up Q1 FY26	2025-02-14	H	Train 2 commissioning started with first alumina output reported in Q2 FY26	MISSED	1 vs 3-1 quarter		
2024-11-01	Q2FY25	Q2FY25 transcript	Full commissioning of Meenakshi Power Plant 1000 MW in FY25	<i>this fiscal year will mark the full commissioning of Meenakshi Power Plant 1,000 Megawatts</i>	Meenakshi Power Plant 1000 MW full commissioning FY25 · full commissioning FY25	2025-05-15	H	Units 3 and 4 (700 MW total) operationalized but full 1000 MW commissioning not reported for FY25	MISSED	700 vs 1,000 MW		
2024-11-01	Q2FY25	Q2FY25 presentation	Ramp up volumes under OALP blocks to 3.8 kboepd in 1H FY25	<i>Volumes under OALP blocks rise to 3.8 kboepd in 1H</i>	OALP volumes 3.8 kboepd in 1HFY25 · 3.8 kboepd OALP volumes in 1HFY25		H	OALP volumes were 3.5 kboepd in 1HFY25, below the 3.8 kboepd target for 1HFY25	MISSED	3.5 vs 3.8 kboepd	Volumes impacted by operational challenges and well failures in Mangala wells	Execution
2024-11-01	Q2FY25	Q2FY25 presentation	Offshore drilling campaign on West Coast to commence in 3QFY25	<i>Offshore drilling campaign on West Coast to commence in 3QFY25</i>	Offshore drilling campaign start in 3QFY25	2025-02-14	H	Drilling campaign commenced in Dwarka offshore; Ambe drilling planned for 3QFY26	MET	3 vs 3 campaign		
2024-11-01	Q2FY25	Q2FY25 transcript	Operationalize Radhikapur coal block before Q1 FY26	<i>Radhikapur also, we are on track</i>	Radhikapur coal block operational before Q1 FY26 · operational before Q1 FY26	2025-08-14	H	Kuraloi coal mine commissioning targeted in Q4FY26 as per latest guidance	MET	4 vs 1 quarter		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve 1906 MW renewable energy power delivery agreements (PDAs)	<i>Secured RE Power Delivery agreements (PDAs) of 1906 MW (+80MW QoQ)</i>	Renewable energy PDAs 1906 MW · 1906 MW renewable energy PDAs	2024-11-14	H	Renewable energy PDAs of 1906 MW are in place as of Q4FY25	MET	1,906 vs 1,906 MW		
2024-11-01	Q2FY25	Q2FY25 transcript	Start Sijimali bauxite mine in Q1 FY26	<i>we expect that in quarter 1, next year, we should start the mine</i>	Sijimali mine start Q1 FY26 · start mine Q1 FY26	2025-08-14	H	Sijimali bauxite mine commissioning rescheduled to 1HFY27	MET	1 vs 1 quarter		
2024-11-01	Q2FY25	Q2FY25 presentation	Commission Train 2 of 1.5 MTPA Lanjigarh Expansion project in Q3FY25	<i>On track to commission Train 2 of 1.5 MTPA of Lanjigarh Expansion project in Q3FY25</i>	Train 2 Lanjigarh Expansion 1.5 MTPA commissioned by Q3FY25 · 1.5 MTPA Train 2 Lanjigarh Expansion commissioned by Q3FY25	2025-02-14	H	Train 2 of 1.5 MTPA Lanjigarh Expansion commissioned in Q4FY25	MET	1.5 vs 1.5 MTPA		
2024-11-01	Q2FY25	Q2FY25 transcript	Full ramp-up of Zinc International Phase 2 expansion during FY26	<i>Our Phase 2 expansion project is in full swing with full ramp-up expected during FY '26</i>	Zinc International Phase 2 full ramp-up FY26 · full ramp-up during FY26	2026-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Spend \$96 million capex on Athena Power Project	<i>Athena Power Project 96</i>	Athena Power Project capex \$96 mn · \$96 million capex on Athena Power Project	2025-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Spend \$125 million capex on Avanstrate Furnace Expansion and Cold Line Repair	<i>Avanstrate Furnace Expansion and Cold Line Repair 125</i>	Avanstrate Furnace Expansion capex \$125 mn · \$125 million capex on Avanstrate Furnace Expansion and Cold Line Repair	2025-05-15	H	Spent 142 INR Crore on Jharsuguda VAP capacity expansion and others in 1HFY26	NYT	actual in INR Crore not comparable to USD_mn		
2024-11-01	Q2FY25	Q2FY25 presentation	Spend \$1.08 billion capex on Balco smelter and VAP capacity expansion	<i>Balco smelter and VAP capacity expansion 1,068</i>	Balco smelter and VAP capacity expansion capex \$1.068 bn · \$1.068 billion capex on Balco smelter and VAP capacity expansion	2025-05-15	H	Approved capex ₹1,656 crore; cumulative spend ₹1,456 crore by 1HFY26, unspent ₹200 crore as of Sep 2025	NYT	actual in INR crore not comparable to USD_mn		
2024-11-01	Q2FY25	Q2FY25 presentation	Spend \$1.07 billion net capex on Cairn India projects	<i>Cairn India1 - Mangala, Bhagyam & Aishwariya infill, OALP, ABH infill, RDG infill, Offshore infill etc 1,070</i>	Cairn India net capex \$1.07 bn · \$1.07 billion net capex on Cairn India projects	2025-05-15	H	Cairn India net capex spent cumulatively 4,774 crore INR by Sep 30, 2025, out of approved 8,471 crore INR.	NYT	actual in INR crore not comparable to USD_mn		
2024-11-01	Q2FY25	Q2FY25 presentation	Spend \$349 million capex on ESL hot metal expansion from 1.5 to 3 MTPA	<i>ESL 1.5 to 3 MTPA hot metal 349</i>	ESL hot metal expansion capex \$349 mn · \$349 million capex on ESL hot metal expansion	2025-05-15	H	\$1,656 million capex approved for Aluminium Sector expansion; \$1,314 million spent up to FY25, \$142 million spent in 1HFY26, \$200 million unspent as of Sep 2025	MET	1,656 vs 349 USD_mn		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-11-01	Q2FY25	Q2FY25 presentation	Spend \$318 million capex on Facor ferrochrome expansion from 150 to 450 KTPA	<i>Facor 150 to 450 KTPA ferro chrome 318</i>	Facor ferrochrome expansion capex \$318 mn · \$318 million capex on Facor ferrochrome expansion	2025-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Spend \$466 million capex on Zinc International Gamsberg Phase II Project	<i>Gamsberg Phase II Project 466</i>	Gamsberg Phase II Project capex \$466 mn · \$466 million capex on Gamsberg Phase II Project	2025-05-15	H	Gamsberg Phase II Project is 89.3% complete; ramp up targeted in Q1FY27.	NYT	actual in percent complete not comparable to USD_mn		
2024-11-01	Q2FY25	Q2FY25 presentation	Spend \$109 million on growth projects in 1HFY25	<i>Spent \$109 mn on growth projects in 1HFY25</i>	Growth projects capex \$109 mn in 1HFY25 · \$109 million capex on growth projects in 1HFY25		H	Reported cumulative growth project capex spend of 4,039 crore INR in 1HFY26 across segments	NYT	actual in INR crore not comparable to USD_mn		
2024-11-01	Q2FY25	Q2FY25 presentation	Spend \$37 million capex on Iron Ore Project	<i>Iron Ore Project 37</i>	Iron Ore Project capex \$37 mn · \$37 million capex on Iron Ore Project	2025-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Spend \$254 million capex on Jharsuguda VAP capacity expansion and others	<i>Jharsuguda VAP capacity expansion and others 254</i>	Jharsuguda VAP capacity expansion capex \$254 mn · \$254 million capex on Jharsuguda VAP capacity expansion and others	2025-05-15	H	\$145.6 million spent on Jharsuguda VAP capacity expansion and others by Sep 30, 2025	MISSED	145.6 vs 254 USD_mn		
2024-11-01	Q2FY25	Q2FY25 presentation	Spend \$280 million capex on 3 MTPA Magnetite iron ore concentrator plant at Liberia	<i>Iron Ore 3 MTPA Magnetite iron ore concentrator plant at Liberia 280</i>	Magnetite iron ore concentrator plant capex \$280 mn · \$280 million capex on Magnetite iron ore concentrator plant at Liberia	2025-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Spend \$482 million capex on other Zinc India projects	<i>Others 482</i>	Other Zinc India projects capex \$482 mn · \$482 million capex on other Zinc India projects	2025-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 transcript	Project CAPEX of ₹5,209 crore for 1,200 MW Athena Power Plant	<i>Our Board has also approved the project CAPEX of 5,209 crores for 1,200 Megawatts Athena Power Plant</i>	Project CAPEX ₹5,209 crore for Athena Power Plant · ₹5,209 crore CAPEX	medium term	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Spend \$128 million capex on Roaster (Debari)	<i>Roaster (Debari) 128</i>	Roaster (Debari) capex \$128 mn · \$128 million capex on Roaster (Debari)	2025-05-15	H	Debari Roaster commissioned in 1HFY26	MET	160 vs 128 USD_mn		
2024-11-01	Q2FY25	Q2FY25 presentation	Spend \$2.08 billion capex on Zinc India mine expansion	<i>Mine expansion 2,077</i>	Zinc India mine expansion capex \$2.077 bn · \$2.077 billion capex on Zinc India mine expansion	2025-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Reduce Holdco debt to \$4.8 billion, lowest level in a decade	<i>we have reduced Holdco. debt to \$4.8 billion, the lowest level in a decade</i>	Holdco debt \$4.8 bn · Holdco debt \$4.8 billion	2024-11-14	H	Holdco debt reduced to almost \$4.4 billion by September end, a decade low	MISSED	4.4 vs 4.8 USD_bn		
2024-11-01	Q2FY25	Q2FY25 transcript	Maintain aluminium cost guidance at \$1,625 to \$1,725 per ton for FY25	<i>we have kept the target the same, \$1625 to 1725</i>	Aluminium cost \$1,625-1,725/t · \$1,625 to \$1,725 per ton	2025-05-15	H	Guidance maintained at \$1,625 to \$1,725 per ton for FY25	MET	1,625 vs 1,625-1,725 USD/t		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve highest-ever first half EBITDA of ₹20,639 crore in 1HFY25	<i>Vedanta is proud to report our highest-ever first-half EBITDA of ₹20,639 crore</i>	1HFY25 EBITDA ₹20,639 crore · ₹20,639 crore EBITDA in 1HFY25		H	Reported record H1 EBITDA of ₹19,224 crore in 1HFY26	MISSED	19,224 vs 20,639 INR_crore		
2024-11-01	Q2FY25	Q2FY25 transcript	Achieve highest-ever annual EBITDA in FY25 by delivering 60% of annual EBITDA in second half	<i>We anticipate achieving our highest-ever annual EBITDA in FY '25 by delivering the remaining 60% in the second half</i>	FY25 annual EBITDA highest-ever with 60% in H2 · highest-ever annual EBITDA in FY25		H	Reported highest-ever annual EBITDA of \$10 billion in FY25	NYT	actual in USD not comparable to % of annual EBITDA		
2024-11-01	Q2FY25	Q2FY25 presentation	Reduce net debt by \$4.7 billion in last 2.5 years	<i>reduced by \$4.7 bn in last 2.5 years</i>	Net debt reduction \$4.7 bn in 2.5 years · Reduce net debt by \$4.7 billion in 2.5 years		H	Net debt reduced by \$4 billion over 3 years as of Mar'25	MET	4 vs 4.7 USD_bn		
2024-11-01	Q2FY25	Q2FY25 transcript	Reduce Vedanta Limited net debt to EBITDA ratio to less than 1x	<i>Net debt to Vedanta will be less than 1x</i>	Net debt/EBITDA < 1x	medium term	H	Net debt to EBITDA ratio reported at almost 0.95x in Q4FY26	MET	0.95 vs 1 x		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2024-11-01	Q2FY25	Q2FY25 transcript	Deleverage Vedanta Resources Limited debt from \$5.8bn to \$3bn by end FY27	<i>at Vedanta Resources, our intent is to go down to 3 billion over 3 years starting the current fiscal</i>	VRL debt \$3bn by FY27 · \$3bn debt by FY27	2027-05-15	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 presentation	Create 6,363 Nand Ghars for women and child welfare	<i>6,363 Nand Ghars created for women and child welfare</i>	6,363 Nand Ghars created	2024-11-14	H	8045 Nand Ghars created as of FY25 year-end	MET	8,045 vs 6,363 units		
2024-11-01	Q2FY25	Q2FY25 presentation	Spend ₹141 crore on CSR initiatives in 1H FY25	<i>Spent INR 141+ crore in 1H FY25 on CSR initiatives</i>	CSR spend ₹141 crore in 1H FY25 · ₹141 crore CSR spend in 1H FY25		H	CSR spend was ₹101.26 crore in 3Q FY26 presentation	MISSED	101.26 vs 141 INR_crore		
2024-11-01	Q2FY25	Q2FY25 presentation	Achieve workplace gender diversity of 22% full-time employees, 7 years ahead of FY30 target	<i>Achieved our workplace gender diversity target for full-time employees 7 years in advance vs FY30 target of 20%. Gender diversity for full-time employees stands at</i>	Workplace gender diversity 22% full-time employees · 22% workplace gender diversity for full-time employees	2024-11-14	H		NYT	no actual reported		
2024-11-01	Q2FY25	Q2FY25 transcript	Complete demerger process on or before 31 March 2025	<i>we are very confident that this will get done on or before 31st of March 2025</i>	Demerger completion by 31 Mar 2025 · on or before 31 March 2025	2025	H	Demerger to start next quarter after Q4 FY26, indicating completion by then	MISSED	slipped ~4 qtrs		
2024-11-01	Q2FY25	Q2FY25 presentation	Complete shareholder and creditor meetings for demerger in coming months	<i>Demerger on track and in its final stages, with shareholder and creditor meetings scheduled in the coming months</i>	Demerger shareholder and creditor meetings in coming months · Shareholder and creditor meetings for demerger in coming months		M	Demerger on track with shareholder and creditor meetings progressing in coming months	NYT	Demerger on track with shareholder and creditor meetings pro		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission BALCO smelter expansion in Q1 FY26	<i>BALCO smelter expansion is now in an advanced stage with commissioning targeted in Quarter 1 of FY '26</i>	BALCO smelter expansion commissioning Q1 FY26 · commission BALCO smelter expansion in Q1 FY26	2025-08-14	H	Commissioning initiated for BALCO smelter expansion in FY26	MET	435 vs 1 quarter		
2025-02-01	Q3FY25	Q3FY25 transcript	Achieve 60-65% captive alumina supply in Q1 FY26	<i>at least 60-65% of our requirement will be met through captive sources</i>	captive alumina supply 60-65% · 60-65% captive alumina supply in Q1 FY26	2025-08-14	H	Captive alumina supply was 60% in Q3 FY26, 70% in Q4 FY26, and expected 80% in Q1 FY27.	MET	80 vs 60-65 %		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission Debari roaster in Q4 FY25	<i>final commissioning targeted for quarter 4 of the current fiscal and quarter 4 of the next fiscal</i>	Debari roaster commissioning Q4 FY25 · commission Debari roaster in Q4 FY25	2025-05-15	H	Debari Roaster commissioned in 1H FY26	MET	160 vs 4 quarter		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission fertilizer plant in Q4 FY26	<i>final commissioning targeted for quarter 4 of the current fiscal and quarter 4 of the next</i>	fertilizer plant commissioning Q4 FY26 · commission fertilizer plant in Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission Ghogarpalli Mine coal extraction in Q4 FY26	<i>original target of Ghogarpalli, quarter 4 of FY '26, they are going to take out the first coal</i>	Ghogarpalli Mine coal extraction Q4 FY26 · first coal extraction in Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	Ramp up KCM copper production to 150-200 KT in next year	<i>next year, I reckon, in the region of 150 to 200</i>	KCM copper production 150-200 KT · 150-200 KT copper production next year	2027-05-15	L		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	Ramp up KCM copper production to 160-175 KT run rate next year	<i>six months of production, we are going to be at a run rate of 160 to 175 kilo tons of</i>	KCM copper production 160-175 KT · 160-175 KT copper production next year	2026-05-15	H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	Meenakshi and Athena power plants to operate at full capacity in FY26	<i>Meenakshi and Athena Power Plants are scheduled to be operating at full capacity in FY '26</i>	Meenakshi and Athena full capacity FY26 · full capacity operation FY26	2026-05-15	H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	Increase merchant power operating capacity to 5 GW within 12-15 months	<i>merchant power operating capacity will increase to 5 Gigawatt within the next 12 to 15 months</i>	merchant power capacity 5 GW within 12-15 months · 5 GW capacity within 12-15 months		H	Merchant power capacity increased to 4.78 GW by FY26, short of 5 GW target within 12-15 months.	PARTIAL	4.78 vs 5 GW		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission Sijimali Mine in Q2 FY26	<i>in the quarter 2, we are going to start the Sijimali</i>	Sijimali Mine commissioning Q2 FY26 · commission Sijimali Mine in Q2 FY26	2025-11-14	H	Commissioning re-guided to 1H FY27	MISSED	1 vs 2 quarter		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-02-01	Q3FY25	Q3FY25 transcript	Commission 250,000 tpa smelter phase by FY27/28	targeting to commission the next phase of 250,000 tons per annum of smelter by FY '27/'28	smelter phase commissioning 250,000 tpa by FY27/28 · commission 250,000 tpa smelter phase by FY27/28		H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission Train 2 of Lanjigarh Refinery in Q4 FY25	Train 2 is scheduled for commissioning in quarter 4 of current fiscal year	Train 2 commissioning Q4 FY25 · commission Train 2 in Q4 FY25	2025-05-15	H	Train 2 commissioning started; first alumina output achieved by Q2 FY26	MISSED	1 vs 4 quarter		
2025-02-01	Q3FY25	Q3FY25 presentation	Commission Train 2 of 1.5 MTPA Lanjigarh Expansion project in Q4FY25	Commissioning of Train 2 of 1.5 MTPA of Lanjigarh Expansion project in Q4FY25	Train 2 Lanjigarh 1.5 MTPA by Q4FY25 · 1.5 MTPA Lanjigarh Train 2 by Q4FY25	2025-05-15	H	Train 2 Lanjigarh produced first alumina output, commissioning started but full 1.5 MTPA capacity not explicitly reported	MET	3 vs 1.5 MTPA		
2025-02-01	Q3FY25	Q3FY25 presentation	Increase Value Added Product capacity to 68% by Jan 2025	Current Value Added Product Capacity increased to 68%	VAP capacity 68% by Jan 2025 · 68% VAP capacity by Jan 2025	2025	H	Reported VAP capacity reached 68% by Jan 2025 as targeted	MET	68 vs 68 %		
2025-02-01	Q3FY25	Q3FY25 transcript	Commission Zinc International Phase-2 expansion in FY26	Phase-2 expansion project is in full swing with commissioning targeted in FY '26	Zinc International Phase-2 commissioning FY26 · commission Zinc International Phase-2 in FY26	2026-05-15	H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 presentation	Spend ₹254 crore on CSR initiatives in 9MFY25	Spent ₹ 254 crore in 9month FY'25 on CSR initiatives	CSR spend ₹254 crore in 9MFY25 · ₹254 crore CSR spend in 9MFY25		H	CSR spend was ₹101.26 crore in 9MFY25 as per Q3FY26 presentation	MISSED	101.26 vs 254 INR_cr		
2025-02-01	Q3FY25	Q3FY25 transcript	Reduce alumina cost to ₹320-325/t for the year	the alumina cost should be closer to the levels of 320-325 for the year	Alumina cost ₹320-325/t · ₹320-325/t alumina cost for the year	2025-05-15	H	Alumina cost around \$750/t in Q2FY26, higher due to Middle East raw material impact	NYT	actual in \$/t not comparable to INR/t		
2025-02-01	Q3FY25	Q3FY25 transcript	Reduce aluminum hot metal cost to ~\$1,800/t for FY25	for the year as a whole, we should be somewhere around \$1,800 on the hot metal cost	Aluminum hot metal cost \$1,800/t · \$1,800/t hot metal cost for FY25	2025-05-15	H	Hot metal cost was \$1,826/t in Q2FY26, slightly above the \$1,800/t target for FY25.	PARTIAL	1,826 vs 1,800 USD/t	Power cost increased by \$75/t and other costs increased by \$40/t, offset partially by \$53/t alumina cost reduction.	Cost inflation
2025-02-01	Q3FY25	Q3FY25 transcript	Reduce power cost by \$20-\$25 in Q4 FY25	Another \$20-\$25 we believe will come down in quarter 4	Power cost reduction \$20-\$25 · \$20-\$25 power cost reduction in Q4 FY25	2025-05-15	H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	Reduce power cost by \$30-\$40 from operating efficiencies	\$30-\$40 will come out of the operating efficiencies	Power cost reduction \$30-\$40 · \$30-\$40 power cost reduction from efficiencies		M	Power cost expected to be sub \$500 per ton in H2 FY26 after timely power plant shutdown	MISSED	500 vs 30-40 USD		
2025-02-01	Q3FY25	Q3FY25 transcript	Reduce Zinc International production cost to \$1,200-\$1,300 per ton	cost range between \$1,200 and \$1,300	Zinc International production cost \$1,200-\$1,300/t · \$1,200-\$1,300 per ton cost		H	Zinc International production cost was \$940 per ton in Q3FY26, lowest in 5 years	MET	940 vs 1,200-1,300 USD/t		
2025-02-01	Q3FY25	Q3FY25 presentation	Deliver highest ever 3Q EBITDA of ₹11,284 crore	highest-ever 3rd Quarter EBITDA of ₹11,284 crore	3QFY25 EBITDA ₹11,284 crore · ₹11,284 crore EBITDA in 3QFY25	2025-02-14	H	3QFY26 EBITDA was ₹15,171 crore, highest-ever reported	MET	15,171 vs 11,284 INR_cr		
2025-02-01	Q3FY25	Q3FY25 transcript	Generate annual EBITDA of ₹150-160 crore from alloy plant	have achieved the run rate of generating annual EBITDA of 150 to 160 crores	annual EBITDA ₹150-160 cr		H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	Deliver \$10 billion EBITDA in the future	we continue our journey to deliver 10 billion USD EBITDA in the future	EBITDA \$10 bn · future		L	Achieved best ever quarterly EBITDA of Rs.15,171 crores in Q3FY26	NYT	actual in INR crores not comparable to USD_bn		
2025-02-01	Q3FY25	Q3FY25 transcript	Deliver highest ever yearly EBITDA in FY25	we are confident of delivering the highest ever yearly EBITDA in FY '25	FY25 EBITDA highest ever · highest ever EBITDA in FY25	2025-05-15	H	Reported second highest EBITDA in FY25 at Rs. 43,541 crores	MET	43,541 vs 25		
2025-02-01	Q3FY25	Q3FY25 transcript	Bring net debt/EBITDA ratio below 1x	progressing towards our target of bringing this ratio below 1x	Net debt/EBITDA < 1x · net debt/EBITDA below 1x		M	Net debt/EBITDA ratio reported at 0.95x pre-demerger as of Q4FY26	MET	0.95 vs 1 x		
2025-02-01	Q3FY25	Q3FY25 presentation	Maintain net debt to EBITDA ratio at 1.4x in 3QFY25	Net debt to EBITDA ratio improved to 1.4x	Net debt/EBITDA 1.4x · Net debt/EBITDA 1.4x in 3QFY25	2025-02-14	H	Net debt to EBITDA ratio was 0.37x in 3QFY26 (Dec'25)	MET	0.37 vs 1.4 x		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-02-01	Q3FY25	Q3FY25 presentation	Achieve EBITDA margin of 34% in 3QFY25	<i>EBITDA margin1 at 34% in 3QFY25</i>	3QFY25 EBITDA margin 34% · 34% EBITDA margin in 3QFY25	2025-02-14	H	EBITDA margin was 41% in 3QFY26, exceeding the 34% target for 3QFY25	MET	41 vs 34 %		
2025-02-01	Q3FY25	Q3FY25 presentation	Achieve profit after tax of ₹4,876 crore in 3QFY25	<i>Profit after tax at ₹ 4,876 crore</i>	3QFY25 PAT ₹4,876 crore · ₹4,876 crore PAT in 3QFY25	2025-02-14	H	PAT was ₹4,961 crore in 4QFY25, exceeding the 3QFY25 target of ₹4,876 crore	MET	4,961 vs 4,876 INR_cr		
2025-02-01	Q3FY25	Q3FY25 presentation	Hold shareholders and creditors meeting for demerger in February 2025	<i>shareholders' and creditors' meeting scheduled for February 2025</i>	Demerger meeting in Feb 2025 · February 2025	2025	H		NYT	no outcome reported		
2025-02-01	Q3FY25	Q3FY25 presentation	Complete Gamsberg Phase 2 project in 2HFY26	<i>Project completion targeted in 2HFY26</i>	Gamsberg Phase 2 completion by 2HFY26 · 2HFY26		H	Gamsberg Phase 2 is 94% complete; commissioning expected next quarter, ramp-up planned for rest of FY26.	MET	on time		
2025-04-01	Q4FY25	Q4FY25 transcript	Ramp up aluminum production to just over 3 million tons in FY26 with exit run rate close to 4 million tons	<i>for us, we intend to be at an exit run rate of close to 4 million tons. And the total production for the year will</i>	Aluminum production >3 Mt in FY26, exit run rate ~4 Mt · >3 Mt production in FY26, ~4 Mt exit run rate	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Reach 5 million tons aluminum production run rate by FY27	<i>of the 5 million tons by FY '27, we hope to be close to those numbers. But to</i>	Aluminum production run rate 5 Mt by FY27 · 5 Mt run rate by FY27	2027-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission Athena power plant Unit-1 in first half of current fiscal year	<i>Unit-1 of Athena power plant is also scheduled for commissioning in first half of this fiscal year</i>	Athena power plant Unit-1 commissioning by H1FY26 · Unit-1 commissioning by H1FY26		H	Athena Unit-1 commissioning re-set to second half of FY26	MET	-1 vs -1		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission Athena power plant Unit-2 by March 2026	<i>Unit-2 is expected to start operation in March '26</i>	Athena power plant Unit-2 commissioning by Mar 2026 · Unit-2 commissioning by Mar 2026	2026	H	Athena power plant Unit-2 commissioning status not explicitly reported; Athena is described as newly commissioned in 2QFY26	MET	45 vs -2		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission BALCO smelter expansion of 435,000 tpa in first half of current financial year	<i>the train targeted in the current quarter. The BALCO smelter expansion of 435,000 tons per annum is in</i>	BALCO smelter expansion 435,000 tpa by H1FY26 · 435,000 tpa by H1FY26		H	Commissioning initiated for 435,000 tpa BALCO smelter expansion	MET	4,35,000 vs 4,35,000 tons per annum		
2025-04-01	Q4FY25	Q4FY25 transcript	Start BALCO smelter first metal by end of Q1FY26	<i>we are still maintaining the guidance of the first metal at end of the Quarter 1</i>	BALCO smelter first metal by Q1FY26 end · first metal by Q1FY26 end	2025-08-14	H	First metal production started from 20 pots; full smelter ramp-up expected over next 3-6 months after March end.	MET	20,000 vs 1		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission 160,000 tpa roaster at Debari in current quarter	<i>160,000 tons per annum roaster at Debari will be commissioned in the current quarter</i>	Debari roaster 160,000 tpa by Q4FY25 · 160,000 tpa by Q4FY25	2025-05-15	H	Debari roaster commissioning anticipated next quarter; project 94% complete	MISSED	94 vs 1,60,000 tons per annum	Delay due to waste stripping catch-up at Gamsberg open pit over last two years	Capacity delay
2025-04-01	Q4FY25	Q4FY25 transcript	Increase ESL hot metal capacity from 1.7 to 3.2 million tons per annum by FY26 end	<i>expecting total hot metal capacity to increase from 1.7 million tons to 3.2 million tons per annum by FY '26 end</i>	ESL hot metal capacity 3.2 Mtpa by FY26 end · 3.2 Mtpa by FY26 end	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Further debottleneck ESL hot metal capacity to 3.5 million tons per annum by FY27	<i>plans to further debottlenecking to 3.5 million tons per annum in FY '27</i>	ESL hot metal capacity 3.5 Mtpa by FY27 · 3.5 Mtpa by FY27	2027-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission 510,000 tpa fertilizer plant in Q4FY25	<i>510,000 tons per annum fertilizer plant in Quarter 4 of this current fiscal year</i>	Fertilizer plant 510,000 tpa by Q4FY25 · 510,000 tpa by Q4FY25	2025-05-15	H	Commissioning re-set to 1HFY27	MET	5,10,000 vs 5,10,000 tons per annum		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Alumina production guidance of 3.0-3.1 million tonnes including trial run production	<i>Alumina 3.0-3.1 Mnt</i>	FY26 Alumina production 3.0-3.1 Mt · 3.0-3.1 Mt Alumina production FY26	2026-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Aluminium production guidance of 2.5-2.6 million tonnes including trial run production	<i>Aluminium1 2.5-2.6 Mnt</i>	FY26 Aluminium production 2.5-2.6 Mt · 2.5-2.6 Mt Aluminium production FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 ESL hot metal production guidance 1.5-1.6 Mnt	<i>Hot Metal 1.5-1.6 Mnt</i>	FY26 ESL hot metal 1.5-1.6 Mt · 1.5-1.6 Mt ESL hot metal FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 FACOR ferrochrome production guidance 100-110 kt	<i>Ferrochrome 100 – 110 kt</i>	FY26 FACOR ferrochrome 100-110 kt · 100-110 kt FACOR ferrochrome FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Iron Ore Goa production guidance 2.2-2.7 Mnt	<i>Goa 2.2 – 2.7 Mnt</i>	FY26 Iron Ore Goa 2.2-2.7 Mt · 2.2-2.7 Mt Iron Ore Goa FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Iron Ore Karnataka production guidance 5.5-6.1 Mnt	<i>Karnataka 5.5 – 6.1 Mnt</i>	FY26 Iron Ore Karnataka 5.5-6.1 Mt · 5.5-6.1 Mt Iron Ore Karnataka FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Iron Ore Orissa production guidance 4.5-5.2 Mnt	<i>Orissa 4.5 – 5.2 Mnt</i>	FY26 Iron Ore Orissa 4.5-5.2 Mt · 4.5-5.2 Mt Iron Ore Orissa FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Oil & Gas average gross volume guidance 95-100 kboepd	<i>Average Gross Volume 95-100 kboepd</i>	FY26 Oil & Gas gross volume 95-100 kboepd · 95-100 kboepd Oil & Gas gross volume FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Pig Iron production guidance 950-1050 kt	<i>Pig Iron 950 - 1050 kt</i>	FY26 Pig Iron 950-1050 kt · 950-1050 kt Pig Iron FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Zinc India finished metal production guidance 1,090-1,100 kt	<i>Finished Metal 1,090 – 1,100 kt</i>	FY26 Zinc India finished metal 1,090-1,100 kt · 1,090-1,100 kt Zinc India finished metal FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Zinc India mined metal production guidance 1,115-1,135 kt	<i>Mined Metal 1,115 - 1,135 kt</i>	FY26 Zinc India mined metal 1,115-1,135 kt · 1,115-1,135 kt Zinc India mined metal FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Zinc India silver production guidance 700-710 tonnes	<i>Silver 700 - 710 tonnes</i>	FY26 Zinc India silver production 700-710 t · 700-710 t Zinc India silver production FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Zinc International BMM production guidance 55-65 kt	<i>BMM 55 - 65 kt</i>	FY26 Zinc International BMM production 55-65 kt · 55-65 kt BMM production FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Zinc International Gamsberg production guidance 180-200 kt	<i>Gamsberg 180 - 200 kt</i>	FY26 Zinc International Gamsberg production 180-200 kt · 180-200 kt Gamsberg production FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Start Ghogharpalli coal mine operations in last quarter of FY26	<i>for our Ghogharpalli coal mines, we are expected that we are going to commence the operation from last quarter of the FY '26</i>	Ghogharpalli coal mine start Q4FY26 · start Q4FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Ramp up Konkola Copper Mine production to about 150,000 tons in 2026	<i>market guidance in October, we said that we will do about 150,000 tons of copper in</i>	Konkola Copper Mine production ~150,000 tons in 2026 · ~150,000 tons in 2026	2026	H	Konkola Copper Mine producing about 108,000 tons annually as of H1 FY26	MISSED	1,08,000 vs 1,50,000 tons		
2025-04-01	Q4FY25	Q4FY25 transcript	Start Kuraloi coal mine operations in Q3FY26	<i>the Kuraloi mines, which we have said, in the Quarter 3 FY '26, we are going to commence the operation</i>	Kuraloi coal mine start Q3FY26 · start Q3FY26	2026-02-14	H	Mining lease received recently; operations expected to start in about a month from April 2026.	NYT	Mining lease received recently; operations expected to start		
2025-04-01	Q4FY25	Q4FY25 transcript	Achieve 3.1 million tons aluminum production from Lanjigarh in FY26	<i>we are planning to have the production of 3.1 million tons of production</i>	Lanjigarh aluminum production 3.1 Mt in FY26 · 3.1 Mt in FY26	2026-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-04-01	Q4FY25	Q4FY25 transcript	Commission Lanjigarh Refinery Train 2 with first metal production in current quarter	<i>on track to commissioning the Lanjigarh Refinery Train 2 with the first metal production from the train targeted in the current quarter</i>	Lanjigarh Refinery Train 2 first metal production in Q4FY25 · first metal production in Q4FY25	2025-05-15	H	First alumina output from Train II achieved by Q2FY26	MISSED	1 vs 4		
2025-04-01	Q4FY25	Q4FY25 transcript	Commission remaining 700 MW of Meenakshi power plant in first half of current fiscal year	<i>remaining 700-megawatt capacity is targeted for commissioning in the first half of this current fiscal year</i>	Meenakshi power plant 700 MW by H1FY26 · 700 MW by H1FY26		H	Meenakshi power plant capacity increased by 950 MW by 31 March 2026, exceeding the 700 MW target for H1FY26	MET	950 vs 700 MW		
2025-04-01	Q4FY25	Q4FY25 transcript	Start Sijimali mine operations by Q2FY26	<i>We are targeting that we are going to get the EC in the June 2025. So we are hopeful that we are</i>	Sijimali mine start Q2FY26 · start Q2FY26	2025-11-14	H	Sijimali mine commissioning re-set to 1HFY27	MISSED	1 vs 2		Capacity delay
2025-04-01	Q4FY25	Q4FY25 transcript	Start Sijimali mine operations by Q2FY26 with full ramp-up by Q4FY26	<i>we are ready with the Sijimali. We are hopeful that the Quarter 3 we are going to start</i>	Sijimali mine start Q3FY26, full ramp-up by Q4FY26 · start Q3FY26, full ramp-up by Q4FY26	2026-02-14	H	Sijimali mine commissioning re-set to 1HFY27	MISSED	1 vs 3	Delay due to waste stripping catch-up at Gamsberg open pit, impacting schedule	Capacity delay
2025-04-01	Q4FY25	Q4FY25 transcript	Commission Zinc International Phase-2 expansion in second half of current fiscal year	<i>Phase-2 expansion project is targeting commissioning in the second half of the current fiscal year</i>	Zinc International Phase-2 expansion commissioning by H2FY26 · commissioning by H2FY26		H	Commissioning delayed; not achieved in H2FY26 as originally guided	MET	2 vs 2		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 capex guidance of \$1.5 billion for Cairn India	<i>Capex approved for Cairn represents Net capex, however Gross capex is \$1.5 bn</i>	FY26 Cairn capex \$1.5 bn	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 capex focused on volume expansion and supply chain integration	<i>Total capital expenditure in the year stood at ₹ 12,626 crores, focused on volume expansion and supply chain integration</i>	FY26 capex = ₹12,626 crore	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Invest just over \$300 million in Konkola Copper Mine in current financial year	<i>we will probably invest just over \$300 million for this financial year</i>	KCM investment >\$300 mn in FY26 · just over \$300 million in FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Invest \$1 billion over five years in Konkola Copper Mine	<i>investment that we have committed to the government of Zambia of \$1 billion over five years</i>	KCM investment \$1 bn over 5 years · \$1 billion over 5 years		H	\$150 million invested in first half of year, compliant with shareholder agreement	MET	150 vs 1 USD_bn		
2025-04-01	Q4FY25	Q4FY25 transcript	Maintain brand fee income of \$400 million for Vedanta Resources	<i>are right, it remains 3%. That number is almost \$400 million in the current</i>	Brand fee income \$400 mn · \$400 mn brand fee		H	Brand fee income maintained at about \$400 million as stated in Q4FY26 transcript.	MET	400 vs 400 USD_mn		
2025-04-01	Q4FY25	Q4FY25 transcript	Maintain dividend yield at about 6% for Vedanta Resources	<i>Even if you pay a normalized dividend with about 6% yield</i>	Dividend yield ~6% · ~6% dividend yield		M	Dividend yield lowered to almost 4% yield, below the ~6% target	MISSED	5 vs 6 %	Lower dividend yield due to managing VRL cash flow and contractual brand fee obligations	Capital allocation
2025-04-01	Q4FY25	Q4FY25 transcript	Deleverage Vedanta Resources by \$600 million in FY26	<i>by paying almost half the dividend than the recent average, we can deleverage Vedanta Resources by \$600 million in the current fiscal</i>	Vedanta Resources deleveraging \$600 mn in FY26 · \$600 mn deleveraging in FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Reduce alumina cost to around \$340-350 per ton in Q1FY26	<i>in Quarter 1, we expect this cost to be somewhere around \$340, \$350</i>	Alumina cost \$340-350/t in Q1FY26 · \$340-350/t in Q1FY26	2025-08-14	H	Alumina cost was around \$800 per ton in Q3FY26, above target range for Q1FY26.	MISSED	800 vs 340-350 USD/t	Higher alumina cost due to LME price surge and captive production costs exceeding market price.	Pricing / mix
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Aluminium cost of production guidance \$1,700-1,750/t	<i>CoP2 \$1,700/t - \$1,750/t</i>	FY26 Aluminium CoP \$1,700-1,750/t · \$1,700-1,750/t Aluminium CoP FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Oil & Gas operating expense guidance \$15-16/boe	<i>Opex \$15-16/boe</i>	FY26 Oil & Gas Opex \$15-16/boe · \$15-16/boe Oil & Gas Opex FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 Zinc India cost of production guidance \$1,025-1,050/t excluding royalty	<i>CoP3 \$1,025/t - \$1,050/t</i>	FY26 Zinc India CoP \$1,025-1,050/t · \$1,025-1,050/t Zinc India CoP FY26	2026-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-04-01	Q4FY25	Q4FY25 transcript	Reduce power cost by \$40-45 per ton in Q1FY26	<i>we expect another \$40, \$45 coming from the power cost</i>	Power cost reduction \$40-45/t in Q1FY26 · \$40-45/t reduction in Q1FY26	2025-08-14	H	Power cost increased by \$75 per ton in Q2FY26, offset by other cost reductions.	MISSED	75 vs 40-45 USD/t	Power cost rose due to planned power plant shutdown and maintenance.	Capacity delay
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 EBITDA of ₹43,541 crore, 2nd highest ever, up 37% YoY	<i>EBITDA stood at ₹ 43,541 crore – 2nd Highest Ever, up 37% YoY</i>	FY26 EBITDA = ₹43,541 crore	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	Vedanta Resources committed to deleveraging by \$3bn in next three years	<i>VRL committed to deleverage by \$ 3bn in next three years</i>	Deleverage \$3bn · \$3bn deleveraging in 3 years		H	Debt reduced from \$8.9bn to \$4.4bn as of September end, nearing decade low	MISSED	4.4 vs 3 USD_bn		
2025-04-01	Q4FY25	Q4FY25 transcript	Achieve group deleveraging of \$1.2 billion in FY25	<i>All these actions have supported us in achieving a deleveraging of \$1.2 billion at group</i>	Group deleveraging \$1.2 bn in FY25 · \$1.2 bn in FY25	2025-05-15	H	Group deleveraging in FY26 expected around \$0.8 to \$1 billion, short of \$1.2 billion FY25 target	MET	0.9 vs 1.2 USD_bn		
2025-04-01	Q4FY25	Q4FY25 transcript	Improve group leverage ratio to 2x from 2.7x a year ago	<i>leverage at the group level has improved to 2x from 2.7x a year ago</i>	Group leverage ratio 2x · 2x leverage ratio		H	Leverage ratio improved to 1.88x as of Q2FY26, down from 2.7x a year ago	MET	1.88 vs 2 x		
2025-04-01	Q4FY25	Q4FY25 transcript	Maintain net debt-to-EBITDA ratio at 1.2x	<i>net debt-to-EBITDA ratio, which has improved to 1.2x</i>	Net debt/EBITDA ratio 1.2x · 1.2x net debt/EBITDA		H	Net debt-to-EBITDA ratio reported at 0.95x at fiscal year end FY26	MET	0.95 vs 1.2 x		
2025-04-01	Q4FY25	Q4FY25 transcript	Reduce parent company VRL debt to \$5 billion	<i>debt of our parent Company, VRL, has decreased to \$5 billion</i>	VRL debt \$5 bn · \$5 bn		H	VRL debt at \$4.7 billion as of Q4FY26	MET	4.7 vs 5 USD_bn		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 TSPL PAF guidance of 85%	<i>International ESL FACOR Power TSPL PAF</i>	FY26 TSPL PAF 85% · 85% TSPL PAF FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 PAT of ₹20,535 crore, up 172% YoY	<i>PAT jumps 172% YoY to ₹ 20,535 crores</i>	FY26 PAT = ₹20,535 crore	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	FY26 revenue growth of 10% YoY	<i>Highest-Ever Consolidated Revenue at ₹ 1,50,725 crore, up 10% YoY</i>	FY26 revenue > ₹1,50,725 crore	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Complete demerger by September 2025	<i>We anticipate completing the demerger by September 2025</i>	Demerger completion by Sep 2025 · by September 2025	2025	H	Demerger accounting incorporated in Q3FY26 results after NCLT order on Dec 16, 2025	NYT	in progress, not yet due		
2025-04-01	Q4FY25	Q4FY25 transcript	Increase domestic share of value-added aluminum products quarter-on-quarter	<i>second is on domestic share, both of which we are seeing a rise</i>	Domestic share of value-added aluminum products rising QoQ · rising QoQ		M	Value-added aluminum product sales volume was 353kt in 1QFY26, 355kt in 2QFY26, and 354kt in 3QFY26, showing no consistent QoQ increase.	NYT	no numeric target		
2025-04-01	Q4FY25	Q4FY25 transcript	Increase oil and gas production contribution from DSF fields to 20-25% in 18-24 months	<i>objective is to move to that 20%-25% in at least 18 to 24 months</i>	DSF fields contribution 20-25% in 18-24 months · 20-25% in 18-24 months		M	ASP project commissioning delayed; startup expected within next three months	NYT	ASP project commissioning delayed; startup expected within n		
2025-04-01	Q4FY25	Q4FY25 transcript	Increase oil and gas production contribution from OALP blocks to 8-10% by Q4FY26	<i>trying to figure out whether we can reach around 8% to 10% by Q4</i>	OALP blocks contribution 8-10% by Q4FY26 · 8-10% by Q4FY26	2026-05-15	M		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	Increase oil and gas production volume to around 98-99 kboepd in Q1FY26	<i>onwards. We will be at around 98, 99 in this</i>	Oil & gas production ~98-99 kboepd in Q1FY26 · ~98-99 kboepd in Q1FY26	2025-08-14	H	Production was 93.2 kboepd in 1QFY26, below the target of 98-99 kboepd.	PARTIAL	93.2 vs 98-99 kboepd	Production decline due to natural decline and lower well intervention activities.	Execution
2025-04-01	Q4FY25	Q4FY25 transcript	Increase oil and gas production volume from Q2FY26 onwards with higher volumes in Q3 and Q4	<i>expect that our volume trajectory will go up from Q2 onwards. We will</i>	Oil & gas volume growth from Q2FY26 onwards · growth from Q2FY26 onwards	2025-11-14	H	3QFY26 production was 85 kboepd, lower than expected due to natural decline and delayed project commissioning.	MET	85 vs 2		
2025-04-01	Q4FY25	Q4FY25 transcript	Increase value-added aluminum product sales to around 70% in FY26	<i>next year we expect it to be somewhere around 70% as we ramp up the VAP facilities</i>	Value-added aluminum sales ~70% in FY26 · ~70% in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Alumina capacity to reach 5 MTPA in FY26 and 6 MTPA in FY28	<i>(5 MTPA in FY26, 6 MPTA - FY28)</i>	Alumina capacity 5 MTPA FY26, 6 MTPA FY28 · 5 MTPA in FY26, 6 MTPA in FY28		H	Lanjigarh alumina capacity expanded to 5 MTPA in FY26 with Train-2 commissioned	MET	5 vs 5-6 MTPA		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-08-01	Q1FY26	Q1FY26 transcript	Expand alumina capacity to 6 million tons by end FY27	the 2.8 million mark. And then in terms of the overall expansion from 5 to 6 million tons	Alumina capacity 6 million tons by FY27-end · 6 million tons by FY27-end	2027-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Expand aluminium capacity to 2.8-2.85 million tons in FY26	focus is to reach to 2.8, 2.85 million tons at both the places at Balco as well as at Jharsuguda	Aluminium capacity 2.8-2.85 million tons in FY26 · 2.8-2.85 million tons in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Aluminium smelting capacity to reach 3.1 MTPA by FY28	Smelting Capacity (MTPA) (3.1 MTPA by FY28)	Aluminium smelting capacity 3.1 MTPA by FY28 · 3.1 MTPA by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Athena power capacity to reach 1,200 MW by end FY26	Athena, as we have guided, we have only commissioned the 600 Megawatts. The remaining 600 Megawatts will come at the end	Athena power 1,200 MW by end FY26 · 1,200 MW by end FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Expand BALCO smelter and VAP capacity, Lanjigarh refinery to 5 MTPA, increase VAP to 2.5 MTPA, debottleneck Lanjigarh to 6 MTPA, smelter capacity to 3.1 MTPA and VAP to 2.8 MTPA	• Ghogarpalli Coal Mine • Debottlenecking to 6 MTPA at Lanjigarh • Smelter capacity expansion to 3.1 MTPA & VAP to 2.8 MTPA	BALCO smelter and VAP expansion, Lanjigarh refinery 5 MTPA, VAP 2.5-2.8 MTPA, Lanjigarh debottleneck 6 MTPA, smelter 3.1 MTPA		H	BALCO smelter ramped to 2.8 MTPA; Lanjigarh refinery close to 5 MTPA run rates	MISSED	2.8 vs 5-6 MTPA		
2025-08-01	Q1FY26	Q1FY26 transcript	Commission 160,000 tpa roaster at Debari in Q2FY26	targeting the commissioning of a 160,000 ton per annum roaster at Debari and in the current quarter	Commission 160,000 tpa roaster at Debari by Q2FY26 · by Q2FY26	2025-11-14	H	160,000 tpa Debari Roaster commissioning scheduled for 1HFY26	MET	1,60,000 vs 1,60,000 tons per annum		
2025-08-01	Q1FY26	Q1FY26 transcript	Commission 350 MW Meenakshi Unit 4 in August 2025	An additional 350 Megawatts at Meenakshi, Unit 4, is planned for commissioning in August	Commission 350 MW Meenakshi Unit 4 in Aug 2025 · August 2025	2025	H	Meenakshi Unit 4 (350 MW) operationalized by 2QFY26 (before August 2025 target)	MISSED	350 vs 2,025		
2025-08-01	Q1FY26	Q1FY26 transcript	Commission 600 MW Athena Unit 2 in Q4FY26	Athena, Unit 2, with a capacity of 600 Megawatts, is scheduled for commissioning in Quarter 4	Commission 600 MW Athena Unit 2 in Q4FY26 · Q4FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Commission BALCO smelter, Lanjigarh Train-2, Sijimali Bauxite Mine and Kuraloi Coal Mine in FY26	FY26: Commissioning of BALCO Smelter, Lanjigarh Train-2, Sijimali Bauxite Mine and Kuraloi Coal Mine	Commission BALCO smelter, Lanjigarh Train-2, Sijimali Bauxite Mine and Kuraloi Coal Mine in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Commission Ghogarpalli Coal Mine in FY27	Kuraloi Coal Mine FY27: Commissioning of	Commission Ghogarpalli Coal Mine in FY27	2027-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Commission Lanjigarh Train II and 435,000 tpa Balco smelter in Q2FY26	commissioning of Lanjigarh Train II and the 435,000 tons per annum Balco smelter is targeted in the current quarter	Commission Lanjigarh Train II and 435,000 tpa Balco smelter by Q2FY26 · by Q2FY26	2025-11-14	H	Lanjigarh Train II produced first alumina; BALCO smelter produced first metal, commissioning ongoing	MISSED	1 vs 2		
2025-08-01	Q1FY26	Q1FY26 transcript	Complete Gamsberg Phase-2 project in H2FY26	complete the Gamsberg Phase-2 project in the second half of the current financial year	Complete Gamsberg Phase-2 by H2FY26 · by H2FY26		H	Project 94% complete; commissioning expected in Q1FY27, ramp-up thereafter.	MET	94 vs 2		
2025-08-01	Q1FY26	Q1FY26 presentation	Ferrochrome capacity to reach 500 KTPA by FY28	Ferrochrome Capacity (KTPA) (500 by FY28) 145 → 500	Ferrochrome capacity 500 KTPA by FY28 · 500 KTPA by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Increase ferrochrome HCFC capacity to 450 KTPA by FY28	New 300 KTPA smelter will take the plant capacity to 450 KTPA	Ferrochrome HCFC capacity 450 KTPA by FY28 · 450 KTPA by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Increase ferrochrome HCFC volume to 390 KTPA by FY28	s s 145 145 145 FY25 FY26e FY27e FY28e	Ferrochrome HCFC volume 390 KTPA by FY28 · 390 KTPA by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Increase ferrochrome smelter plant production to 500 KTPA by FY28	Smelter Plant Production to 500 KTPA	Ferrochrome smelter plant production 500 KTPA by FY28 · 500 KTPA by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Iron & Steel smelting capacity to reach 1.38 MTPA by FY29	1.1 → 1.13 →1.38* Smelting Capacity (MTPA) (1.38 MTPA by FY29)	Iron & Steel smelting capacity 1.38 MTPA by FY29 · 1.38 MTPA by FY29	2029-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-08-01	Q1FY26	Q1FY26 presentation	Increase iron ore production to 6.5 MTPA by FY28	<i>Iron Ore Production (MTPA) Pig Iron Production (KTPA) 118 137 FY25</i>	Iron ore production 6.5 MTPA by FY28 · 6.5 MTPA by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Increase iron ore VAP DI pipe production to 780 KTPA by FY28	<i>700 780 400 420 FY25 FY26e FY27e FY28e VAP</i>	Iron ore VAP DI pipe production 780 KTPA by FY28 · 780 KTPA by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Meenakshi power capacity to reach 1,000 MW by end Q2FY26	<i>Meenakshi, by the end of this quarter or the end of Quarter 2, will have the full 1,000 Megawatts power</i>	Meenakshi power 1,000 MW by end Q2FY26 · 1,000 MW by end Q2FY26	2025-11-14	H	1.6 GW commissioned at Meenakshi by Q3FY26, total capacity 4.2 GW, expected 4.8 GW by H1FY27	MET	1,600 vs 1,000 MW		
2025-08-01	Q1FY26	Q1FY26 presentation	Merchant iron ore capacity to reach 17 MTPA in FY28 and 30 MTPA later	<i>Merchant Iron Ore (MTPA) (17 MTPA in FY28) 12 →17 → 30</i>	Merchant iron ore capacity 17 MTPA FY28, 30 MTPA later · 17 MTPA in FY28, 30 MTPA later		H	Merchant iron ore capacity reported as 0.623 MTPA in 1H FY26, no update on FY28 target	MISSED	0.62 vs 17-30 MTPA		
2025-08-01	Q1FY26	Q1FY26 presentation	Merchant power capacity to reach 4.78 GW by FY26	<i>Merchant Power Capacity (GW) (FY26) 2.9 → 4.78</i>	Merchant power capacity 4.78 GW by FY26 · 4.78 GW by FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Increase merchant power capacity from 2880 MW as on FY25 to 4180 MW by H1 FY26	<i>MW Athena) Capacity As on 31st March 2025: 2880MW As on</i>	Merchant power capacity 4180 MW by H1 FY26 · 4180 MW by H1 FY26		H	Merchant power capacity reached 3,889 MW by Q2FY26, short of 4,180 MW target for H1 FY26	MISSED	3,889 vs 4,180 MW	Lower PLF at Jharsuguda expected to improve in upcoming quarters	Execution
2025-08-01	Q1FY26	Q1FY26 presentation	Increase merchant power capacity from 2880 MW as on FY25 to 4780 MW by H2 FY26	<i>MW Athena) Capacity As on 31st March 2025: 2880MW As on</i>	Merchant power capacity 4780 MW by H2 FY26 · 4780 MW by H2 FY26		H	Meenakshi Power Plant Units 3&4 (700 MW total) operationalized by Q2 FY26, increasing merchant power capacity	MISSED	3,530 vs 4,780 MW		
2025-08-01	Q1FY26	Q1FY26 presentation	Oil production to reach 125 kboepd in FY28 and 150 kboepd later	<i>Oil Production (kboepd) (125 kboepd in FY28)</i>	Oil production 125 kboepd FY28, 150 kboepd later · 125 kboepd in FY28, 150 kboepd later		H	3QFY26 oil production was 85 kboepd, below target due to natural decline and lower well intervention activities	MISSED	85 vs 125-150 kboepd	Natural decline and lower well intervention activities in Cambay block	Execution
2025-08-01	Q1FY26	Q1FY26 presentation	Increase pig iron production to 4.5 KTPA by FY28	<i>Iron Ore Production (MTPA) Pig Iron Production (KTPA) 118 137 FY25 FY27e</i>	Pig iron production 4.5 KTPA by FY28 · 4.5 KTPA by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Silver capacity to reach 830 TPA by FY29	<i>Silver 800 → 830 Silver Capacity (TPA)</i>	Silver capacity 830 TPA by FY29 · 830 TPA by FY29	2029-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Steel capacity to reach 3.5 MTPA by FY28	<i>Steel Capacity (MTPA) (3.5 MTPA by FY28) 1.7 → 3.5**</i>	Steel capacity 3.5 MTPA by FY28 · 3.5 MTPA by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Zinc India MIC capacity to reach 525 KTPA by FY26	<i>325 → 525 MIC Capacity (KTPA) (525 by FY26)</i>	Zinc India MIC capacity 525 KTPA by FY26 · 525 KTPA by FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Increase Zinc International mine capacity to 525,000 tpa by H2FY26	<i>increasing operational mine capacity of Zinc International to 525,000 tons per annum</i>	Zinc International mine capacity 525,000 tpa by H2FY26 · 525,000 tpa by H2FY26		H	Capacity ramp-up for Zinc International mine expansion is targeted in Q1FY27, not H2FY26 as promised.	MISSED	89.3 vs 5,25,000 tons per annum		Capacity delay
2025-08-01	Q1FY26	Q1FY26 transcript	Expand zinc metal production capacity to 2 million tons with 0.25 million ton phase 1 expansion	<i>as we are concerned. Arun Misra: Zinc, we are going for a 2-million-ton expansion, of which</i>	Zinc metal capacity 2 million tons with 0.25 million ton phase 1 · 2 million tons with 0.25 million ton phase 1	medium term	H	Phase 1 expansion progress at 89.3%, ramp up targeted in Q1FY27.	MET	89.3 vs 2 million tons		
2025-08-01	Q1FY26	Q1FY26 transcript	Expand zinc ore production from 17 to 35 million tons	<i>of the mine, which are currently at 17-million-ton ore production to go up to 35-million-ton</i>	Zinc ore production 35 million tons · 35 million tons	medium term	H	Quarterly mined metal production at 0.276 million tons, up 4% YoY and 7% QoQ	MISSED	0.28 vs 35 million tons		
2025-08-01	Q1FY26	Q1FY26 presentation	Capex of approximately \$10 billion under implementation	<i>Capex of ~ \$10 bn Under Implementation</i>	Capex ~\$10 bn under implementation · ~\$10 bn under implementation		H	Reported growth capex of USD 1.3 billion under implementation as of Q3FY26.	MISSED	1.3 vs 10 USD_bn		
2025-08-01	Q1FY26	Q1FY26 transcript	Athena power cost Rs. 3.6 per unit in FY26	<i>cost per unit is about Rs. 3.6 per unit</i>	Athena power cost Rs. 3.6/unit in FY26 · Rs. 3.6 per unit in FY26	2026-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-08-01	Q1FY26	Q1FY26 transcript	Meenakshi power cost Rs. 5 per unit from Q2FY26	<i>the cost per unit is about Rs. 3.6 per</i>	Meenakshi power cost Rs. 5/unit from Q2FY26 · Rs. 5 per unit from Q2FY26	2025-11-14	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Maintain oil & gas OPEX at \$15-16 per barrel in FY26	<i>OPEX, which is going to be around \$15 to \$16 per barrel</i>	Oil & gas OPEX \$15-16/bbl · \$15-16 per barrel	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	Consolidated EBITDA CAGR of 18% over medium term	<i>EBITDA CAGR Of 18% Over Medium Term</i>	Consolidated EBITDA CAGR 18% medium term · 18% CAGR medium term	medium term	H	Reported highest-ever EBITDA of ₹15,171 crore in Q3FY26	NYT	actual in INR crore not comparable to %		
2025-08-01	Q1FY26	Q1FY26 transcript	Vedanta India leverage to improve to 1x net debt/EBITDA by FY26-end	<i>At Vedanta India, by the end of the fiscal, our leverage will further improve to 1x</i>	Vedanta India net debt/EBITDA 1x by FY26-end · 1x net debt/EBITDA by FY26-end	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Vedanta Resources to deleverage \$3 billion over 3 years	<i>VRL will deleverage 3 billion over the 3 years</i>	VRL deleverage \$3bn over 3 years · \$3 billion over 3 years		H	Debt at Vedanta Resources was \$4.8 billion as of September end 2025.	MISSED	4.8 vs 3 USD_bn		
2025-08-01	Q1FY26	Q1FY26 transcript	Athena power selling price Rs. 5 per unit in FY26	<i>selling price at Rs. 5 per unit</i>	Athena power selling price Rs. 5/unit in FY26 · Rs. 5 per unit in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Meenakshi power selling price Rs. 5.50 to 5.70 per unit from Q2FY26	<i>selling price will be between Rs. 5.50 to Rs. 5.70 per unit</i>	Meenakshi power selling price Rs. 5.50-5.70/unit from Q2FY26 · Rs. 5.50 to 5.70 per unit from Q2FY26	2025-11-14	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Demerger hearing scheduled for 20th August 2025	<i>next hearing is scheduled on 20th August</i>	Demerger hearing on 20 Aug 2025 · 20 August 2025	2025	H	NCLT order received Dec 16, 2025; demerger approval targeted for April 1, 2026	NYT	in progress, not yet due		
2025-08-01	Q1FY26	Q1FY26 transcript	Mechanical completion of Gamsberg Phase-2 by December 2025	<i>targeting mechanical completion by December as we previously guided</i>	Mechanical completion of Gamsberg Phase-2 by Dec 2025 · by December 2025	2025	H	Mechanical completion not achieved by Dec 2025; progress at 89.3%, ramp-up targeted Q1FY27.	MISSED	slipped ~2 qtrs	Delay due to project ramp-up rescheduled to Q1FY27.	Capacity delay
2025-08-01	Q1FY26	Q1FY26 transcript	NCLAT hearing on TSPL demerger on 4th August 2025	<i>next hearing scheduled on 4th August</i>	NCLAT hearing on 4 Aug 2025 · 4 August 2025	2025	H	NCLT order for demerger received on December 16, 2025, after the originally scheduled NCLAT hearing date.	NYT	in progress, not yet due		
2025-08-01	Q1FY26	Q1FY26 transcript	Start ASP injection in Mangala cluster wells in August-September 2025	<i>ASP injection in the cluster well pad in Mangala, and that is now targeted for August and September</i>	Start ASP injection Aug-Sep 2025 · August-September 2025	2025	H	ASP injection commissioning delayed; expected startup within next three months from Jan 2026	MISSED	slipped ~2 qtrs	delays due to complexity and expense of enhanced oil recovery technology	Execution
2025-08-01	Q1FY26	Q1FY26 transcript	Start drilling DSF field in KG Basin in October 2025	<i>drilling in that field will start in October this year</i>	Start DSF drilling Oct 2025 · October 2025	2025	H	Drilling start re-planned to 2QFY27, not October 2025	NYT	in progress, not yet due		
2025-08-01	Q1FY26	Q1FY26 transcript	Gain 15,000 bpd from full-scale ASP injection in 3-4 quarters	<i>once we are through with the full-scale injection, in three to four quarters, we expect the additional gain of around 15,000 barrels per day from</i>	Add 15,000 bpd from ASP injection in 3-4 quarters · 15,000 bpd gain in 3-4 quarters		H	ASP commissioning delayed; first volumes expected in next three months	MET	85,000 vs 15,000 bpd		
2025-08-01	Q1FY26	Q1FY26 transcript	Add 18,000 bpd from DSF field in 1.5 years	<i>add around 18,000 barrels of oil equivalent in around 1.5 years time</i>	Add 18,000 bpd from DSF in 1.5 years · 18,000 bpd in 1.5 years	2025	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Add 5,000 bpd from additional wells drilled in FY26	<i>is additional wells planned for this year that are already starting to give us an uplift in barrels, and that is about 5,000 barrels of</i>	Add 5,000 bpd from FY26 wells · 5,000 bpd from FY26 wells	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Alumina production over 3 million metric tons in FY26	<i>delivering a guided volume of over 3 million metric tons in the current financial year</i>	FY26 alumina production > 3 million tons · over 3 million metric tons in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Oil and gas production target 95,000 to 100,000 barrels per day in FY26	<i>FY '26, we are targeting a range of 95,000 to 100,000 barrels of oil equivalent per day</i>	FY26 oil & gas production 95,000-100,000 bpd · 95,000 to 100,000 barrels per day in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	Manage oil & gas decline by about 15% from FY25 levels	<i>we want to manage the decline by about 15% from FY '25 levels</i>	Oil & gas decline ~15% from FY25 levels · about 15% decline from FY25 levels	2026-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-08-01	Q1FY26	Q1FY26 transcript	Increase silver production from 700-800 tons to 1,500 tons	<i>jump in silver production from currently 700 to 800 tons to about 1,500 tons</i>	Silver production 1,500 tons · 1,500 tons	medium term	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Add 1.3 GW combined capacity at Meenakshi and Athena power plants in H1 FY26	<i>Meenakshi and Athena plant added a combined 1.3 GW in the first half of the year</i>	1.3 GW power capacity added in H1 FY26 · 1.3 GW added in H1 FY26		H	1.6 GW capacity commissioned at Athena and Meenakshi as of Q3 FY26	MET	1.6 vs 1.3 GW		
2025-11-01	Q2FY26	Q2FY26 transcript	Reach total merchant power capacity of 4.2 GW by H1 FY26	<i>bringing our total merchant power capacity to 4.2 GW</i>	4.2 GW merchant power capacity by H1 FY26		H	Reached 4.2 GW merchant power capacity by Q3 FY26, on track for H1 FY26 target	MET	4.2 vs 4.2 GW		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission 600 MW at Athena	<i>600 MW at Athena</i>	Athena 600 MW · 600 MW Athena		H	Athena capacity reported as 1200 MW in Q3FY26 presentation, exceeding 600 MW target	MET	1,200 vs 600 MW		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission additional 600 MW at Athena taking total capacity to 1200 MW	<i>Additional 600 MW at Athena taking total capacity to 1200 MW</i>	Athena additional 600 MW · Additional 600 MW Athena		H	Commissioned around 1.6 GW additional capacity at Athena as of Q3FY26	MET	1,600 vs 600 MW		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission Athena Unit 2 (600MW) in 4QFY26	<i>Athena: Unit 2 (600MW) is expected to start commissioning in 4QFY26</i>	Athena Unit 2 commissioning 600 MW in 4QFY26 · 600 MW Athena Unit 2 commissioning	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Commission both units of Athena power plant by Q4 FY26 with 87% PLF, cost Rs 2.8/unit, realization Rs 5.7/unit	<i>At Athena, we would have hopefully both units commissioned then. PLF about 87%. Cost of generation, Rs. 2.8 per unit and realization at 5.7</i>	Athena units commissioned, 87% PLF, Rs 2.8 cost, Rs 5.7 realization by Q4 FY26 · Both units commissioned, 87% PLF, Rs 2.8 cost, Rs 5.7 realization by Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Commission 435,000 tons per annum smelter at BALCO in H1 FY26	<i>commissioning of the 435,000 tons per annum smelter at BALCO, with the first metal production achieved earlier this month</i>	BALCO smelter 435,000 tpa commissioned by H1 FY26 · 435,000 tpa smelter commissioned by H1 FY26		H	Partial commissioning by March; ramp-up planned quarterly to full by Q4 FY26	MISSED	70 vs 4,35,000 tons per annum	Delay due to partner substitution and resource augmentation	Execution
2025-11-01	Q2FY26	Q2FY26 presentation	Bicholim Mine (Goa) expansion from 3.6 to 4.32 MTPA	<i>Bicholim Mine (Goa) expansion from 3.6 to 4.32 MTPA</i>	Bicholim Mine capacity 4.32 MTPA · 4.32 MTPA Bicholim Mine		H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	0.5 MTPA Cudnem Mine (Goa)	<i>0.5 MTPA Cudnem Mine (Goa)</i>	Cudnem Mine capacity 0.5 MTPA · 0.5 MTPA Cudnem Mine		H	Commissioning initiated for 0.435 MTPA capacity in Q3FY26	MISSED	0.44 vs 0.5 MTPA		
2025-11-01	Q2FY26	Q2FY26 transcript	Commission 160,000 ton per annum Debari roaster at Hindustan Zinc	<i>Hindustan Zinc. commissioned 160,000 ton per annum Debari roaster</i>	Debari roaster 160,000 tpa commissioned · 160,000 tpa Debari roaster commissioned		H	160,000 tpa Debari roaster commissioned in 1HFY26 as scheduled	MET	1,60,000 vs 1,60,000 tons per annum		
2025-11-01	Q2FY26	Q2FY26 presentation	420 KTPA DI Pipe Plant (Goa)	<i>420 KTPA DI Pipe Plant (Goa)</i>	DI Pipe Plant capacity 420 KTPA · 420 KTPA DI Pipe Plant		H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission Gamsberg Phase 2 project by 2HFY26	<i>Project completion targeted in 2HFY26</i>	Gamsberg Phase 2 completion by 2HFY26 · Gamsberg Phase 2 completion		H	Gamsberg Phase 2 is 94% complete; commissioning expected in Q1FY27 with ramp-up thereafter.	MET	94 vs 2		
2025-11-01	Q2FY26	Q2FY26 transcript	Commission Gamsberg Phase-II expansion with 220,000 tons per annum incremental capacity by end of FY26	<i>Gamsberg Phase-II expansion, targeting 220,000 tons per annum incremental capacity, is now at 80% completion and is on track for commissioning by the end of</i>	Gamsberg Phase-II 220,000 tpa commissioned by FY26-end · 220,000 tpa incremental capacity by FY26-end	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Commission Ghogharpalli mine in Q2 or Q3 FY27	<i>Ghogharpalli, we had originally communicated the 2nd Quarter of FY '27, that might move up by a quarter, but still positive. So, that will be</i>	Ghogharpalli mine commissioned by Q2-Q3 FY27 · Q2-Q3 FY27	2027-05-15	M		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Hot Metal Capacity Expansion from 1.7 to 3.5 MTPA	<i>Hot Metal Capacity Expansion from 1.7 to 3.5 MTPA</i>	Hot Metal Capacity 3.5 MTPA · 3.5 MTPA Hot Metal Capacity		H	Commissioning initiated for 435 KTPA expansion in Q3FY26	MISSED	0.44 vs 3.5 MTPA		
2025-11-01	Q2FY26	Q2FY26 presentation	Janthakal Mine (Karnataka)	<i>Janthakal Mine (Karnataka)</i>	Janthakal Mine capacity · Janthakal Mine		H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-11-01	Q2FY26	Q2FY26 transcript	Commission Kuraloi mine in Q4 FY26	<i>Kuraloi, previously, we had communicated Quarter 3 this year. I think given the timelines there, we might push it out by a couple of months</i>	Kuraloi mine commissioned by Q4 FY26 · Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Debottlenecking to 6 MTPA at Lanjigarh	<i>Debottlenecking to 6 MTPA at Lanjigarh</i>	Lanjigarh capacity 6 MTPA · 6 MTPA Lanjigarh capacity		H	Ramp up to 5 MTPA at Lanjigarh reported, short of 6 MTPA target	MISSED	5 vs 6 MTPA	Calciners and boiler running at 75-80% capacity causing delay to full rated capacity	Capacity delay
2025-11-01	Q2FY26	Q2FY26 transcript	Commission 1.5 million tons per annum alumina Train II at Lanjigarh in H1 FY26	<i>At Lanjigarh, we began commissioning Train II, which is an additional 1.5 million tons per annum capacity and produced the first alumina from the new</i>	Lanjigarh Train II 1.5 Mtpa commissioned by H1 FY26 · 1.5 Mtpa alumina Train II commissioned by H1 FY26		H	Train II commissioned during Q3FY26 as per presentation	MET	1.5 vs 1.5 million tons per annum		
2025-11-01	Q2FY26	Q2FY26 transcript	Achieve 1 GW capacity at Meenakshi power plant by Q4 FY26 with 65% PLF, cost Rs 4.7/unit, realization Rs 5.7/unit	<i>Meenakshi capacity will be at 1 gigawatt. PLF will be around 65%. Cost of generation in rupees per unit, 4.7, and the realization will be</i>	Meenakshi 1 GW capacity, 65% PLF, Rs 4.7 cost, Rs 5.7 realization by Q4 FY26 · 1 GW capacity, 65% PLF, Rs 4.7 cost, Rs 5.7 realization by Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Commission 1000 MW at Meenakshi Power	<i>1000 MW at Meenakshi Power</i>	Meenakshi Power 1000 MW · 1000 MW Meenakshi Power		H	Commissioned 1600 MW capacity at Meenakshi and Athena combined as of Q3FY26	MET	1,600 vs 1,000 MW		
2025-11-01	Q2FY26	Q2FY26 presentation	Merchant Thermal Power capacity enhanced to 4.2 GW with commissioning of Athena 600MW and Meenakshi 1000 MW	<i>Merchant Power capacity expanded by 1.3 GW</i>	Merchant Thermal Power capacity 4.2 GW · 4.2 GW Merchant Thermal Power capacity	2025-11-14	H	Merchant Thermal Power capacity reached 4.2 GW as of Q3FY26, currently up and running	MET	4.2 vs 4.2 GW		
2025-11-01	Q2FY26	Q2FY26 transcript	Commission Sijimali mine in FY26	<i>We are hopeful for the mine to become operational in the current financial</i>	Sijimali mine commissioned by FY26 · commissioned in FY26	2026-05-15	M		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Smelter capacity expansion to 3.1 MTPA & VAP to 90%	<i>Smelter capacity expansion to 3.1 MTPA & VAP to 90%</i>	Smelter capacity 3.1 MTPA & VAP 90% · 3.1 MTPA smelter capacity & 90% VAP		H	Smelter capacity expansion to 3 MTPA & VAP to 90% stated as upcoming milestone	PARTIAL	3 vs 3.1 MTPA		
2025-11-01	Q2FY26	Q2FY26 presentation	Smelter Plant Production to 500 KTPA	<i>Smelter Plant Production to 500 KTPA</i>	Smelter Plant Production 500 KTPA · 500 KTPA Smelter Plant Production		H	Commissioning initiated for 435 KTPA smelter expansion, short of 500 KTPA target	MISSED	435 vs 500 KTPA	Delay due to waste stripping catch-up at open pit, impacting ramp-up schedule	Capacity delay
2025-11-01	Q2FY26	Q2FY26 transcript	Commission Sumangal mine in Q4 FY26	<i>Sumangal, on Sijimali, we have previously communicated Quarter 4 FY '26</i>	Sumangal mine commissioned by Q4 FY26 · Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	Doubling of VAP capacity from 1.4 to 2.8 MTPA	<i>Doubling of VAP capacity from 1.4 to 2.8 MTPA</i>	VAP capacity 2.8 MTPA · 2.8 MTPA VAP capacity		H	Reached 2.8 MTPA aluminum capacity after BALCO ramp up	MET	2.8 vs 2.8 MTPA		
2025-11-01	Q2FY26	Q2FY26 presentation	4 MTPA Wet Beneficiation Plant at IOK	<i>4 MTPA Wet Beneficiation Plant at IOK</i>	Wet Beneficiation Plant 4 MTPA · 4 MTPA Wet Beneficiation Plant		H	Commissioning initiated in FY26 as per Q3FY26 presentation	MET	4 vs 4 MTPA		
2025-11-01	Q2FY26	Q2FY26 transcript	Commission India's first Zinc tailings reprocessing plant at Rampura Agucha with 10 million ton per annum capacity	<i>secured Board approval for India's first Zinc tailings reprocessing plant at Rampura Agucha. That's at a 10 million ton per annum capacity</i>	Zinc tailings plant 10 Mtpa capacity commissioned · 10 Mtpa Zinc tailings plant capacity		H	10 Mtpa Zinc Tailings Reprocessing listed in commissioning schedule for FY26	MET	10 vs 10 million tons per annum		
2025-11-01	Q2FY26	Q2FY26 presentation	Growth capex of USD 0.9 billion in 1H FY26	<i>Growth Capex of USD 0.9 bn in 1H</i>	1H FY26 capex \$0.9 bn · \$0.9 bn capex in 1H FY26		H	Growth capex was USD 1.3 billion in 9M FY26, exceeding the 1H FY26 target of USD 0.9 billion.	MET	1.3 vs 0.9 USD_bn		
2025-11-01	Q2FY26	Q2FY26 transcript	Invest \$4.5 to \$5 billion in growth CAPEX over next three years	<i>over the next three years, cumulatively, collectively, it will be about \$4.5 billion to \$5 billion</i>	Growth CAPEX \$4.5-5.0 bn over 3 years · \$4.5 to \$5 billion over 3 years		H	Growth CAPEX was USD 1.3 billion in first 9 months of FY26	MISSED	1.3 vs 4.5-5 USD_bn		
2025-11-01	Q2FY26	Q2FY26 presentation	Declared dividend of Rs. 16 per share during the quarter	<i>declared a dividend of Rs. 16 per share during the quarter</i>	Dividend Rs.16 per share	2025-11-14	H	Dividend of Rs.16 per share was paid last quarter as stated in Q4FY26 transcript	MET	16 vs 16 INR/share		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-11-01	Q2FY26	Q2FY26 transcript	Reduce alumina cost by \$50 per ton in Q3 and Q4 FY26	<i>we expect in the next two quarters, the prices to go down further by \$50 each</i>	Alumina cost reduction \$50/t in Q3 and Q4 FY26 · \$50/t alumina cost reduction in Q3 and Q4 FY26	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Reduce average cost of borrowings to below 8% in near term	<i>We are targeting to bring down our average cost of borrowings to below 8% in near term</i>	Average cost of borrowings < 8% · below 8% average cost of borrowings	near term	H	Average cost of borrowings at ~9% in 3QFY26, down 160 bps YoY but still above 8% target	MISSED	9 vs 8 %	No explicit explanation for not reaching below 8% given	Other
2025-11-01	Q2FY26	Q2FY26 presentation	Net Debt to EBITDA ratio to improve to 1.37x	<i>Our Net Debt to EBITDA ratio stands at 1.37x, improving from 1.49x last year</i>	Net Debt/EBITDA 1.37x	2025-11-14	H	Net Debt/EBITDA ratio reported at 1.23x in 3QFY26 presentation.	MET	1.23 vs 1.37 x		
2025-11-01	Q2FY26	Q2FY26 transcript	Repay \$417 million ICL debt as scheduled in Jan and May 2026	<i>the remainder part of the ICL is about \$417 million, out of which \$200 million is due in January, and the balance, \$217 million, sometimes</i>	Repay \$417 million ICL debt by May 2026 · Repay \$417 million by May 2026	2026-05-31	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	Reduce Vedanta India net debt to EBITDA ratio from 1.37x to 1x	<i>debt to EBITDA ratio, which has improved from almost 1.88x leverage to 1.37 as we closed the previous quarter. And from here, we have committed</i>	Vedanta India net debt/EBITDA 1x · 1x net debt/EBITDA	near term	H	Vedanta India net debt to EBITDA ratio reported at 0.95x at fiscal year end FY26	MET	0.95 vs 1 x		
2025-11-01	Q2FY26	Q2FY26 transcript	Reduce Vedanta Resources debt from \$4.4 billion to \$3 billion over next two years	<i>publicly committed that from current \$4.4 billion will go down to \$3 billion over next two years</i>	Vedanta Resources debt \$3bn in 2 years · \$3 billion debt in 2 years		H	Debt reduced close to target, at \$3.2 billion by Dec 2025	MISSED	3.2 vs 3 USD_bn	Slightly above target due to timing of repayments and market conditions	Execution
2025-11-01	Q2FY26	Q2FY26 transcript	Achieve hot metal cost of production below \$1,650 per ton in H2 FY26	<i>we are on the track for full-year guidance with H2 hot metal cost being sub \$1,650</i>	H2 FY26 hot metal COP < \$1,650/t · sub \$1,650 hot metal COP in H2 FY26		H	Hot metal cost was \$1,674/t in 3QFY26, slightly above the \$1,650/t target for H2 FY26.	MET	1,674 vs 1,650 USD/ton		
2025-11-01	Q2FY26	Q2FY26 transcript	Complete demerger and list all five entities by end of FY26	<i>listing of all five demerged entities by the end of FY '26</i>	5 entities listed by FY26-end	2026-05-15	H	Demerger completed; five entities listed and operating separately from next quarter.	MET	on time		
2025-11-01	Q2FY26	Q2FY26 presentation	Start ASP Injection in mid 3QFY26	<i>ASP Injection is being targeted in mid of 3QFY26</i>	ASP Injection start mid 3QFY26 · mid 3QFY26	2026-02-14	H	Project 94% complete; confident about commissioning in this quarter (Q4FY26)	PARTIAL	late ~1 qtr	Delay due to complexity and scale of enhanced oil recovery technology	Execution
2025-11-01	Q2FY26	Q2FY26 transcript	Final NCLT hearing for demerger on November 12, 2025	<i>final NCLT hearing is scheduled for November 12</i>	NCLT hearing on 12 Nov 2025 · 12 November 2025	2025	H	NCLT order for demerger received on December 16, 2025, before the target date	NYT	in progress, not yet due		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission 1000 MW at Meenakshi Power in 1HFY26	<i>1000 MW at Meenakshi Power - 1HFY26</i>	1000 MW Meenakshi Power commissioned by 1HFY26 · Commission by 1HFY26		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission first 125,000 tons per annum billet line at Jharsuguda plant	<i>commissioning of the first 125,000 tons per annum billet line as part of the 250,000 tons per annum project at the Jharsuguda plant</i>	125,000 tpa billet line · 125,000 tpa billet line at Jharsuguda	2026-02-14	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission 420,000 tons per annum DI pipe plant in Goa by FY27	<i>our 420,000-tons per annum DI pipe plant in Goa</i>	420,000 tpa DI pipe plant · 420,000 tpa DI pipe plant in Goa	2027-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission 510,000 tons per annum fertilizer project at Hindustan Zinc by FY27	<i>our 510,000-tons per annum fertilizer project at Hindustan Zinc</i>	510,000 tpa fertilizer project · 510,000 tpa fertilizer project at Hindustan Zinc	2027-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission 600 MW additional capacity at Athena in 2HFY27	<i>Additional 600 MW at Athena - 2HFY27</i>	600 MW additional Athena capacity by 2HFY27 · Commission by 2HFY27		H	Restart timeline for Athena capacity commissioning not committed yet due to incident	NYT	Restart timeline for Athena capacity commissioning not commi		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission 600 MW at Athena in 1HFY26	<i>600 MW at Athena - 1HFY26</i>	600 MW Athena commissioned by 1HFY26 · Commission by 1HFY26		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission second 600 MW turbine at Athena by FY27	<i>commissioning of the second 600 MW turbine at Athena</i>	600 MW turbine commissioning · Commission second 600 MW turbine at Athena by FY27	2027-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2026-01-01	Q3FY26	Q3FY26 transcript	Commission 250,000 tons and 510,000 tons VAB projects at Jharsuguda and BALCO by FY27	<i>our 250,000-tons and 510,000-tons VAB projects at both Jharsuguda and BALCO</i>	760,000 tpa VAB projects · 250,000 tpa Jharsuguda + 510,000 tpa BALCO VAB projects	2027-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Aluminum production capacity to 5 million tons per annum after commissioning Lanjigarh Train 2	<i>addition of the 1.5 million tons per annum, Train 2, at our refinery in Lanjigarh, thereby taking our total aluminum production capacity to 5 million</i>	Aluminum capacity 5 Mtpa · 5 Mtpa aluminum capacity	2026-02-14	H	Aluminum capacity reached close to 4 million tons per annum at fiscal year end, below 5 Mtpa target	MISSED	4 vs 5 million tons per annum	Calciners and boiler running at 75-80% capacity causing delay in achieving rated capacity	Capacity delay
2026-01-01	Q3FY26	Q3FY26 transcript	Increase aluminum production to 2.8 million tons post BALCO ramp-up and close gap to 3 million tons in 18 months	<i>for that, Rajiv. Just to summarize on that, we will get to 2.8 million tons of aluminum post our BALCO project ramp up. The</i>	Aluminum production 2.8-3.0 million tons · 2.8 million tons now, 3 million tons in 18 months		H	Aluminum production at run rate close to 4 million tons exiting FY26	MET	40,00,000 vs 2.8-3 million tons		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission BALCO smelter with 435,000 tons per annum capacity	<i>production of first metal from the new 435,000 tons per annum BALCO smelter</i>	BALCO smelter capacity 435,000 tpa · 435,000 tpa BALCO smelter	2026-02-14	H	Aluminium smelter commissioning delayed; not fully operational by Q4FY26.	NYT	Aluminium smelter commissioning delayed; not fully operation		
2026-01-01	Q3FY26	Q3FY26 transcript	Ramp up BALCO smelter to 100,000 tons by March end and full ramp-up in next 3-6 months	<i>We intend to increase to about 1 lakh ton by this March end, and then next three to six months, we will ramp up the</i>	BALCO smelter ramp-up to 100,000 tons by Mar 2026 · 100,000 tons by Mar 2026, full ramp-up in 3-6 months	2026	H	BALCO smelter ramp-up progressing quarterly to full 100,000 tons run rate by Q4 FY26	MET	1,00,000 vs 1,00,000 tons		
2026-01-01	Q3FY26	Q3FY26 transcript	Increase captive alumina mix to 80% by Q1FY27	<i>going forward, Q1, Q2, it should be 80%</i>	Captive alumina mix 80% · 80% captive alumina mix by Q1FY27	2026-08-14	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission phase-II at Gamsberg by FY27	<i>phase-II commission at Gamsberg</i>	Gamsberg Phase-II commissioning	2027-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission Gamsberg Phase-II project next quarter	<i>The Gamsberg Phase-II project at our Zinc International business is almost 90% complete, with commissioning being targeted in the next quarter</i>	Gamsberg Phase-II commissioning by Q4FY26 · Gamsberg Phase-II commissioning	2026-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Start operations at Ghogharpalli coal mines by Q1FY27	<i>start of operations at Ghogharpalli coal mines</i>	Ghogharpalli coal mines operations start · Start operations at Ghogharpalli coal mines by Q1FY27	2026-08-14	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission Hot Acid Leaching Plant by Q4FY26	<i>Hot Acid Leaching Plant – Q4FY26</i>	Hot Acid Leaching Plant commissioned by Q4FY26 · Commission by Q4FY26	2026-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Commission Kuraloi Coal Mine by Q4FY26	<i>Kuraloi Coal Mine – Q4FY26</i>	Kuraloi Coal Mine commissioned by Q4FY26 · Commission by Q4FY26	2026-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission Kuraloi mine by Q4FY26	<i>we are very hopeful of commissioning the Kuraloi mine by Quarter 4 of FY26</i>	Kuraloi mine commissioning · Commission Kuraloi mine by Q4FY26	2026-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Add 1.3 GW new power capacity at Meenakshi and Athena plants	<i>The Power business added 1.3 GW of new capacity at Meenakshi and Athena power plants</i>	Power capacity +1.3 GW · 1.3 GW new power capacity	2026-02-14	H	Restart of Athena power plant capacity addition not yet committed; assessment just started	NYT	Restart of Athena power plant capacity addition not yet comm		
2026-01-01	Q3FY26	Q3FY26 transcript	Add 10 to 12 GW power capacity over next 5 to 7 years	<i>we are having a plan in place to put additional 10 to 12 gigawatt</i>	Power capacity +10-12 GW · Add 10-12 GW power capacity in 5-7 years		L		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Increase power capacity to 4.8 GW by H1FY27	<i>total capacity as of now up and running is 4.2 gigawatt. This is expected to go to around 4.8 gigawatt by end of H1 of</i>	Power capacity 4.8 GW · 4.8 GW power capacity by H1FY27		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Achieve 750 MW short and medium-term supply contract at Meenakshi and 600 MW at Athena	<i>Meenakshi has entered into a short and medium-term supply contract for 750 MW capacity, while Athena has signed supply contracts for its entire first unit</i>	Power supply contracts 750 MW + 600 MW · 750 MW Meenakshi + 600 MW Athena supply contracts	2026-02-14	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2026-01-01	Q3FY26	Q3FY26 transcript	Commission 160,000 tons per annum Debari roaster and add 21,000 tons per annum refined zinc capacity	<i>Zinc India business commissioned its 160,000 ton per annum Debari roaster and completed the debottlenecking projects at Chanderia and Dariba smelters, which added 21,000 tons</i>	Refined zinc capacity +181,000 tpa · 160,000 tpa Debari roaster + 21,000 tpa capacity addition	2026-02-14	H	Refined zinc capacity at run rate close to 4 million tons per annum exiting FY26	MET	40,00,000 vs 1,81,000 tons per annum		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission Sijimali bauxite mine by Q1FY27	<i>having received FC1 earlier this month, the start of operations at Ghogharpalli coal mines, commissioning of the second 600 MW turbine at Athena, our 510,000-tons</i>	Sijimali bauxite mine commissioning · Commission Sijimali bauxite mine by Q1FY27	2026-08-14	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Commission SP-I exploratory appraisal project by end of March FY26	<i>program. We hope it will be commissioned end of this</i>	SP-I project commissioning · Commission SP-I project by end March FY26	2026	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Invest \$1.7 billion in growth CAPEX for full FY26	<i>we are on track to achieve our full year guidance of around \$1.7 billion</i>	FY26 growth CAPEX \$1.7 bn · \$1.7 billion growth CAPEX in FY26	2026-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Alumina cost to reduce by about \$25 in Q4FY26 compared to Q3FY26	<i>next quarter alumina cost will be lower \$25 almost</i>	Alumina cost reduction \$25 · \$25 alumina cost reduction in Q4FY26	2026-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Reduce hot metal cost by \$50-\$60 by Q1FY27 compared to current levels	<i>we believe we should have a \$50-\$60 cost reduction compared to where we are today</i>	Hot metal cost reduction \$50-\$60 · \$50-\$60 hot metal cost reduction by Q1FY27	2026-08-14	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Deleverage Vedanta group by \$0.8 to \$1 billion in current fiscal	<i>we as a group at VRL level, almost half a billion deleveraging and given the current OFS in the play, again, another half a billion</i>	Group deleveraging \$0.8-1.0 bn · \$0.8-1.0 billion deleveraging in current fiscal	2026-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	Reduce Vedanta India net debt-to-EBITDA ratio to about 1x by fiscal year end	<i>we will be closing the fiscal at about 1x and that will be, I think, lowest in the last many, many years</i>	Net debt/EBITDA ~1x · Net debt/EBITDA about 1x by FY26-end	2026-05-15	H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 presentation	Ramp up Gamsberg Phase 2 project in Q1FY27	<i>Project ramp up is targeted in Q1FY27</i>	Gamsberg Phase 2 ramp up by Q1FY27 · Ramp up by Q1FY27	2026-08-14	H	Anticipated commissioning in next quarter and ramp-up for rest of the year	MET	on time		
2026-01-01	Q3FY26	Q3FY26 transcript	Increase alumina production to around 0.9 million tons in Q4FY26	<i>we are expecting 900 KT plus in Q4</i>	Alumina production >900 KT · 900 KT+ alumina production in Q4FY26	2026-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	BALCO expansion to ramp up to 100% by Q4 FY27 with ~105 KT per quarter	<i>Q1 should be 25%, Q2 ramped up to 50%, Q3 75%, and as we go into the Q4, it will be 100%</i>	BALCO expansion 100% ramp-up by Q4 FY27 · 100% ramp-up by Q4 FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Gamsberg Phase 2 commissioning and ramp-up in Q4 FY26 and FY27	<i>tons. The team is anticipating to commission in the next quarter and to have the plant ramped up for the rest of the</i>	Gamsberg Phase 2 commission Q1 FY27 and ramp-up FY27 · Commission Q1 FY27 and ramp-up FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Gamsberg Phase 3 medium-term expansion over next 2-3 years	<i>the medium-term outlook spanning next 2 to 3 years is completely detailed out</i>	Gamsberg Phase 3 expansion 2-3 years · Expansion over 2-3 years	medium term	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Ghogharpalli bauxite mine to commission in H1 FY27	<i>to Ghogharpalli, EC has been recommended at the start of this month, the month of April. We are also targeting FC in this quarter, and</i>	Ghogharpalli mine commission H1 FY27 · Commission in H1 FY27		H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Kuraloi coal mine to start operations about one month after mining lease received	<i>Kuraloi we have got the mining lease maybe a week back. Now from here, probably in a month or so, we should start seeing the</i>	Kuraloi coal mine start ~1 month after lease · Start mining operations ~1 month after lease	2026-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Sijimali bauxite mine to open in H1 FY27	<i>FC-1 is granted, EC we're expecting next month, and hopefully in H1 we will see the mines</i>	Sijimali mine open H1 FY27 · Open in H1 FY27		H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Copper brand fee to reduce from 3% to 0.75% post de-merger	<i>the brand fee for copper from the current 3% will go down to 0.75%</i>	Copper brand fee 0.75% · Copper brand fee 0.75% post de-merger		H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2026-04-01	Q4FY26	Q4FY26 transcript	Vedanta India to pay 4-5% dividend in FY27 plus routine brand fee	<i>So with 4% to 5% dividend and the routine brand fee, VRL can be managed</i>	Dividend 4-5% plus brand fee in FY27 · 4-5% dividend plus brand fee in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Alumina cost to be around \$740-750 per ton in Q2 FY27	<i>we expect the cost to be around broadly 740, 750 in the quarter 2 of financial year '27</i>	Alumina cost \$740-750/t · Alumina cost \$740-750/t in Q2 FY27	2026-11-14	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Aluminium cost of production guidance 1650-1700 \$/t for FY27	<i>the yearly guidance remains 1650 to 1700</i>	Aluminium CoP \$1650-1700/t · Aluminium CoP \$1650-1700/t in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Vedanta Limited debt to EBITDA ratio about 0.4 post de-merger	<i>to 10 years. Vedanta Limited's debt will be</i>	Debt/EBITDA 0.4x		H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Vedanta Resources FY27 loan requirement about USD0.3 billion	<i>the need for the loan in FY27 is almost USD0.3 billion</i>	FY27 loan requirement USD0.3 bn · USD0.3 bn loan requirement in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Vedanta Resources total combined principal and interest requirement about USD1 billion in FY27	<i>total combined half a billion is the requirement for the principal amount. The interest will be something similar; it is in fact a shy of</i>	FY27 total requirement ~USD1 bn · ~USD1 bn total requirement in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Vedanta group leverage under 1x pre-de-merger	<i>our leverage ratio has been brought down to under 1x, 0.95 from 1.22 last year same time</i>	Leverage ratio 0.95x	2026-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Vedanta Iron and Steel and Oil and Gas to be zero or near zero net debt post de-merger	<i>Iron and Steel and Oil and Gas are zero or almost net zero debt companies</i>	Net debt ~0 · Zero or near zero net debt		H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	De-leveraging Vedanta India by INR7,370 crore in Q4 FY26	<i>In Q4 FY26, we de-leveraged Vedanta India's balance sheet by INR7,370 crores</i>	Q4 FY26 deleveraging INR7,370 cr · Deleveraging INR7,370 cr in Q4 FY26	2026-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Copper business margin to increase to at least 5% in FY27	<i>we do foresee the margin in the Copper business going from roughly 1%. right now, going to at least 5%</i>	Copper margin ≥ 5% · Copper margin ≥ 5% in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Gamsberg underground mine project to add 3 metals by 2030	<i>we should look at somewhere around 2030 adding three more metals to the bottom line of Vedanta</i>	Add 3 metals by 2030	2030	H		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 transcript	Listing and commencement of trading of demerged companies by Q1 FY27	<i>We are targeting listing and commencement of trading of these shares by Q1 FY27</i>	Listing by Q1 FY27	2026-08-14	H		NYT	no outcome reported		

04 Methodology & Sources

What qualifies as a commitment

Only **measurable** statements — a number, %, ratio, ₹/\$ figure or a dated milestone. Generic or aspirational commentary is rejected. One promise per row, with a verbatim ≤ 25 -word quote.

How status is judged (deterministic rules — the model only retrieves)

- **MET** — delivered or exceeded the target
- **PARTIAL** — close but below target / a milestone slipped within grace
- **MISSED** — failed, incl. a date the company later pushed past the promised window
- **NYT** — outcome not yet reported within the verification window (excluded from scoring)

Confidence & the credibility score

H = hard numeric · **M** = directional · **L** = aspirational. Credibility = confidence-weighted delivery over testable promises (MET=1, PARTIAL=0.5, MISSED=0; H=1.0, M=0.8, L=0.6); bands A $\geq$ 75 B $\geq$ 60 C $\geq$ 45 D $\geq$ 30 E<30.

The verification window

Outcomes are verifiable only through **Q4FY26** (reported 2026-04-01). Later targets are therefore **NYT**. *Full retrieval · openai, mistral, gemini, groq.*

Source documents

Q1FY25 Presn
2024-08-01 · both

Q1FY25 Call
2024-08-01 · both

Q2FY25 Presn
2024-11-01 · both

Q2FY25 Call
2024-11-01 · both

Q3FY25 Presn
2025-02-01 · both

Q3FY25 Call
2025-02-01 · both

Q4FY25 Presn
2025-04-01 · both

Q4FY25 Call
2025-04-01 · both

Q1FY26 Presn
2025-08-01 · both

Q1FY26 Call
2025-08-01 · both

Q2FY26 Presn
2025-11-01 · both

Q2FY26 Call
2025-11-01 · both

+3 more

source documents (see the master table)
