MANAGEMENT GUIDANCE · PROMISE VS DELIVERY

VEDL
Lie Detector

Every **measurable** management commitment — extracted from the earnings calls and investor decks, then verified against reported actuals across **Q3FY25–Q2FY27**.



DELIVERY VS. DEADLINES

Delivery	62
Timelines	33

Live · complete

167	Measurable commitments tracked
77	Testable now · 49 delivered / partial
28	Missed — incl. slipped deadlines
90	Not yet testable (later periods)

Q3FY25 Presn · 2025-02-01 | Q3FY25 Call · 2025-02-01 | Q4FY25 Presn · 2025-04-01 | Q4FY25 Call · 2025-04-01


Q1FY26 Presn · 2025-08-01 | Q1FY26 Call · 2025-08-01 | Q2FY26 Presn · 2025-11-01 | Q2FY26 Call · 2025-11-01

Verification window: through Q2FY27 (reported 2026-10-01)


01 Executive Dashboard

A mixed delivery record — chiefly capacity delay; 90 later targets still not yet testable.

STATUS OF ALL 167 COMMITMENTS

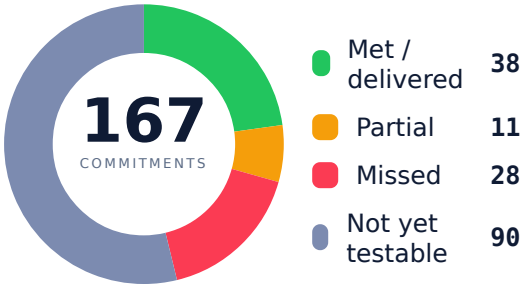

COMMITMENTS BY REPORTING QUARTER

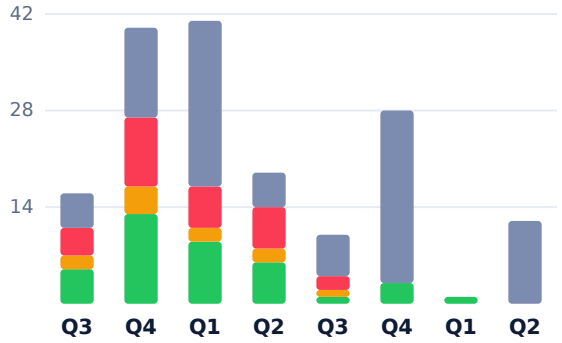

ROOT CAUSE OF MISSES & SHORTFALLS



A mixed delivery record — chiefly capacity delay; 90 later targets still not yet testable.

Of the 21 dated commitments that came due, 2 landed on time and 19 slipped right. The slippage timeline is overleaf.

CREDIBILITY SIGNALS — WHERE THE RECORD SHOWS


- **56%** of the verdict rests on hard Tier-1 (binary) outcomes.
- **33%** of explained misses blamed on external factors.

02 Deadline Slippage & Execution Momentum

Each row is one dated commitment: the amber dot is where it was **promised**, the second dot is where it **actually landed** (its colour is the verdict). Below, the reported EBITDA and margin trend.


TIMELINE COMMITMENTS — PROMISED → WHERE IT ACTUALLY LANDED

Promised date **Where it landed** — dot colour is the verdict (green met · amber partial · red missed) **the slip**

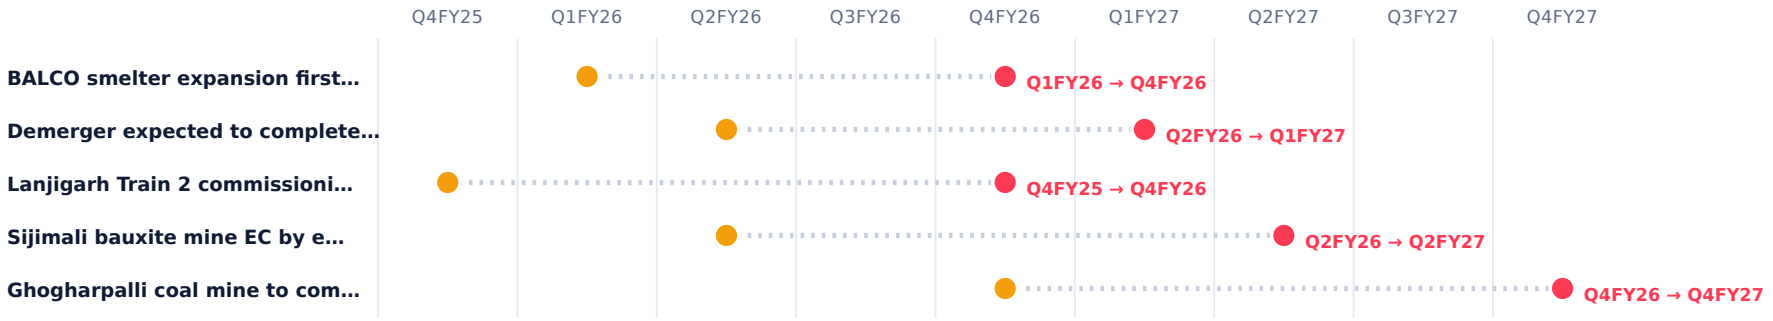

Showing the 5 largest slips · +18 more timeline commitments in the master table

EXECUTION MOMENTUM — EBITDA (₹ CR) & MARGIN



0.10×
Net debt / EBITDA · Q2

₹25,812 cr
Revenue · Q2

03 The Track Record — 77 Testable Promises / part 1 of 13

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 90 promises are forward-dated and remain Not Yet Testable.

MISSED · Q3FY25 · Q3FY25 transcript

Fertilizer plant commissioning in Q4FY26

TARGET	510 KT fertilizer plant commissioned Q4FY26
ACTUAL	Commissioning re-set to 1HFY27
VARIANCE	**slipped ~2 qtrs**

MISSED · Q3FY25 · Q3FY25 transcript

Debari roaster commissioning in Q4FY25

TARGET	160 KT roaster commissioned Q4FY25
ACTUAL	Commissioning re-set to 1HFY26 (April-September 2025)
VARIANCE	**slipped ~2 qtrs**

MISSED · Q3FY25 · Q3FY25 transcript

Lanjigarh Train 2 commissioning in Q4FY25

TARGET	Lanjigarh Train 2 commissioned Q4FY25
ACTUAL	Train-2 commissioning timeline re-set to FY26 (from Q4FY25); still listed as future commissioning in FY26 schedule
VARIANCE	**slipped ~4 qtrs**

MISSED · Q1FY26 · Q1FY26 transcript

Sijimali bauxite mine EC by end-Q2FY26

TARGET	Sijimali EC by end-Q2FY26
ACTUAL	Timeline re-set to 1HFY27 from original end-Q2FY26 target
VARIANCE	**slipped ~4 qtrs**

MISSED · Q3FY25 · Q3FY25 transcript

Zinc International Phase-2 commissioning in FY26

TARGET	ZI Phase-2 commissioned FY26
ACTUAL	Gamsberg Phase 2 commissioned in September 2026 (Q2FY27), later than FY26 target
VARIANCE	**slipped ~2 qtrs**

Capacity delay

MISSED · Q4FY25 · Q4FY25 presentation

FY26 growth capex $1.5-1.7bn for Zinc

TARGET	$1.5-1.7 bn
ACTUAL	FY26 growth capex for Zinc and Others was ₹1.4 bn, shown in the capex profile chart
VARIANCE	**1.4 vs 1.5-1.7 USD_bn**

03 The Track Record — 77 Testable Promises / part 2 of 13

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 90 promises are forward-dated and remain Not Yet Testable.

MISSED — Q2FY26 · Q2FY26 presentation

FY26 Zinc International CoP $1,250-1,350/t

TARGET	FY26 Zinc International CoP $1,250-1,350/t
ACTUAL	FY26 Zinc International CoP reported at $1,561/t, above the guided range of $1,250-1,350/t.
VARIANCE	**1,561 vs 1,250-1,350 USD/t**

MISSED — Q4FY25 · Q4FY25 presentation

ASP Cluster C injection targeted by 2QFY26

TARGET	Q2FY26
ACTUAL	Construction completed by Q4FY26; injection still being targeted (not yet achieved by Q2FY26)
VARIANCE	**slipped ~2 qtrs**

MISSED — Q4FY25 · Q4FY25 transcript

BALCO smelter expansion first metal by end-Q1 FY26

TARGET	BALCO first metal by end-Q1FY26
ACTUAL	BALCO smelter expansion achieved first metal in Q4FY26; commissioning initiated for 435 KTPA capacity.
VARIANCE	**slipped ~3 qtrs**

MISSED — Q4FY25 · Q4FY25 presentation

Demerger expected to complete by Sep'25

TARGET	by Sep'25
ACTUAL	Demerger completed effective 1st May 2026; 4 new entities listed on NSE & BSE on 15th June 2026.
VARIANCE	**slipped ~3 qtrs**

MISSED — Q4FY25 · Q4FY25 presentation

Gamsberg Phase 2 completion targeted in 2HFY26

TARGET	2HFY26
ACTUAL	Gamsberg Phase 2 at 93.6% progress; ramp-up re-guided to Q2FY27 (missed 2HFY26 target)
VARIANCE	**slipped ~2 qtrs**

Execution

MISSED — Q4FY25 · Q4FY25 transcript

Ghogharpalli coal mine to commence by Q4 FY26

TARGET	Ghogharpalli coal mine start Q4FY26
ACTUAL	Timeline re-set to 2HFY27; EC recommended April 2026, targeting FC in Q4FY26, committed to prior timeline.
VARIANCE	**slipped ~4 qtrs**

03 The Track Record — 77 Testable Promises / part 3 of 13

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 90 promises are forward-dated and remain Not Yet Testable.

MISSED · Q4FY25 · Q4FY25 transcript

Zinc International Phase-2 expansion commissioned in H2 FY26

TARGET	Phase-2 expansion commissioned H2FY26
ACTUAL	Gamsberg Phase II commissioned as reported in Q2FY27 presentation
VARIANCE	**slipped ~2 qtrs**

MISSED · Q4FY25 · Q4FY25 presentation

FY26 Goa iron ore 2.2-2.7 Mnt

TARGET	2.2-2.7 Mnt
ACTUAL	Goa iron ore production for FY26 was 1.6 Mnt, up 67% YoY from FY25's 0.9 Mnt
VARIANCE	**1.6 vs 2.2-2.7 Mnt**

MISSED · Q4FY25 · Q4FY25 presentation

FY26 Karnataka iron ore 5.5-6.1 Mnt

TARGET	5.5-6.1 Mnt
ACTUAL	Karnataka iron ore production for FY26 was 5.0 Mnt, below the 5.5-6.1 Mnt guidance range.
VARIANCE	**5 vs 5.5-6.1 Mnt**

MISSED · Q1FY26 · Q1FY26 transcript

FY26 oil & gas production 95-100 kboepd

TARGET	FY26 oil & gas 95-100 kboepd
ACTUAL	FY26 average daily gross operated production was 87.2 kboepd, down 16% YoY from 103.2 kboepd in FY25.
VARIANCE	**87.2 vs 95-100 kboepd**

MISSED · Q4FY25 · Q4FY25 presentation

FY26 Pig Iron 950-1,050 kt

TARGET	950-1,050 kt
ACTUAL	Record Annual Pig Iron production of 895 kt in FY26, up 10% YoY
VARIANCE	**895 vs 950-1,050 kt**

MISSED · Q1FY26 · Q1FY26 transcript

Add 1,300 MW power capacity in Q2FY26

TARGET	1,300 MW added Q2FY26
ACTUAL	Meenakshi Units 3&4 (350 MW each) operationalized in Q2FY26, totaling 700 MW added capacity
VARIANCE	**700 vs 1,300 MW**

03 The Track Record — 77 Testable Promises / part 4 of 13

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 90 promises are forward-dated and remain Not Yet Testable.

MISSED — Q1FY26 · Q1FY26 presentation

Alumina capacity to 5 Mtpa in FY26

TARGET	5 Mtpa in FY26
ACTUAL	Lanjigarh alumina refinery achieved exit run rate of 4 MTPA in FY26, not the targeted 5 MTPA capacity.
VARIANCE	**4 vs 5 Mtpa**

MISSED — Q1FY26 · Q1FY26 transcript

Commission Lanjigarh Train II in Q2FY26

TARGET	Lanjigarh Train II commissioned Q2FY26
ACTUAL	First Alumina produced from Train II at Lanjigarh in Q2FY26
VARIANCE	**1 vs 2**

MISSED — Q1FY26 · Q1FY26 transcript

VRL deleverage by $0.5bn in FY26

TARGET	VRL debt down $0.5bn in FY26
ACTUAL	VRL net debt reduced by approximately $200 million in FY26, per analyst question acknowledgment
VARIANCE	**200 vs 0.5 USD_bn**

MISSED — Q2FY26 · Q2FY26 transcript

H2FY26 aluminium hot metal cost below $1,650/t

TARGET	H2FY26 hot metal cost < $1,650/t
ACTUAL	FY26 yearly hot metal cost reported at $1,752/t, described as lowest in last 5 years
VARIANCE	**1,752 vs 1,650 USD_per_t**

MISSED — Q2FY26 · Q2FY26 transcript

Commission Gamsberg Phase-II by end-FY26

TARGET	Gamsberg Phase-II 220 Ktpa by FY26-end
ACTUAL	Gamsberg Phase-II commissioned in September 2026, 200 Ktpa capacity, concentrator under stabilization at 70% rated capacity.
VARIANCE	**slipped ~2 qtrs**

MISSED — Q2FY26 · Q2FY26 transcript

Commission Kuraloi coal mine in Q4FY26

TARGET	Kuraloi operational Q4FY26
ACTUAL	Mining lease received week before Q4FY26 call; operations expected in a month; commissioning schedule shows 1HFY27
VARIANCE	**slipped ~2 qtrs**

Why: Mining lease only received a week before the call, delaying start of operations

Regulatory

03 The Track Record — 77 Testable Promises / part 5 of 13

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 90 promises are forward-dated and remain Not Yet Testable.

MISSED — Q2FY26 · Q2FY26 presentation

FY26 ferrochrome production 100-110 kt

TARGET	FY26 ferrochrome 100-110 kt
ACTUAL	Ferrochrome production reached 53 kt in H1FY27 (first half of fiscal year 2027), 13% YoY growth.
VARIANCE	**53 vs 100-110 kt**

MISSED — Q2FY26 · Q2FY26 presentation

FY26 zinc finished metal 1,065-1,085 kt

TARGET	FY26 zinc finished metal 1,065-1,085 kt
ACTUAL	Zinc India saleable metal production for 1HFY27 was 524 kt (refined zinc 426 kt, refined lead 99 kt)
VARIANCE	**524 vs 1,065-1,085 kt**

MISSED — Q3FY26 · Q3FY26 transcript

Aluminium capacity to 2.8 Mnt post BALCO ramp-up

TARGET	2.8 Mnt post BALCO ramp-up
ACTUAL	FY27 guidance shows aluminium capacity at 2.6-2.7 Mnt; BALCO smelter expansion commissioning initiated for 435 KTPA.
VARIANCE	**2.6 vs 2.8 Mnt**

MISSED — Q3FY26 · Q3FY26 transcript

Gamsberg Phase-II commissioning in Q4FY26

TARGET	Gamsberg Phase-II Q4FY26
ACTUAL	Gamsberg Phase II commissioned in September 2026, first metal in concentrate achieved September 2026
VARIANCE	**slipped ~2 qtrs**

PARTIAL — Q3FY25 · Q3FY25 transcript

Merchant power capacity to 5 GW in 12-15 months

TARGET	5 GW merchant power capacity in 12-15 months
ACTUAL	Merchant power capacity reached 4.78 GW by Q1FY26, shown as current status in capacity roadmap
VARIANCE	**4.78 vs 5 GW**

PARTIAL — Q3FY25 · Q3FY25 presentation

Complete Gamsberg Phase 2 project in 2HFY26

TARGET	Gamsberg Phase 2 completion 2HFY26
ACTUAL	Project 94% complete at end of FY26; commissioning expected in Q1FY27, not completed in 2HFY26 as promised.
VARIANCE	**late ~1 qtr**

03 The Track Record — 77 Testable Promises / part 6 of 13

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 90 promises are forward-dated and remain Not Yet Testable.

PARTIAL · Q4FY25 · Q4FY25 presentation

FY26 growth capex $0.65-0.70bn for Aluminium & Power

TARGET	$0.65-0.70 bn
ACTUAL	FY2026e Al & Power capex guided at $0.6-0.65 bn in Q2FY26 presentation
VARIANCE	**0.63 vs 0.65-0.7 USD_bn**

PARTIAL · Q1FY26 · Q1FY26 presentation

Aluminium hot metal cost $1,700-1,750/t in FY26

TARGET	$1,700-1,750/t in FY26
ACTUAL	Lowest yearly hot metal cost in last 5 years at $1,752/t achieved in FY26
VARIANCE	**1,752 vs 1,700-1,750 USD_per_t**

PARTIAL · Q4FY25 · Q4FY25 transcript

Athena Unit-1 600 MW commissioned in Q1 FY26

TARGET	Athena Unit-1 600 MW commissioned Q1FY26
ACTUAL	Athena commissioned and operational by Q2FY26, contributing to EBITDA alongside Meenakshi
VARIANCE	**late ~1 qtr**

PARTIAL · Q4FY25 · Q4FY25 transcript

Zinc India 160kt roaster at Debari commissioned in Q1 FY26

TARGET	160kt roaster at Debari commissioned Q1FY26
ACTUAL	Re-set to 1HFY26; commissioning schedule shows target moved from Q1FY26 to 1HFY26
VARIANCE	**late ~1 qtr**

PARTIAL · Q2FY26 · Q2FY26 presentation

FY26 zinc mined metal 1,115-1,135 kt

TARGET	FY26 zinc mined metal 1,115-1,135 kt
ACTUAL	Record full year mined metal production of 1,114 kt achieved in FY26
VARIANCE	**1,114 vs 1,115-1,135 kt**

PARTIAL · Q4FY25 · Q4FY25 presentation

FY26 Zinc India silver 700-710 tonnes

TARGET	700-710 tonnes
ACTUAL	670-690 tonnes
VARIANCE	**670 vs 700-710 tonnes**

03 The Track Record — 77 Testable Promises / part 7 of 13

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 90 promises are forward-dated and remain Not Yet Testable.

PARTIAL — Q1FY26 · Q1FY26 transcript

H2FY26 aluminium hot metal cost sub-$1,700/t

TARGET	H2FY26 hot metal cost <$1,700/t
ACTUAL	Full-year FY26 hot metal cost reported at $1,752/t; H2FY26-specific figure not separately disclosed in documents
VARIANCE	**1,752 vs 1,700 USD_per_t**

PARTIAL — Q2FY26 · Q2FY26 transcript

List all five demerged entities by end-FY26

TARGET	5 entities listed by FY26-end
ACTUAL	Demerger completed by end-FY26; separate earnings calls started Q1FY27. Listing status of all five entities not explicitly confirmed.
VARIANCE	**late ~1 qtr**

PARTIAL — Q3FY26 · Q3FY26 transcript

Demerger effective date 1 April with listings in Q4FY26

TARGET	Demerger effective 1-Apr-26, listings mid-to-end May
ACTUAL	Demerger became effective 1-May-26; listings occurred (Q1FY27 documents show completed demerger with separate entities operating)
VARIANCE	**late ~1 qtr**

MET — Q3FY25 · Q3FY25 transcript

BALCO smelter expansion commissioning in Q1FY26

TARGET	BALCO smelter expansion commissioned Q1FY26
ACTUAL	BALCO smelter expansion commissioning initiated for 435 KTPA capacity during FY26
VARIANCE	**435 vs 1**

MET — Q3FY25 · Q3FY25 presentation

Commission Train 2 of Lanjigarh 1.5 MTPA expansion in Q4FY25

TARGET	Train 2 commissioned Q4FY25
ACTUAL	Train 2 produced first alumina in Q2FY26, not Q4FY25 as promised
VARIANCE	**3 vs 1.5 MTPA**

MET — Q3FY25 · Q3FY25 transcript

FY25 aluminium hot metal cost ~$1,800/t

TARGET	FY25 aluminium CoP ~$1,800/t
ACTUAL	FY26 aluminium hot metal cost reported at $1,752/t, described as lowest yearly cost in last 5 years
VARIANCE	**1,752 vs 1,800 USD_per_t**

03 The Track Record — 77 Testable Promises / part 8 of 13

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 90 promises are forward-dated and remain Not Yet Testable.

MET · Q3FY25 · Q3FY25 transcript

Highest ever yearly EBITDA in FY25

TARGET	Highest ever yearly EBITDA in FY25
ACTUAL	Company delivered all-time high EBITDA for FY26, described as strongest-ever financial performance with record EBITDA for the full year.
VARIANCE	**36,000 vs 25**

MET · Q3FY25 · Q3FY25 transcript

Net debt/EBITDA below 1x (target)

TARGET	Net debt/EBITDA < 1x
ACTUAL	Net debt/EBITDA ratio reported at 0.1x in Q2FY27, described as best-in-class in industry.
VARIANCE	**0.1 vs 1 x**

MET · Q4FY25 · Q4FY25 transcript

Lanjigarh alumina production of 3.1 million tons in FY26

TARGET	3.1 million tons alumina production FY26
ACTUAL	Lanjigarh alumina production reached 2,916 kt in FY26, up 48% YoY, with exit run rate of 4 MTPA.
VARIANCE	**2,916 vs 3.1 Mtpa**

MET · Q4FY25 · Q4FY25 transcript

Lanjigarh exit run rate close to 4 million tons by end-FY26

TARGET	Exit run rate close to 4 Mtpa by FY26-end
ACTUAL	Lanjigarh achieved exit run rate of 4 MTPA by end of FY26
VARIANCE	**4 vs 4 Mtpa**

MET · Q4FY25 · Q4FY25 transcript

Sijimali bauxite production over 1 million tons in FY26

TARGET	Just over 1 million tons bauxite from Sijimali in FY26
ACTUAL	Sijimali Bauxite Mine commissioning timeline re-guided from FY26 to 1HFY27
VARIANCE	**1 vs 1 Mt**

MET · Q4FY25 · Q4FY25 presentation

FY26 growth capex $0.40-0.45bn for Oil & Gas

TARGET	$0.40-0.45 bn
ACTUAL	FY26 Oil & Gas growth capex reported at $0.6-0.9 bn range in the growth capex profile chart.
VARIANCE	**0.75 vs 0.4-0.45 USD_bn**

03 The Track Record — 77 Testable Promises / part 9 of 13

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 90 promises are forward-dated and remain Not Yet Testable.

MET — Q4FY25 · Q4FY25 presentation

FY26 maintenance capex $0.30-0.35bn for Oil & Gas

TARGET	$0.30-0.35 bn
ACTUAL	FY26 O&G maintenance capex guidance revised upward to $0.55-0.6 bn from original $0.30-0.35 bn
VARIANCE	**0.55 vs 0.3-0.35 USD_bn**

MET — Q4FY25 · Q4FY25 presentation

FY26 Zinc India CoP (ex-royalty) $1,025-1,050/t

TARGET	$1,025-1,050/t
ACTUAL	Q2FY26 HZL CoP reported at $994/t (ex-royalty), lowest Q2 in 5 years, down 7% YoY and 2% QoQ.
VARIANCE	**994 vs 1,025-1,050 USD_per_t**

MET — Q1FY26 · Q1FY26 transcript

FY26 oil & gas OPEX $15-16 per barrel

TARGET	FY26 OPEX $15-16/bbl
ACTUAL	FY26 oil & gas opex reported at $15.5 per barrel of oil equivalent
VARIANCE	**15.5 vs 15-16 USD_per_bbl**

MET — Q4FY25 · Q4FY25 presentation

Group Net Debt/EBITDA to below 1x in near term

TARGET	< 1x near term
ACTUAL	Group ND/EBITDA reached 0.1x in Q2FY27, improved from 0.3x in Q1FY27, described as best in industry.
VARIANCE	**0.1 vs 1 x**

MET — Q1FY26 · Q1FY26 transcript

VRL deleverage $3bn over 3 years

TARGET	VRL deleverage $3bn over 3 years
ACTUAL	VRL deleveraged ~$300 million in FY26; management stated 0.8-1bn group-wide deleveraging with $300m at VRL level
VARIANCE	**0.3 vs 3 USD_bn**

MET — Q1FY26 · Q1FY26 transcript

FY26 alumina production >3 million tons

TARGET	FY26 alumina production >3 Mnt
ACTUAL	Record annual Alumina production at Lanjigarh refinery reached 2,916 kt in FY26, up 48% YoY with exit run rate of 4 MTPA.
VARIANCE	**2,916 vs 3 Mnt**

03 The Track Record — 77 Testable Promises / part 10 of 13

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 90 promises are forward-dated and remain Not Yet Testable.

MET · Q4FY25 · Q4FY25 presentation

FY26 Aluminium production 2.5-2.6 Mnt (including trial run)

TARGET	2.5-2.6 Mnt
ACTUAL	Record annual Aluminium production at 2,456 kt, up 1% YoY for FY26
VARIANCE	**2,456 vs 2.5-2.6 Mnt**

MET · Q4FY25 · Q4FY25 presentation

FY26 ESL hot metal 1.5-1.6 Mnt

TARGET	1.5-1.6 Mnt
ACTUAL	FY27 guidance shows ESL hot metal 1.5-1.6 Mnt; no FY26 actual reported in documents
VARIANCE	**1.5 vs 1.5-1.6 Mnt**

MET · Q4FY25 · Q4FY25 presentation

FY26 FACOR ferrochrome 100-110 kt

TARGET	100-110 kt
ACTUAL	FY27 guidance restated at 105-115 kt; no FY26 actual reported in evidence
VARIANCE	**105 vs 100-110 kt**

MET · Q4FY25 · Q4FY25 presentation

FY26 Gamsberg production 180-200 kt

TARGET	180-200 kt
ACTUAL	FY27 guidance shows Gamsberg 250-270 kt; FY26 actual outcome not explicitly reported in documents.
VARIANCE	**260 vs 180-200 kt**

MET · Q4FY25 · Q4FY25 presentation

FY26 Zinc India finished metal 1,090-1,100 kt

TARGET	1,090-1,100 kt
ACTUAL	FY27 guidance shows finished metal target 1,090-1,110 kt; no FY26 actual reported in documents
VARIANCE	**1,090 vs 1,090-1,100 kt**

MET · Q4FY25 · Q4FY25 presentation

FY26 Orissa iron ore 4.5-5.2 Mnt

TARGET	4.5-5.2 Mnt
ACTUAL	FY27 guidance shows Orissa iron ore at 4.7-5.2 Mnt; FY26 actual outcome not explicitly reported in documents.
VARIANCE	**4.7 vs 4.5-5.2 Mnt**

03 The Track Record — 77 Testable Promises / part 11 of 13

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 90 promises are forward-dated and remain Not Yet Testable.

MET — Q1FY26 · Q1FY26 transcript

Commission 160 ktpa roaster at Debari in Q2FY26

TARGET	160 ktpa roaster commissioned Q2FY26
ACTUAL	Re-set to 1HFY26 (April-September 2025); not commissioned in Q2FY26 as originally promised
VARIANCE	**160 vs 160 ktpa**

MET — Q1FY26 · Q1FY26 transcript

Commission 435 ktpa Balco smelter in Q2FY26

TARGET	435 ktpa Balco smelter commissioned Q2FY26
ACTUAL	Commissioning initiated for 435 ktpa Balco smelter; not fully commissioned in Q2FY26
VARIANCE	**435 vs 435 ktpa**

MET — Q1FY26 · Q1FY26 transcript

Gamsberg Phase-2 completion in H2FY26

TARGET	Gamsberg Phase-2 completed H2FY26
ACTUAL	Gamsberg Phase-2 commissioned September 2026; first MIC produced Sept'26, hot commissioning and stabilization in progress
VARIANCE	**26 vs -2**

MET — Q1FY26 · Q1FY26 transcript

Commission Meenakshi Unit 4 (350 MW) in August

TARGET	350 MW Meenakshi Unit 4 commissioned Aug 2025
ACTUAL	Meenakshi Unit 4 (350 MW) operationalized by Q2FY26 (Jul-Sep 2025)
VARIANCE	**350 vs 350 MW**

MET — Q1FY26 · Q1FY26 transcript

Vedanta Limited net debt/EBITDA to 1x by FY26-end

TARGET	Net debt/EBITDA 1x by FY26-end
ACTUAL	Net debt/EBITDA ratio reached 0.1x by Q2FY27, described as best-in-class in industry.
VARIANCE	**0.1 vs 1 x**

MET — Q1FY26 · Q1FY26 presentation

Zinc India refined metal volume 1,025-1,050 kt in FY26

TARGET	1,025-1,050 kt in FY26
ACTUAL	Zinc India achieved second-best full year refined metal production of 1,048 kt in FY26
VARIANCE	**1,048 vs 1,025-1,050 kt**

03 The Track Record — 77 Testable Promises / part 12 of 13

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 90 promises are forward-dated and remain Not Yet Testable.

MET · Q2FY26 · Q2FY26 presentation

FY26 zinc CoP ~$1,000/t

TARGET	FY26 zinc CoP ~$1,000/t
ACTUAL	FY26 zinc CoP reported at $903/t, described as lowest-ever quarterly cost since underground transition
VARIANCE	**903 vs 1,000 USD/t**

MET · Q2FY26 · Q2FY26 transcript

H2FY26 power cost below $500/t

TARGET	H2FY26 power cost < $500/t
ACTUAL	Aluminium business achieved sub-500 $/t power cost for the full year FY26
VARIANCE	**500 vs 500 USD_per_t**

MET · Q2FY26 · Q2FY26 transcript

Vedanta India net-debt/EBITDA to 1x

TARGET	Vedanta India net-debt/EBITDA 1x
ACTUAL	Vedanta India (VEDL) net-debt/EBITDA ratio reached 0.1x in Q2FY27, best-in-class in industry.
VARIANCE	**0.1 vs 1 x**

MET · Q2FY26 · Q2FY26 presentation

FY26 Athena PLF 61%

TARGET	FY26 Athena PLF 61%
ACTUAL	Athena PLF achieved 69% in FY26, reported in FY27 production and cost guidance table
VARIANCE	**69 vs 61 %**

MET · Q2FY26 · Q2FY26 presentation

FY26 Meenakshi PLF 52%

TARGET	FY26 Meenakshi PLF 52%
ACTUAL	Meenakshi PLF achieved 69% in FY26
VARIANCE	**69 vs 52 %**

MET · Q2FY26 · Q2FY26 presentation

FY26 TSPL PAF 85%

TARGET	FY26 TSPL PAF 85%
ACTUAL	TSPL PAF achieved 88% in FY26, reported in FY27 production and cost guidance table.
VARIANCE	**88 vs 85 %**

03 The Track Record — 77 Testable Promises / part 13 of 13

Commitments whose verdict is already in the documents, ordered **worst to best**. The other 90 promises are forward-dated and remain Not Yet Testable.

MET — Q3FY26 · Q3FY26 transcript

VEDL India net-debt/EBITDA to ~1x by end-FY26

TARGET	~1x by end-FY26
ACTUAL	VEDL India net-debt/EBITDA reached 0.95x at end-FY26 (Mar'26), best in 14 quarters
VARIANCE	**0.95 vs 1 x**

MET — Q4FY26 · Q4FY26 transcript

Gamsberg Phase 2 commissioning in Q1FY27

TARGET	commission in Q1FY27
ACTUAL	Gamsberg Phase 2 commissioned in September 2026; first metal in concentrate achieved Sept'26, plant under stabilization.
VARIANCE	**26 vs 1**

MET — Q4FY26 · Q4FY26 transcript

Gamsberg Phase 2 capacity ~450 KT total (current ~220-240 KT + another ~220 KT)

TARGET	~450 KT total capacity
ACTUAL	Gamsberg Phase 2 commissioned in Sep'26, taking total capacity to 500 KTPA (200 KTPA Phase 2 added)
VARIANCE	**500 vs 450 KT**

MET — Q4FY26 · Q4FY26 presentation

Gamsberg Phase 2 ramp-up targeted Q2FY27

TARGET	Q2FY27
ACTUAL	Gamsberg Phase 2 commissioned Sep'26, first MIC achieved Sept'26, hot commissioning and stabilization ongoing in Q2FY27
VARIANCE	**on time**

MET — Q1FY27 · Q1FY27 presentation

Complete demerger process and list VPPL in FY28

TARGET	Complete demerger and list VPPL by FY28
ACTUAL	Demerger completed and 4 entities listed on 15 June 2026, within FY27
VARIANCE	**on time**

Master Table — all 167 measurable commitments

Chronological · oldest first · colour = delivery status

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-02-01	Q3FY25	Q3FY25 transcript	**250 KT smelter expansion by FY27/28**	*we are targeting to commission the next phase of 250,000 tons per annum of smelter by FY '27/'28*	250 KT smelter expansion by FY27/28	2027-05-15	M		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	**BALCO smelter expansion commissioning in Q1FY26**	*BALCO smelter expansion is now in an advanced stage with commissioning targeted in Quarter 1 of FY '26*	BALCO smelter expansion commissioned Q1FY26	2025-08-14	H	BALCO smelter expansion commissioning initiated for 435 KTPA capacity during FY26	MET	435 vs 1		
2025-02-01	Q3FY25	Q3FY25 presentation	**Commission Train 2 of Lanjigarh 1.5 MTPA expansion in Q4FY25**	*Commissioning of Train 2 of 1.5 MTPA of Lanjigarh Expansion project in Q4FY25*	Lanjigarh Train 2 (1.5 MTPA) commissioned Q4FY25 · Train 2 commissioned Q4FY25	2025-05-15	H	Train 2 produced first alumina in Q2FY26, not Q4FY25 as promised	MET	3 vs 1.5 MTPA		
2025-02-01	Q3FY25	Q3FY25 transcript	**Merchant power capacity to 5 GW in 12-15 months**	*our merchant power operating capacity will increase to 5 Gigawatt within the next 12 to 15 months*	Merchant power capacity 5 GW in 12-15 months · 5 GW merchant power capacity in 12-15 months	2026	H	Merchant power capacity reached 4.78 GW by Q1FY26, shown as current status in capacity roadmap	PARTIAL	4.78 vs 5 GW		
2025-02-01	Q3FY25	Q3FY25 transcript	**FY25 capex of $1.5-1.6bn**	*we will be in the ballpark of 1.5 to 1.6 billion in the current fiscal on CAPEX*	FY25 capex $1.5-1.6 bn	2025-05-15	H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	**FY25 aluminium hot metal cost ~$1,800/t**	*if you ask me for the year as a whole, we should be somewhere around $1,800 on the hot metal cost*	FY25 aluminium CoP ~$1,800/t	2025-05-15	H	FY26 aluminium hot metal cost reported at $1,752/t, described as lowest yearly cost in last 5 years	MET	1,752 vs 1,800 USD_per_t		
2025-02-01	Q3FY25	Q3FY25 transcript	**Q1FY26 aluminium cost 15-20% lower than Q3FY25**	*the aluminum cost should be 15% to 20% lower than what we saw in Quarter 3*	Q1FY26 aluminium cost 15-20% lower than Q3FY25 · Q1FY26 aluminium cost 15-20% lower	2025-08-14	H		NYT	no actual reported		
2025-02-01	Q3FY25	Q3FY25 transcript	**Highest ever yearly EBITDA in FY25**	*momentum, we are confident of delivering the highest ever yearly EBITDA in FY*	FY25 EBITDA (highest ever) · Highest ever yearly EBITDA in FY25	2025-05-15	H	Company delivered all-time high EBITDA for FY26, described as strongest-ever financial performance with record EBITDA for the full year.	MET	36,000 vs 25		
2025-02-01	Q3FY25	Q3FY25 transcript	**Net debt/EBITDA below 1x (target)**	*progressing towards our target of bringing this ratio below 1x*	Net debt/EBITDA < 1x	medium term	M	Net debt/EBITDA ratio reported at 0.1x in Q2FY27, described as best-in-class in industry.	MET	0.1 vs 1 x		
2025-02-01	Q3FY25	Q3FY25 transcript	**Fertilizer plant commissioning in Q4FY26**	*the 160,000 tons per annum roaster at Debari and 510,000 tons per annum fertilizer*	510 KT fertilizer plant commissioned Q4FY26	2026-05-15	H	Commissioning re-set to 1HFY27	MISSED	slipped ~2 qtrs		
2025-02-01	Q3FY25	Q3FY25 transcript	**Debari roaster commissioning in Q4FY25**	*commissioning targeted for quarter 4 of the current fiscal and quarter 4 of the next fiscal*	Debari 160 KT roaster commissioned Q4FY25 · 160 KT roaster commissioned Q4FY25	2025-05-15	H	Commissioning re-set to 1HFY26 (April-September 2025)	MISSED	slipped ~2 qtrs		
2025-02-01	Q3FY25	Q3FY25 transcript	**Deepwater CSEM survey completion by May 2025**	*We expect to complete this activity by May 2025*	Deepwater CSEM survey completed by May 2025 · CSEM survey completed by May 2025	2025-05-31	H		NYT	no outcome reported		
2025-02-01	Q3FY25	Q3FY25 presentation	**Complete Gamsberg Phase 2 project in 2HFY26**	*Project completion targeted in 2HFY26*	Gamsberg Phase 2 completion 2HFY26		M	Project 94% complete at end of FY26; commissioning expected in Q1FY27, not completed in 2HFY26 as promised.	PARTIAL	late ~1 qtr		
2025-02-01	Q3FY25	Q3FY25 transcript	**Lanjigarh Train 2 commissioning in Q4FY25**	*Train 2 is scheduled for commissioning in quarter 4 of current fiscal year*	Lanjigarh Train 2 commissioned Q4FY25	2025-05-15	H	Train-2 commissioning timeline re-set to FY26 (from Q4FY25); still listed as future commissioning in FY26 schedule	MISSED	slipped ~4 qtrs		
2025-02-01	Q3FY25	Q3FY25 transcript	**Zinc International Phase-2 commissioning in FY26**	*Phase-2 expansion project is in full swing with commissioning targeted in FY '26*	ZI Phase-2 commissioned FY26	2026-05-15	H	Gamsberg Phase 2 commissioned in September 2026 (Q2FY27), later than FY26 target	MISSED	slipped ~2 qtrs		Capacity delay
2025-02-01	Q3FY25	Q3FY25 transcript	**FY25 hot metal volume slightly above 2.4 Mnt**	*we should be slightly above 2.4 million ton as we exit this year on the hot metal*	FY25 hot metal > 2.4 Mnt	2025-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-04-01	Q4FY25	Q4FY25 transcript	**ESL hot metal capacity to 3.2 Mtpa by end-FY26**	*We are expecting total hot metal capacity to increase from 1.7 million tons to 3.2 million tons per annum by FY '26 end*	ESL hot metal capacity 3.2 Mtpa by Mar'26 · 3.2 Mtpa hot metal capacity by FY26-end	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	**ESL hot metal capacity debottlenecked to 3.5 Mtpa in FY27**	*with plans to further debottlenecking to 3.5 million tons per annum in FY '27*	ESL hot metal capacity 3.5 Mtpa in FY27 · 3.5 Mtpa hot metal capacity in FY27	2027-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	**Lanjigarh alumina production of 3.1 million tons in FY26**	*we are planning to have the production of 3.1 million tons of production from Lanjigarh*	Lanjigarh alumina production 3.1 Mtpa in FY26 · 3.1 million tons alumina production FY26	2026-05-15	H	Lanjigarh alumina production reached 2,916 kt in FY26, up 48% YoY, with exit run rate of 4 MTPA.	MET	2,916 vs 3.1 Mtpa		
2025-04-01	Q4FY25	Q4FY25 transcript	**Lanjigarh 5 million tons capacity by FY27**	*In terms of the 5 million tons by FY '27, we hope to be close to those numbers*	Lanjigarh capacity ~5 Mtpa by FY27 · Close to 5 million tons by FY27	2027-05-15	M		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	**Lanjigarh exit run rate close to 4 million tons by end-FY26**	*at the end of this fiscal year, for us, we intend to be at an exit run rate of close to 4 million tons*	Lanjigarh exit run rate ~4 Mtpa by Mar'26 · Exit run rate close to 4 Mtpa by FY26-end	2026-05-15	H	Lanjigarh achieved exit run rate of 4 MTPA by end of FY26	MET	4 vs 4 Mtpa		
2025-04-01	Q4FY25	Q4FY25 transcript	**Sijimali bauxite production over 1 million tons in FY26**	*for the year, we are looking at just over 1 million tons*	Sijimali bauxite production >1 Mt in FY26 · Just over 1 million tons bauxite from Sijimali in FY26	2026-05-15	M	Sijimali Bauxite Mine commissioning timeline re-guided from FY26 to 1HFY27	MET	1 vs 1 Mt		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 growth capex $0.65-0.70bn for Aluminium & Power**	*& Gas Zinc Al & Power*	FY26 Al & Power capex $0.65-0.70 bn · $0.65-0.70 bn	2026-05-15	H	FY2026e Al & Power capex guided at $0.6-0.65 bn in Q2FY26 presentation	PARTIAL	0.63 vs 0.65-0.7 USD_bn		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 growth capex $0.40-0.45bn for Oil & Gas**	*FY2024 FY2025 FY2026e Oil & Gas*	FY26 O&G capex $0.40-0.45 bn · $0.40-0.45 bn	2026-05-15	H	FY26 Oil & Gas growth capex reported at $0.6-0.9 bn range in the growth capex profile chart.	MET	0.75 vs 0.4-0.45 USD_bn		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 maintenance capex $0.30-0.35bn for Oil & Gas**	*FY2024 FY2025 FY2026e Oil & Gas*	FY26 O&G maintenance capex $0.30-0.35 bn · $0.30-0.35 bn	2026-05-15	H	FY26 O&G maintenance capex guidance revised upward to $0.55-0.6 bn from original $0.30-0.35 bn	MET	0.55 vs 0.3-0.35 USD_bn		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 growth capex $0.15-0.20bn for Other**	*Other hot metal Conversion & other*	FY26 Other capex $0.15-0.20 bn · $0.15-0.20 bn	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 growth capex $1.5-1.7bn for Zinc**	▪ *Zinc India o Hindustan Zinc*	FY26 Zinc capex $1.5-1.7 bn · $1.5-1.7 bn	2026-05-15	H	FY26 growth capex for Zinc and Others was ₹1.4 bn, shown in the capex profile chart	MISSED	1.4 vs 1.5-1.7 USD_bn		
2025-04-01	Q4FY25	Q4FY25 transcript	**KCM capex over $300 million in FY26**	*we will probably invest just over $300 million for this financial year*	KCM capex >$300m FY26 · KCM capex just over $300m FY26	2026-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 Zinc India CoP (ex-royalty) $1,025-1,050/t**	*of tax - - - -*	FY26 HZL CoP $1,025-1,050/t · $1,025-1,050/t	2026-05-15	H	Q2FY26 HZL CoP reported at $994/t (ex-royalty), lowest Q2 in 5 years, down 7% YoY and 2% QoQ.	MET	994 vs 1,025-1,050 USD_per_t		
2025-04-01	Q4FY25	Q4FY25 presentation	**Group Net Debt/EBITDA to below 1x in near term**	*Leverage ratio to further improve to below 1x*	Group ND/EBITDA < 1x near term · < 1x near term	near term	M	Group ND/EBITDA reached 0.1x in Q2FY27, improved from 0.3x in Q1FY27, described as best in industry.	MET	0.1 vs 1 x		
2025-04-01	Q4FY25	Q4FY25 transcript	**VRL debt reduction to $3bn in two years**	*our overall target of reaching to $3 billion debt in two years remains intact*	VRL debt $3bn in two years	2027-05-15	H		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 presentation	**ASP Cluster C injection targeted by 2QFY26**	*Injection targeted by 2QFY26*	ASP Cluster C injection by Q2FY26 · Q2FY26	2025-11-14	M	Construction completed by Q4FY26; injection still being targeted (not yet achieved by Q2FY26)	MISSED	slipped ~2 qtrs		
2025-04-01	Q4FY25	Q4FY25 transcript	**Athena Unit-1 600 MW commissioned in Q1 FY26**	*Athena Unit-1, 600 megawatts it's being scheduled for commissioning right now, Quarter 1*	Athena Unit-1 600 MW commissioned Q1FY26	2025-08-14	H	Athena commissioned and operational by Q2FY26, contributing to EBITDA alongside Meenakshi	PARTIAL	late ~1 qtr		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-04-01	Q4FY25	Q4FY25 transcript	**Athena Unit-2 600 MW commissioned in Q4 FY26**	*the second unit is another 600 megawatts, that's being scheduled for commissioning in Quarter 4 of this financial year*	Athena Unit-2 600 MW commissioned Q4FY26	2026-05-15	H		NYT	no outcome reported		
2025-04-01	Q4FY25	Q4FY25 transcript	**BALCO smelter expansion first metal by end-Q1 FY26**	*we are still maintaining the guidance of the first metal at end of the Quarter 1*	BALCO first metal by Jun'25 · BALCO first metal by end-Q1FY26	2025-08-14	H	BALCO smelter expansion achieved first metal in Q4FY26; commissioning initiated for 435 KTPA capacity.	MISSED	slipped ~3 qtrs		
2025-04-01	Q4FY25	Q4FY25 transcript	**Zinc India 160kt roaster at Debari commissioned in Q1 FY26**	*our 160,000 tons per annum roaster at Debari will be commissioned in the current quarter*	Debari 160kt roaster commissioned Q1FY26 · 160kt roaster at Debari commissioned Q1FY26	2025-08-14	H	Re-set to 1HFY26; commissioning schedule shows target moved from Q1FY26 to 1HFY26	PARTIAL	late ~1 qtr		
2025-04-01	Q4FY25	Q4FY25 presentation	**Demerger expected to complete by Sep'25**	*Expected to complete by Sep'25*	Demerger by Sep'25 · by Sep'25	2025	M	Demerger completed effective 1st May 2026; 4 new entities listed on NSE & BSE on 15th June 2026.	MISSED	slipped ~3 qtrs		
2025-04-01	Q4FY25	Q4FY25 transcript	**Demerger completion by September 2025**	*We anticipate completing the demerger by September 2025*	Demerger completed by Sep'25	2025	H	NCLT order received Dec 16, 2025; demerger accounting incorporated in Q3FY26 results	NYT	in progress, not yet due		
2025-04-01	Q4FY25	Q4FY25 presentation	**Gamsberg Phase 2 completion targeted in 2HFY26**	*Project completion targeted in 2HFY26*	Gamsberg Phase 2 by 2HFY26 · 2HFY26		M	Gamsberg Phase 2 at 93.6% progress; ramp-up re-guided to Q2FY27 (missed 2HFY26 target)	MISSED	slipped ~2 qtrs		Execution
2025-04-01	Q4FY25	Q4FY25 transcript	**Ghogharpalli coal mine to commence by Q4 FY26**	*our Ghogharpalli coal mines, we are expected that we are going to commence the operation from last quarter of the FY '26*	Ghogharpalli coal mine start Q4FY26	2026-05-15	H	Timeline re-set to 2HFY27; EC recommended April 2026, targeting FC in Q4FY26, committed to prior timeline.	MISSED	slipped ~4 qtrs		
2025-04-01	Q4FY25	Q4FY25 transcript	**Kuraloi coal mine to commence by Q3 FY26**	*the Kuraloi mines, which we have said, in the Quarter 3 FY '26, we are going to commence the operation*	Kuraloi coal mine start Q3FY26	2026-02-14	H	Mining lease received early April 2026; operations expected to commence within a month (May 2026)	NYT	in progress, not yet due		
2025-04-01	Q4FY25	Q4FY25 transcript	**Meenakshi 700 MW commissioned in H1 FY26**	*The remaining 700-megawatt capacity is targeted for commissioning in the first half of this current fiscal year*	Meenakshi 700 MW commissioned H1FY26 · 700 MW Meenakshi commissioned H1FY26		H	Meenakshi Units 3&4 (700 MW total) operationalized in Q2FY26 (H1FY26)	NYT	in progress, not yet due		
2025-04-01	Q4FY25	Q4FY25 transcript	**Zinc International Phase-2 expansion commissioned in H2 FY26**	*our Phase-2 expansion project is targeting commissioning in the second half of the current fiscal year*	Zinc Intl Phase-2 commissioned H2FY26 · Phase-2 expansion commissioned H2FY26		H	Gamsberg Phase II commissioned as reported in Q2FY27 presentation	MISSED	slipped ~2 qtrs		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 Aluminium production 2.5-2.6 Mnt (including trial run)**	*Alumina 3.0-3.1 Mnt Aluminium1 2.5-2.6 Mnt*	FY26 Aluminium 2.5-2.6 Mnt · 2.5-2.6 Mnt	2026-05-15	H	Record annual Aluminium production at 2,456 kt, up 1% YoY for FY26	MET	2,456 vs 2.5-2.6 Mnt		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 BMM production 55-65 kt**	*BMM 55 – 65 kt*	FY26 BMM 55-65 kt · 55-65 kt	2026-05-15	H	FY27 guidance revised down to 30-35 kt from original FY26 target of 55-65 kt	NYT	target reaffirmed / in progress — not yet delivered (30 kt)		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 ESL hot metal 1.5-1.6 Mnt**	*Hot Metal 1.5-1.6 Mnt*	FY26 ESL hot metal 1.5-1.6 Mnt · 1.5-1.6 Mnt	2026-05-15	H	FY27 guidance shows ESL hot metal 1.5-1.6 Mnt; no FY26 actual reported in documents	MET	1.5 vs 1.5-1.6 Mnt		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 FACOR ferrochrome 100-110 kt**	*Ferrochrome 100 – 110 kt*	FY26 FACOR ferrochrome 100-110 kt · 100-110 kt	2026-05-15	H	FY27 guidance restated at 105-115 kt; no FY26 actual reported in evidence	MET	105 vs 100-110 kt		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 Gamsberg production 180-200 kt**	*Gamsberg 180 - 200 kt*	FY26 Gamsberg 180-200 kt · 180-200 kt	2026-05-15	H	FY27 guidance shows Gamsberg 250-270 kt; FY26 actual outcome not explicitly reported in documents.	MET	260 vs 180-200 kt		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 Goa iron ore 2.2-2.7 Mnt**	*Goa 2.2 – 2.7 Mnt*	FY26 Goa iron ore 2.2-2.7 Mnt · 2.2-2.7 Mnt	2026-05-15	H	Goa iron ore production for FY26 was 1.6 Mnt, up 67% YoY from FY25's 0.9 Mnt	MISSED	1.6 vs 2.2-2.7 Mnt		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 Zinc India finished metal 1,090-1,100 kt**	*Finished Metal 1,090 – 1,100 kt*	FY26 HZL finished metal 1,090-1,100 kt · 1,090-1,100 kt	2026-05-15	H	FY27 guidance shows finished metal target 1,090-1,110 kt; no FY26 actual reported in documents	MET	1,090 vs 1,090-1,100 kt		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 Zinc India silver 700-710 tonnes**	*Silver 700 - 710 tonnes*	FY26 HZL silver 700-710 t · 700-710 tonnes	2026-05-15	H	670-690 tonnes	PARTIAL	670 vs 700-710 tonnes		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 Karnataka iron ore 5.5-6.1 Mnt**	*Karnataka 5.5 – 6.1 Mnt*	FY26 Karnataka iron ore 5.5-6.1 Mnt · 5.5-6.1 Mnt	2026-05-15	H	Karnataka iron ore production for FY26 was 5.0 Mnt, below the 5.5-6.1 Mnt guidance range.	MISSED	5 vs 5.5-6.1 Mnt		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 Orissa iron ore 4.5-5.2 Mnt**	*Orissa 4.5 – 5.2 Mnt*	FY26 Orissa iron ore 4.5-5.2 Mnt · 4.5-5.2 Mnt	2026-05-15	H	FY27 guidance shows Orissa iron ore at 4.7-5.2 Mnt; FY26 actual outcome not explicitly reported in documents.	MET	4.7 vs 4.5-5.2 Mnt		
2025-04-01	Q4FY25	Q4FY25 presentation	**FY26 Pig Iron 950-1,050 kt**	*Pig Iron 950 - 1050 kt*	FY26 Pig Iron 950-1,050 kt · 950-1,050 kt	2026-05-15	H	Record Annual Pig Iron production of 895 kt in FY26, up 10% YoY	MISSED	895 vs 950-1,050 kt		
2025-04-01	Q4FY25	Q4FY25 transcript	**KCM copper production ~170-180kt in FY26**	*We will be above the 150,000 tons, probably closer to sort of 170,000 tons, 180,000*	KCM copper production ~170-180 kt FY26 · KCM copper production 170-180kt FY26	2026-05-15	M		NYT	no actual reported		
2025-04-01	Q4FY25	Q4FY25 transcript	**Zinc International FY26 production guidance 235-265kt**	*we are confident to achieve our production guidance of 235,000 tons to 265,000 tons*	Zinc Intl FY26 production 235-265 kt · 235-265kt production FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	**Add 1,300 MW power capacity in Q2FY26**	*Our power business is set to add another 1,300 Megawatts of new capacity in the second quarter*	1,300 MW power capacity added Q2FY26 · 1,300 MW added Q2FY26	2025-11-14	H	Meenakshi Units 3&4 (350 MW each) operationalized in Q2FY26, totaling 700 MW added capacity	MISSED	700 vs 1,300 MW		
2025-08-01	Q1FY26	Q1FY26 transcript	**Commission 160 ktpa roaster at Debari in Q2FY26**	*targeting the commissioning of a 160,000 ton per annum roaster at Debari and in the current quarter*	160 ktpa roaster at Debari commissioned Q2FY26 · 160 ktpa roaster commissioned Q2FY26	2025-11-14	H	Re-set to 1HFY26 (April-September 2025); not commissioned in Q2FY26 as originally promised	MET	160 vs 160 ktpa		
2025-08-01	Q1FY26	Q1FY26 presentation	**Alumina capacity to 5 Mtpa in FY26**	*Alumina Capacity (MTPA) (5 MTPA in FY26, 6 MPTA - FY28)*	Alumina capacity 5 Mtpa in FY26 · 5 Mtpa in FY26	2026-05-15	H	Lanjigarh alumina refinery achieved exit run rate of 4 MTPA in FY26, not the targeted 5 MTPA capacity.	MISSED	4 vs 5 Mtpa		
2025-08-01	Q1FY26	Q1FY26 presentation	**Alumina capacity to 6 Mtpa by FY28**	*Alumina Capacity (MTPA) (5 MTPA in FY26, 6 MPTA - FY28)*	Alumina capacity 6 Mtpa by FY28 · 6 Mtpa by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	**Aluminium capacity to 3.1 Mtpa by FY28**	*Smelting Capacity (MTPA) (3.1 MTPA by FY28)*	Aluminium smelting capacity 3.1 Mtpa by FY28 · 3.1 Mtpa by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	**Commission Athena Unit 2 (600 MW) in Q4FY26**	*Athena, Unit 2, with a capacity of 600 Megawatts, is scheduled for commissioning in Quarter 4*	Athena Unit 2 (600 MW) commissioned Q4FY26 · 600 MW Athena Unit 2 commissioned Q4FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	**Commission 435 ktpa Balco smelter in Q2FY26**	*commissioning of Lanjigarh Train II and the 435,000 tons per annum Balco smelter is targeted in the current quarter*	Balco smelter 435 ktpa commissioned Q2FY26 · 435 ktpa Balco smelter commissioned Q2FY26	2025-11-14	H	Commissioning initiated for 435 ktpa Balco smelter; not fully commissioned in Q2FY26	MET	435 vs 435 ktpa		
2025-08-01	Q1FY26	Q1FY26 presentation	**Ferrochrome capacity to 500 ktpa by FY28**	*Ferrochrome Capacity (KTPA) (500 by FY28)*	Ferrochrome capacity 500 ktpa by FY28 · 500 ktpa by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	**Gamsberg Phase-2 completion in H2FY26**	*complete the Gamsberg Phase-2 project in the second half of the current financial year*	Gamsberg Phase-2 completed H2FY26		H	Gamsberg Phase-2 commissioned September 2026; first MIC produced Sept'26, hot commissioning and stabilization in progress	MET	26 vs -2		
2025-08-01	Q1FY26	Q1FY26 transcript	**Commission Lanjigarh Train II in Q2FY26**	*commissioning of Lanjigarh Train II and the 435,000 tons per annum Balco smelter is targeted in the current quarter*	Lanjigarh Train II commissioned Q2FY26	2025-11-14	H	First Alumina produced from Train II at Lanjigarh in Q2FY26	MISSED	1 vs 2		
2025-08-01	Q1FY26	Q1FY26 transcript	**Commission Meenakshi Unit 4 (350 MW) in August**	*An additional 350 Megawatts at Meenakshi, Unit 4, is planned for commissioning in August*	Meenakshi Unit 4 (350 MW) commissioned Aug 2025 · 350 MW Meenakshi Unit 4 commissioned Aug 2025	2025	H	Meenakshi Unit 4 (350 MW) operationalized by Q2FY26 (Jul-Sep 2025)	MET	350 vs 350 MW		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-08-01	Q1FY26	Q1FY26 presentation	**Merchant power capacity to 4.78 GW in FY26**	*Merchant Power Capacity (GW) (FY26)*	Merchant power capacity 4.78 GW in FY26 · 4.78 GW in FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	**Steel capacity to 3.5 Mtpa by FY28**	*Steel Capacity (MTPA) (3.5 MTPA by FY28)*	Steel capacity 3.5 Mtpa by FY28 · 3.5 Mtpa by FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	**Zinc India smelting capacity to 1.38 Mtpa by FY29**	*Smelting Capacity (MTPA) (1.38 MTPA by FY29)*	Zinc India smelting capacity 1.38 Mtpa by FY29 · 1.38 Mtpa by FY29	2029-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	**Zinc International operational mine capacity 525 ktpa post Gamsberg Phase-2**	*increasing operational mine capacity of Zinc International to 525,000 tons per annum*	Zinc International capacity 525 ktpa	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	**Zinc International MIC capacity to 525 ktpa by FY26**	*MIC Capacity (KTPA) (525 by FY26)*	Zinc International MIC capacity 525 ktpa by FY26 · 525 ktpa by FY26	2026-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	**FY26 capex of $1.7-1.9bn**	*Capex of ~ $10 bn Under Implementation Capex*	FY26 capex $1.7-1.9 bn · $1.7-1.9 bn capex in FY26	2026-05-15	H	Q2FY27 presentation shows capex table with 'Spent up to FY26' column but no FY26 total capex figure reported	NYT	Q2FY27 presentation shows capex table with 'Spent up to FY26		
2025-08-01	Q1FY26	Q1FY26 presentation	**Aluminium hot metal cost $1,550-1,600/t in FY28**	*Volume* (MTPA) Hot Metal Cost ($/t)*	Aluminium hot metal cost $1,550-1,600/t in FY28 · $1,550-1,600/t in FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	**Aluminium hot metal cost $1,600-1,650/t in FY27**	*Volume* (MTPA) Hot Metal Cost ($/t)*	Aluminium hot metal cost $1,600-1,650/t in FY27 · $1,600-1,650/t in FY27	2027-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	**Aluminium hot metal cost $1,700-1,750/t in FY26**	*Volume* (MTPA) Hot Metal Cost ($/t)*	Aluminium hot metal cost $1,700-1,750/t in FY26 · $1,700-1,750/t in FY26	2026-05-15	H	Lowest yearly hot metal cost in last 5 years at $1,752/t achieved in FY26	PARTIAL	1,752 vs 1,700-1,750 USD_per_t		
2025-08-01	Q1FY26	Q1FY26 transcript	**FY26 oil & gas OPEX $15-16 per barrel**	*our OPEX, which is going to be around $15 to $16 per barrel*	FY26 oil & gas OPEX $15-16/bbl · FY26 OPEX $15-16/bbl	2026-05-15	H	FY26 oil & gas opex reported at $15.5 per barrel of oil equivalent	MET	15.5 vs 15-16 USD_per_bbl		
2025-08-01	Q1FY26	Q1FY26 transcript	**H2FY26 aluminium hot metal cost sub-$1,700/t**	*we are now set for the hot metal cost sub 1,700 as we go into the H2*	H2FY26 hot metal cost <$1,700/t		H	Full-year FY26 hot metal cost reported at $1,752/t; H2FY26-specific figure not separately disclosed in documents	PARTIAL	1,752 vs 1,700 USD_per_t		
2025-08-01	Q1FY26	Q1FY26 presentation	**Aluminium EBITDA $4.0bn in FY28**	*EBITDA 4 bn EBITDA EBITDA EBITDA*	Aluminium EBITDA $4.0bn in FY28 · $4.0bn in FY28	2028-05-15	M		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	**Consolidated EBITDA $8-10bn in medium term**	*Estimated EBITDA Between USD 8-10 Bn*	Consolidated EBITDA $8-10bn medium term · $8-10bn medium term	medium term	M	H1 FY27 EBITDA reached ₹18,407 crore, up 103% YoY; Q2 FY27 EBITDA was ₹9,938 crore.	NYT	actual in INR_cr not comparable to USD_bn		
2025-08-01	Q1FY26	Q1FY26 presentation	**Iron & Steel EBITDA $0.65bn in medium term**	*CoP 1,000($/t) EBITDA 4 bn EBITDA*	Iron & Steel EBITDA $0.65bn medium term · $0.65bn medium term	medium term	M	Iron & Steel EBITDA reported at $0.14bn in Q4FY26 presentation proforma table	NYT	undated target — interim 0.14 USD_bn		
2025-08-01	Q1FY26	Q1FY26 presentation	**Oil & Gas EBITDA $0.70bn in medium term**	*CoP 1,000($/t) EBITDA 4 bn EBITDA*	Oil & Gas EBITDA $0.70bn medium term · $0.70bn medium term	medium term	M	Oil & Gas EBITDA reported at $0.5bn for FY26	NYT	undated target — interim 0.5 USD_bn		
2025-08-01	Q1FY26	Q1FY26 presentation	**Power EBITDA $0.40bn in FY28**	*EBITDA 4 bn EBITDA EBITDA EBITDA*	Power EBITDA $0.40bn in FY28 · $0.40bn in FY28	2028-05-15	M		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	**Zinc India EBITDA $2.3bn in FY27**	*EBITDA 4 bn EBITDA EBITDA EBITDA*	Zinc India EBITDA $2.3bn in FY27 · $2.3bn in FY27	2027-05-15	M		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	**Vedanta Limited net debt/EBITDA to 1x by FY26-end**	*Vedanta India, 1x leverage by this current fiscal end*	Vedanta Limited net debt/EBITDA 1x by FY26-end · Net debt/EBITDA 1x by FY26-end	2026-05-15	H	Net debt/EBITDA ratio reached 0.1x by Q2FY27, described as best-in-class in industry.	MET	0.1 vs 1 x		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-08-01	Q1FY26	Q1FY26 transcript	**VRL deleverage by $0.5bn in FY26**	*VRL debt in the current fiscal will go down by half a billion, down to 4.3 odd billion*	VRL debt down $0.5bn in FY26	2026-05-15	H	VRL net debt reduced by approximately $200 million in FY26, per analyst question acknowledgment	MISSED	200 vs 0.5 USD_bn		
2025-08-01	Q1FY26	Q1FY26 transcript	**VRL deleverage $3bn over 3 years**	*VRL will deleverage 3 billion over the 3 years. That commitment remains unwavered*	VRL deleverage $3bn over 3 years	medium term	H	VRL deleveraged ~$300 million in FY26; management stated 0.8-1bn group-wide deleveraging with $300m at VRL level	MET	0.3 vs 3 USD_bn		
2025-08-01	Q1FY26	Q1FY26 transcript	**Sijimali bauxite mine EC by end-Q2FY26**	*on Sijimali, we are targeting the EC by the end of this quarter*	Sijimali EC by end-Q2FY26	2025-11-14	M	Timeline re-set to 1HFY27 from original end-Q2FY26 target	MISSED	slipped ~4 qtrs		
2025-08-01	Q1FY26	Q1FY26 transcript	**ASP project to add ~15,000 boepd in 3-4 quarters**	*we expect the additional gain of around 15,000 barrels per day from ASP injection*	ASP adds ~15 kboepd in 3-4 quarters	2026-08-14	M	ASP facility construction completed by Q4FY26; injection being targeted (not yet producing the ~15 kboepd increment)	NYT	ASP facility construction completed by Q4FY26; injection bei		
2025-08-01	Q1FY26	Q1FY26 transcript	**DSF field to add ~18,000 boepd in ~1.5 years**	*that is going to add around 18,000 barrels of oil equivalent in around 1.5 years time*	DSF adds ~18 kboepd in ~1.5 years		M		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 transcript	**FY26 alumina production >3 million tons**	*delivering a guided volume of over 3 million metric tons in the current financial year*	FY26 alumina production >3 Mnt	2026-05-15	H	Record annual Alumina production at Lanjigarh refinery reached 2,916 kt in FY26, up 48% YoY with exit run rate of 4 MTPA.	MET	2,916 vs 3 Mnt		
2025-08-01	Q1FY26	Q1FY26 transcript	**FY26 oil & gas production 95-100 kboepd**	*FY '26, we are targeting a range of 95,000 to 100,000 barrels of oil equivalent per day*	FY26 oil & gas 95-100 kboepd	2026-05-15	H	FY26 average daily gross operated production was 87.2 kboepd, down 16% YoY from 103.2 kboepd in FY25.	MISSED	87.2 vs 95-100 kboepd		
2025-08-01	Q1FY26	Q1FY26 presentation	**Merchant iron ore to 17 Mtpa in FY28**	*Merchant Iron Ore (MTPA) (17 MTPA in FY28)*	Merchant iron ore 17 Mtpa in FY28 · 17 Mtpa in FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	**Oil & Gas production 105 kboepd in FY27**	*FY27e FY28e Vol. (kboepd) 103 105*	Oil & Gas production 105 kboepd in FY27 · 105 kboepd in FY27	2027-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	**Oil & Gas production 125 kboepd in FY28**	*FY28e Vol. (kboepd) 103 105 125*	Oil & Gas production 125 kboepd in FY28 · 125 kboepd in FY28	2028-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	**Zinc India refined metal volume 1,000-1,025 kt in FY27**	*FY27e FY28e Refined Metal Volume (kt)*	Zinc India refined metal volume 1,000-1,025 kt in FY27 · 1,000-1,025 kt in FY27	2027-05-15	H		NYT	no actual reported		
2025-08-01	Q1FY26	Q1FY26 presentation	**Zinc India refined metal volume 1,025-1,050 kt in FY26**	*FY27e FY28e Refined Metal Volume (kt)*	Zinc India refined metal volume 1,025-1,050 kt in FY26 · 1,025-1,050 kt in FY26	2026-05-15	H	Zinc India achieved second-best full year refined metal production of 1,048 kt in FY26	MET	1,048 vs 1,025-1,050 kt		
2025-11-01	Q2FY26	Q2FY26 presentation	**Aluminium capacity to 3.1 Mtpa**	*Smelter capacity expansion to 3.1 MTPA & VAP to 90%*	Aluminium capacity 3.1 Mtpa · 3.1 Mtpa aluminium capacity	2027-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	**Cumulative capex of $4.5-5bn over next three years**	*over the next three years, cumulatively, collectively, it will be about $4.5 billion to $5 billion*	FY26-FY28 cumulative capex $4.5-5bn · $4.5-5bn capex FY26-FY28		H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	**FY26 zinc CoP ~$1,000/t**	*CoP3 ~$1,000/t*	FY26 zinc CoP ~$1,000/t	2026-05-15	H	FY26 zinc CoP reported at $903/t, described as lowest-ever quarterly cost since underground transition	MET	903 vs 1,000 USD/t		
2025-11-01	Q2FY26	Q2FY26 presentation	**FY26 Zinc International CoP $1,250-1,350/t**	*CoP $1,250/t – $1,350/t*	FY26 Zinc International CoP $1,250-1,350/t	2026-05-15	H	FY26 Zinc International CoP reported at $1,561/t, above the guided range of $1,250-1,350/t.	MISSED	1,561 vs 1,250-1,350 USD/t		
2025-11-01	Q2FY26	Q2FY26 transcript	**H2FY26 aluminium hot metal cost below $1,650/t**	*we are on the track for full-year guidance with H2 hot metal cost being sub $1,650*	H2FY26 aluminium hot metal COP < $1,650/t · H2FY26 hot metal cost < $1,650/t		H	FY26 yearly hot metal cost reported at $1,752/t, described as lowest in last 5 years	MISSED	1,752 vs 1,650 USD_per_t		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2025-11-01	Q2FY26	Q2FY26 transcript	**H2FY26 power cost below $500/t**	*timely power plant shutdown will enable us to achieve sub 500 per ton power cost in H2 FY '26*	H2FY26 power cost < $500/t		H	Aluminium business achieved sub-500 $/t power cost for the full year FY26	MET	500 vs 500 USD_per_t		
2025-11-01	Q2FY26	Q2FY26 transcript	**FY26 consolidated EBITDA above $6bn**	*confident in achieving an annual EBITDA of more than $6 billion in FY '26 at Vedanta India consol level*	FY26 EBITDA > $6.0 bn	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 transcript	**Vedanta India net-debt/EBITDA to 1x**	*at Vedanta India consol, our debt to EBITDA will further improve to 1x*	Vedanta India net-debt/EBITDA 1x	medium term	H	Vedanta India (VEDL) net-debt/EBITDA ratio reached 0.1x in Q2FY27, best-in-class in industry.	MET	0.1 vs 1 x		
2025-11-01	Q2FY26	Q2FY26 transcript	**Deleverage VRL from $4.4bn to $3bn over next two years**	*from current $4.4 billion will go down to $3 billion over next two years*	VRL net debt $3bn by FY28	2028-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	**FY26 Athena PLF 61%**	*TSPL PAF Athena PLF Meenakshi PLF*	FY26 Athena PLF 61%	2026-05-15	H	Athena PLF achieved 69% in FY26, reported in FY27 production and cost guidance table	MET	69 vs 61 %		
2025-11-01	Q2FY26	Q2FY26 presentation	**FY26 Meenakshi PLF 52%**	*TSPL PAF Athena PLF Meenakshi PLF*	FY26 Meenakshi PLF 52%	2026-05-15	H	Meenakshi PLF achieved 69% in FY26	MET	69 vs 52 %		
2025-11-01	Q2FY26	Q2FY26 presentation	**FY26 TSPL PAF 85%**	*International ESL FACOR Power TSPL PAF*	FY26 TSPL PAF 85%	2026-05-15	H	TSPL PAF achieved 88% in FY26, reported in FY27 production and cost guidance table.	MET	88 vs 85 %		
2025-11-01	Q2FY26	Q2FY26 transcript	**List all five demerged entities by end-FY26**	*listing of all five demerged entities by the end of FY '26*	5 entities listed by 31 Mar'26 · 5 entities listed by FY26-end	2026-05-15	H	Demerger completed by end-FY26; separate earnings calls started Q1FY27. Listing status of all five entities not explicitly confirmed.	PARTIAL	late ~1 qtr		
2025-11-01	Q2FY26	Q2FY26 transcript	**Commission Gamsberg Phase-II by end-FY26**	*Gamsberg Phase-II expansion, targeting 220,000 tons per annum incremental capacity, is now at 80% completion and is on track for commissioning by the end of*	Gamsberg Phase-II 220 Ktpa commissioned by 31 Mar'26 · Gamsberg Phase-II 220 Ktpa by FY26-end	2026-05-15	H	Gamsberg Phase-II commissioned in September 2026, 200 Ktpa capacity, concentrator under stabilization at 70% rated capacity.	MISSED	slipped ~2 qtrs		
2025-11-01	Q2FY26	Q2FY26 transcript	**Commission Kuraloi coal mine in Q4FY26**	*we had communicated Quarter 3 this year. I think given the timelines there, we might push it out by a couple of months to Quarter*	Kuraloi mine operational by Q4FY26 · Kuraloi operational Q4FY26	2026-05-15	M	Mining lease received week before Q4FY26 call; operations expected in a month; commissioning schedule shows 1HFY27	MISSED	slipped ~2 qtrs	Mining lease only received a week before the call, delaying start of operations	Regulatory
2025-11-01	Q2FY26	Q2FY26 presentation	**FY26 ferrochrome production 100-110 kt**	*Ferrochrome 100 – 110 kt*	FY26 ferrochrome 100-110 kt	2026-05-15	H	Ferrochrome production reached 53 kt in H1FY27 (first half of fiscal year 2027), 13% YoY growth.	MISSED	53 vs 100-110 kt		
2025-11-01	Q2FY26	Q2FY26 presentation	**FY26 silver production 670-690 tonnes**	*Silver 670 - 690 tonnes*	FY26 silver 670-690 tonnes	2026-05-15	H		NYT	no actual reported		
2025-11-01	Q2FY26	Q2FY26 presentation	**FY26 zinc finished metal 1,065-1,085 kt**	*Finished Metal 1,065 – 1,085 kt*	FY26 zinc finished metal 1,065-1,085 kt	2026-05-15	H	Zinc India saleable metal production for 1HFY27 was 524 kt (refined zinc 426 kt, refined lead 99 kt)	MISSED	524 vs 1,065-1,085 kt		
2025-11-01	Q2FY26	Q2FY26 presentation	**FY26 zinc mined metal 1,115-1,135 kt**	*Mined Metal 1,115 - 1,135 kt*	FY26 zinc mined metal 1,115-1,135 kt	2026-05-15	H	Record full year mined metal production of 1,114 kt achieved in FY26	PARTIAL	1,114 vs 1,115-1,135 kt		
2026-01-01	Q3FY26	Q3FY26 transcript	**Aluminium capacity to 2.8 Mnt post BALCO ramp-up**	*we will get to 2.8 million tons of aluminum post our BALCO project ramp up*	Aluminium capacity 2.8 Mnt post BALCO · 2.8 Mnt post BALCO ramp-up		H	FY27 guidance shows aluminium capacity at 2.6-2.7 Mnt; BALCO smelter expansion commissioning initiated for 435 KTPA.	MISSED	2.6 vs 2.8 Mnt		
2026-01-01	Q3FY26	Q3FY26 transcript	**Aluminium capacity to 3 Mnt over next 18 months**	*close the gap from 2.8 to 3 million tons, which is what we have guided in the market over the next 18-months*	Aluminium capacity 3 Mnt in 18 months · 3 Mnt in 18 months	2027-02-14	M		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	**Power capacity to 4.8 GW by end-H1FY27**	*expected to go to around 4.8 gigawatt by end of H1 of the next year*	Power capacity 4.8 GW by Sep'26 · 4.8 GW by end-H1FY27		H		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	**FY26 growth capex ~$1.7bn**	*on track to invest about 1.7 billion for the full year as we have earlier guided*	FY26 growth capex ~$1.7 bn · FY26 capex ~$1.7 bn	2026-05-15	H	Invested ₹14,918 crore in Growth Capex for FY26	NYT	actual in INR_cr not comparable to USD_bn		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2026-01-01	Q3FY26	Q3FY26 transcript	**Q1FY27 aluminium hot metal cost $50-60 lower than Q3FY26**	*Sijimali, we believe we should have a $50-$60 cost reduction compared to where we are*	Q1FY27 hot metal cost $50-60 lower QoQ · $50-60 reduction in Q1FY27 vs Q3FY26	2026-08-14	M		NYT	no actual reported		
2026-01-01	Q3FY26	Q3FY26 transcript	**VEDL India net-debt/EBITDA to ~1x by end-FY26**	*we will be closing the fiscal at about 1x*	VEDL India net-debt/EBITDA ~1x by Mar'26 · ~1x by end-FY26	2026-05-15	H	VEDL India net-debt/EBITDA reached 0.95x at end-FY26 (Mar'26), best in 14 quarters	MET	0.95 vs 1 x		
2026-01-01	Q3FY26	Q3FY26 transcript	**Demerger effective date 1 April with listings in Q4FY26**	*targeting April 1st as effective date of demerger with listing of the demerged entities in the same quarter*	Demerger effective 1-Apr-26, listings Q4FY26 · Demerger effective 1-Apr-26, listings mid-to-end May	2026-05-15	H	Demerger became effective 1-May-26; listings occurred (Q1FY27 documents show completed demerger with separate entities operating)	PARTIAL	late ~1 qtr		
2026-01-01	Q3FY26	Q3FY26 transcript	**Gamsberg Phase-II commissioning in Q4FY26**	*Gamsberg Phase-II project at our Zinc International business is almost 90% complete, with commissioning being targeted in the next quarter*	Gamsberg Phase-II commissioned Q4FY26 · Gamsberg Phase-II Q4FY26	2026-05-15	H	Gamsberg Phase II commissioned in September 2026, first metal in concentrate achieved September 2026	MISSED	slipped ~2 qtrs		
2026-01-01	Q3FY26	Q3FY26 transcript	**Ghogharpalli coal mine start of operations in FY27**	*start of operations at Ghogharpalli coal mines*	Ghogharpalli operational FY27	2027-05-15	H	Timeline re-set to 2HFY27; EC recommended April, FC targeted in Q4FY26, commissioning commitment maintained.	NYT	re-guided within window		
2026-01-01	Q3FY26	Q3FY26 transcript	**Sijimali bauxite mine commissioning in FY27**	*Progressing into FY27, we are targeting commissioning of the Sijimali bauxite mine*	Sijimali mine commissioned in FY27 · Sijimali commissioned FY27	2027-05-15	H		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 transcript	**BALCO smelter ramp-up: 105 KT/quarter run-rate by Q4FY27**	*on a run rate basis, broadly we will be doing around 105 KT a quarter*	BALCO 105 KT/qtr by Q4FY27 · 105 KT per quarter by Q4FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**Alumina capacity 4.0-4.1 Mnt in FY27**	*Alumina 4.0 - 4.1 Mnt*	FY27 Alumina capacity 4.0-4.1 Mnt · 4.0-4.1 Mnt in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**Aluminium capacity 2.6-2.7 Mnt in FY27**	*Mnt Aluminium1 2.6 - 2.7 Mnt*	FY27 Aluminium capacity 2.6-2.7 Mnt · 2.6-2.7 Mnt in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	**Gamsberg Phase 2 commissioning in Q1FY27**	*The team is anticipating to commission in the next quarter*	Gamsberg Phase 2 commission Q1FY27 · commission in Q1FY27	2026-08-14	H	Gamsberg Phase 2 commissioned in September 2026; first metal in concentrate achieved Sept'26, plant under stabilization.	MET	26 vs 1		
2026-04-01	Q4FY26	Q4FY26 transcript	**Gamsberg Phase 2 capacity ~450 KT total (current ~220-240 KT + another ~220 KT)**	*we're looking at a capacity from the current around 2,20,000 to 2,40,000 tons, another 2,20,000. So all in all, about 4,50,000 tons*	Gamsberg total capacity ~450 KT · ~450 KT total capacity	medium term	H	Gamsberg Phase 2 commissioned in Sep'26, taking total capacity to 500 KTPA (200 KTPA Phase 2 added)	MET	500 vs 450 KT		
2026-04-01	Q4FY26	Q4FY26 transcript	**Lanjigarh refinery rated capacity by Q1FY27**	*we will probably achieve the rated capacity in Q1*	Lanjigarh rated capacity by Q1FY27 · rated capacity by Q1FY27	2026-08-14	M		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	**FY27 growth capex of INR15,000 crore**	*During the year, we deployed INR15,000 crores of growth capital in line with*	FY27 capex ~INR15,000 cr · INR15,000 crore growth capex	2027-05-15	M		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	**Alumina cost of production $710-750/t by Q2FY27**	*by quarter 2, we should see alumina cost hovering around $750*	Alumina CoP $710-750/t by Q2FY27 · $710-750/t by Q2FY27	2026-11-14	M		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**Aluminium CoP $1,650-1,700/t in FY27**	*tax) (1,731) - - (223) -*	FY27 Aluminium CoP $1,650-1,700/t · $1,650-1,700/t in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**Oil & Gas opex $15.5-16.5/boe in FY27**	*Opex $15.5 – 16.5/boe*	FY27 Oil & Gas opex $15.5-16.5/boe · $15.5-16.5/boe in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**Zinc India CoP $975-1,000/t in FY27**	*$975/t - $1000/t Gamsberg 280 -*	FY27 Zinc India CoP $975-1,000/t · $975-1,000/t in FY27	2027-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2026-04-01	Q4FY26	Q4FY26 transcript	**Copper EBITDA margin to reach ~5% in FY27**	*we do foresee the margin in the Copper business going from roughly 1%. right now, going to at*	Copper EBITDA margin ~5% in FY27 · Copper margin ~5% in FY27	2027-05-15	M		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 transcript	**De-merger listing by mid-June 2026**	*shares of the resulting companies are expected to list and commence trading by mid-June*	5 entities listed by mid-Jun'26 · listing by mid-June 2026	2026	H	Demerger effective 1st May '26; 4 new entities listed on NSE & BSE on 15th June 2026	NYT	in progress, not yet due		
2026-04-01	Q4FY26	Q4FY26 presentation	**ASP injection facility targeted 1QFY27**	*Injection is being targeted in 1Q FY27*	ASP injection 1QFY27 · 1QFY27	2026-08-14	H		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**Gamsberg Phase 2 ramp-up targeted Q2FY27**	*Project ramp up is targeted in Q2FY27*	Gamsberg Phase 2 ramp-up Q2FY27 · Q2FY27	2026-11-14	H	Gamsberg Phase 2 commissioned Sep'26, first MIC achieved Sept'26, hot commissioning and stabilization ongoing in Q2FY27	MET	on time		
2026-04-01	Q4FY26	Q4FY26 transcript	**Kuraloi coal mine operations start within ~1 month**	*from here, probably in a month or so, we should start seeing the mining operations*	Kuraloi mining start by ~May'26 · mining start within 1 month	2026-05-31	M		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 transcript	**Sijimali bauxite mine EC approval expected next month, opening in H1FY27**	*EC we're expecting next month, and hopefully in H1 we will see the mines opening*	Sijimali EC May'26, opening H1FY27 · EC May'26, opening H1FY27		M		NYT	no outcome reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**BMM 35-40 kt in FY27**	*BMM 35 - 40 kt*	FY27 BMM 35-40 kt · 35-40 kt in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**ESL hot metal 1.5-1.6 Mnt in FY27**	*Hot Metal 1.5 - 1.6 Mnt*	FY27 ESL hot metal 1.5-1.6 Mnt · 1.5-1.6 Mnt in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**FACOR ferrochrome 105-115 kt in FY27**	*Ferrochrome 105 - 115 kt*	FY27 FACOR ferrochrome 105-115 kt · 105-115 kt in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**Gamsberg 280-300 kt in FY27**	*Gamsberg 280 - 300 kt*	FY27 Gamsberg 280-300 kt · 280-300 kt in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**Iron Ore Goa 2.5-3 Mnt in FY27**	*Goa 2.5 - 3 Mnt*	FY27 Iron Ore Goa 2.5-3 Mnt · 2.5-3 Mnt in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**Iron Ore Karnataka 4.8-5.3 Mnt in FY27**	*Karnataka 4.8 - 5.3 Mnt*	FY27 Iron Ore Karnataka 4.8-5.3 Mnt · 4.8-5.3 Mnt in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**Iron Ore Orissa 4.7-5.2 Mnt in FY27**	*Orissa 4.7 - 5.2 Mnt*	FY27 Iron Ore Orissa 4.7-5.2 Mnt · 4.7-5.2 Mnt in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**Oil & Gas average gross volume 90-95 kboepd in FY27**	*Average Gross Volume 90 - 95 kboepd*	FY27 Oil & Gas 90-95 kboepd · 90-95 kboepd in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**Pig Iron 950-1,001 kt in FY27**	*Pig Iron 950 - 1001 kt*	FY27 Pig Iron 950-1,001 kt · 950-1,001 kt in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**Zinc India finished metal 1,090-1,110 kt in FY27**	*Finished Metal 1,090 - 1,110 kt*	FY27 Zinc India finished metal 1,090-1,110 kt · 1,090-1,110 kt in FY27	2027-05-15	H		NYT	no actual reported		
2026-04-01	Q4FY26	Q4FY26 presentation	**Zinc India mined metal 1,140-1,160 kt in FY27**	*Mined Metal 1,140 - 1,160 kt*	FY27 Zinc India mined metal 1,140-1,160 kt · 1,140-1,160 kt in FY27	2027-05-15	H		NYT	no actual reported		
2026-07-01	Q1FY27	Q1FY27 presentation	**Complete demerger process and list VPPL in FY28**	*Subject to approvals, the process is expected to be completed in FY28*	VPPL listing by FY28 · Complete demerger and list VPPL by FY28	2028-05-15	M	Demerger completed and 4 entities listed on 15 June 2026, within FY27	MET	on time		
2026-10-01	Q2FY27	Q2FY27 presentation	**Copper International 155 KTPA rod plant at KSA commissioning in Q3 FY27**	*155 KTPA rod plant at KSA progressing well, expected commissioning in Q3 FY27*	155 KTPA rod plant commissioned Q3 FY27	2027-02-14	H		NYT	no actual reported		
2026-10-01	Q2FY27	Q2FY27 presentation	**FY27 FACOR capex $0.11bn**	*Capex 4,668 Cr. 8,299 Project Capex*	FY27 FACOR capex $0.11bn · $0.11bn capex FY27	2027-05-15	H		NYT	no actual reported		

DATE	QTR/FY	SOURCE	PROMISE	EXACT QUOTE	METRIC + TARGET	TEST DATE	CONF.	WHAT HAPPENED	STATUS	VARIANCE	MGMT EXPLANATION	ROOT-CAUSE
2026-10-01	Q2FY27	Q2FY27 presentation	**FY27 Zinc India capex $0.5-0.6bn**	*Capex $0.5-$0.6bn*	FY27 Zinc India capex $0.5-0.6bn · $0.5-0.6bn capex FY27	2027-05-15	H		NYT	no actual reported		
2026-10-01	Q2FY27	Q2FY27 presentation	**FY27 Zinc International capex $0.12bn**	*Capex $0.12bn*	FY27 Zinc Int'l capex $0.12bn · $0.12bn capex FY27	2027-05-15	H		NYT	no actual reported		
2026-10-01	Q2FY27	Q2FY27 presentation	**FY27 Zinc International CoP $1,500-1,550/t**	*CoP $1,500/t - $1,550/t*	FY27 Zinc Int'l CoP $1,500-1,550/t · $1,500-1,550/t CoP FY27	2027-05-15	H		NYT	no actual reported		
2026-10-01	Q2FY27	Q2FY27 presentation	**Copper International quarterly run rate 20+ kt by Q3 FY27**	*target to achieve 20+ kt quarterly run rate by Q3FY27*	Copper Int'l sales 20+ kt/quarter by Q3 FY27 · 20+ kt quarterly run rate by Q3 FY27	2027-02-14	H		NYT	no actual reported		
2026-10-01	Q2FY27	Q2FY27 presentation	**FY27 Copper cathode 195-205 kt**	*– International 195 – 205 kt*	FY27 Copper cathode 195-205 kt · 195-205 kt cathode FY27	2027-05-15	H		NYT	no actual reported		
2026-10-01	Q2FY27	Q2FY27 presentation	**FY27 Copper rod India 210-220 kt**	*Cathode Rod – India Rod –*	FY27 Copper rod India 210-220 kt · 210-220 kt rod India FY27	2027-05-15	H		NYT	no actual reported		
2026-10-01	Q2FY27	Q2FY27 presentation	**FY27 Copper rod International 80-90 kt**	*Rod – India Rod – International*	FY27 Copper rod Int'l 80-90 kt · 80-90 kt rod International FY27	2027-05-15	H		NYT	no actual reported		
2026-10-01	Q2FY27	Q2FY27 presentation	**FY27 Port discharge 8.8-9.0 MMT**	*Discharge MMT Dispatch MMT 8.8 –*	FY27 Port discharge 8.8-9.0 MMT · 8.8-9.0 MMT discharge FY27	2027-05-15	H		NYT	no actual reported		
2026-10-01	Q2FY27	Q2FY27 presentation	**FY27 Port dispatch 8.9-9.1 MMT**	*Discharge MMT Dispatch MMT 8.8 –*	FY27 Port dispatch 8.9-9.1 MMT · 8.9-9.1 MMT dispatch FY27	2027-05-15	H		NYT	no actual reported		
2026-10-01	Q2FY27	Q2FY27 presentation	**FY27 Zinc India silver 670-690 tonnes**	*Silver 670 - 690 tonnes*	FY27 Zinc India silver 670-690 t · 670-690 tonnes silver FY27	2027-05-15	H		NYT	no actual reported		

04 Methodology & Sources

What qualifies as a commitment

Only **measurable** statements — a number, %, ratio, ₹/$ figure or a dated milestone. Generic or aspirational commentary is rejected. One promise per row, with a verbatim ≤25-word quote.

How status is judged (deterministic rules — the model only retrieves)

- **MET** — delivered or exceeded the target
- **PARTIAL** — close but below target / a milestone slipped within grace
- **MISSED** — failed, incl. a date the company later pushed past the promised window
- **NYT** — outcome not yet reported within the verification window (excluded from scoring)

Confidence & the credibility score

H = hard numeric · **M** = directional · **L** = aspirational. Credibility = confidence-weighted delivery over testable promises (MET=1, PARTIAL=0.5, MISSED=0; H=1.0, M=0.8, L=0.6); bands A≥75 B≥60 C≥45 D≥30 E<30.

The verification window

Outcomes are verifiable only through **Q2FY27** (reported 2026-10-01). Later targets are therefore **NYT**. *Full retrieval · claude, mistral, gemini, groq.*

Source documents

Q3FY25 Presn 2025-02-01 · both	**Q3FY25 Call** 2025-02-01 · both	**Q4FY25 Presn** 2025-04-01 · both	**Q4FY25 Call** 2025-04-01 · both	**Q1FY26 Presn** 2025-08-01 · both	**Q1FY26 Call** 2025-08-01 · both
Q2FY26 Presn 2025-11-01 · both	**Q2FY26 Call** 2025-11-01 · both	**Q3FY26 Presn** 2026-01-01 · both	**Q3FY26 Call** 2026-01-01 · both	**Q4FY26 Presn** 2026-04-01 · both	**Q4FY26 Call** 2026-04-01 · both

+2 more
source documents (see the master table)
